

## BEE FORMATION TESTING CO., INC.

TEST TICKET

DATE 2-13-58

P. O. BOX 491

GREAT BEND, KANSAS

15-009-06898  
Nº ✓ 3136CUSTOMER'S  
ORDER NO. \_\_\_\_\_NAME OF COMPANY FRANCIS OIL & GAS CO.ADDRESS TO MAIL INVOICE 905 PALACE Bldg. TULSA, OKLA.ADDRESS TO MAIL PRESSURE CHARTS SAMELEASE WOLF WELL NO. C-1(1) COUNTY BARTON STATE KS.TESTER William M. Blake APPROVED William M. BlakeDRILL STEM TEST NO. 2 SUCCESSFUL NO. \_\_\_\_\_ MIS-RUN NO. \_\_\_\_\_ FORMATION TESTED K.C.SIZE HOLE 7 7/8 TOOL JT. 4 1/2 F.H.RUBBER SIZE 6 3/4 - 2 7/8 - 30 TEST TOOL SIZE 4 3/8PACKER SET AT 3143 ANCHOR SIZE 4 1/2TOTAL DEPTH WELL 3176 LENGTH ANCHOR 33'PRESSURE RECORDER CAP. 3000-3000 DRILL PIPE RUN: DRY YES WITH FLUID \_\_\_\_\_

## RESULTS:

PACKER SET 3:44 P.M. TOOL OPEN 3:48 P.M. TOOL OPEN 1 hr. HRS.BLOW Good Steady Blow Through Out Test.  
Gas To Surface In 57 min.

## RECOVERY

127' SL. O.G.C.M.BHP 430 IBHP 710 IFP 0 FFP 0 HYDROSTATIC HEAD 1835SHUT IN PRESSURE TIME 20 MIN. INITIAL SHUT IN PRESSURE TIME 15 MIN.MUD WT. 10.3 VIS. 38 WATER LOSS 16.8EXTRA EQUIPMENT NONE JARS — NO. — SIZE —OPERATOR TIME — TOOL RENTAL TIME —

BEE FORMATION TESTING CO., INC.

SHALL NOT BE LIABLE FOR DAMAGE OF ANY KIND TO THE PROPERTY OR PERSONNEL OF THE PARTY FOR WHOM A TEST IS MADE, OR FROM ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH OR IN THE COURSE OF THE USE OF ITS EQUIPMENT, ALL OF WHICH LOSS OR DAMAGE IS ASSUMED BY THE CUSTOMER. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT THE COST OF THE PARTY FOR WHOM TEST IS MADE.

## BEE FORMATION TESTING COMPANY, INC.


EAST TENTH STREET

GREAT BEND, KANSAS

Company Francis Oil & Gas Company Date 2-13-58  
Address 905 Palace Building Tulsa, Oklahoma  
Lease Wolf Well No. C-1 Test No. 2 No. of Copies \_\_\_\_\_  
Pressure Recorder (Cap) Top 3000# Bottom 3000# Mud Wt. 10.3#  
Total Depth 3176' No. Feet Tested 33' Packer(s) set at 3143' and ----  
Packer Set 3:44 P.M. Tool Opened 3:48 P.M. Tool Open 1 Hr. ---- Min.  
I.S.I.P. ---- Hr(s) 15 Min. F.S.I.P. ---- Hr(s) 20 Min. Total Time On Bottom 1 Hr(s) 39 Min.  
Blow good steady through out test - gas to surface in 57 minutes  
Recovery 127' slightly oil gas cut mud  
Remarks:  
I.H.P. 1835# Choke Top 1/2"  
I.S.I.P. 710# Choke Bot 1/2"  
I.F.P. -----  
F.F.P. -----  
F.S.I.P. 430#  
F.H.P. 1835#  
Extra Equipment none Jars ---- Straddle Packer ---- Safety Joint ----  
Test OK yes Mis-Run no Tool Plugged no Anchor Plugged no

Operator William Blake Formation Kansas City Test Ticket No. 3136

outside

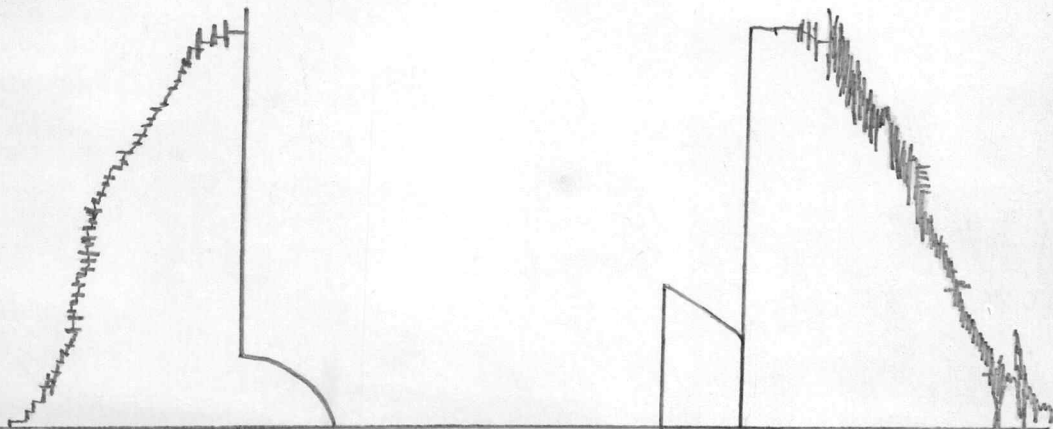

inside

