


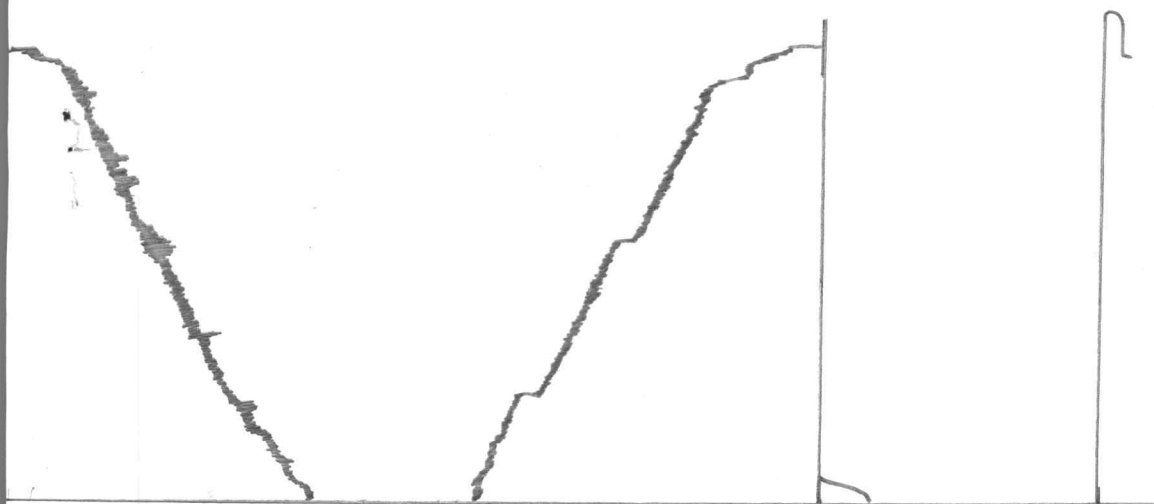

BEE FORMATION TESTING CO.

DATE 5-23-56

P. O. BOX 491

N^o 1626

GREAT BEND, KANSAS

CUSTOMER'S
ORDER NO. _____NAME OF COMPANY OKMAR OIL CO.ADDRESS TO MAIL INVOICE 817 UNION NATL. BANK - WICHITA, KANSASADDRESS TO MAIL PRESSURE CHARTS SAMELEASE STABB WELL NO. #1 COUNTY ELLIS STATE KANSASTESTER G.C. SKINNER APPROVED Harold E. McNeilDRILL STEM TEST NO. 1 SUCCESSFUL NO. 1 MIS-RUN NO. 0 FORMATION TESTED K.C.SIZE HOLE 7 7/8 TOOL JT. 4 1/2 FHRUBBER SIZE 6 3/4 X 2 7/8 X 30 TEST TOOL SIZE 4 5/8PACKER SET AT 3390' ANCHOR SIZE 4 1/2 FHTOTAL DEPTH WELL 3423' LENGTH ANCHOR 33'PRESSURE RECORDER CAP. 3000 X 3000 DRILL PIPE RUN: DRY ✓ WITH FLUID ✓


RESULTS:

PACKER SET 11:00 A. M. TOOL OPEN 11:06 A. M. TOOL OPEN 30 MIN HRS.BLOW WEAK 4 MIN BLOWRECOVERY 5' ROTARY MUDSHUT IN PRESSURE TIME 20 MIN. MUD WT. 10.2 VIS. 40 WATER LOSS 19.4BHP 125 IFP 0 FFP 0 HYDROSTATIC HEAD 1940EXTRA EQUIPMENT NONE JARS ✓ NO. ✓ SIZE ✓OPERATOR TIME 8 TOOL RENTAL TIME _____

BEE FORMATION TESTING CO.

SHALL NOT BE LIABLE FOR DAMAGE OF ANY KIND TO THE PROPERTY OR PERSONNEL OF THE PARTY FOR WHOM A TEST IS MADE, OR FROM ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH OR IN THE COURSE OF THE USE OF ITS EQUIPMENT, ALL OF WHICH LOSS OR DAMAGE IS ASSUMED BY THE CUSTOMER. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT THE COST OF THE PARTY FOR WHOM TEST IS MADE.

THANKS

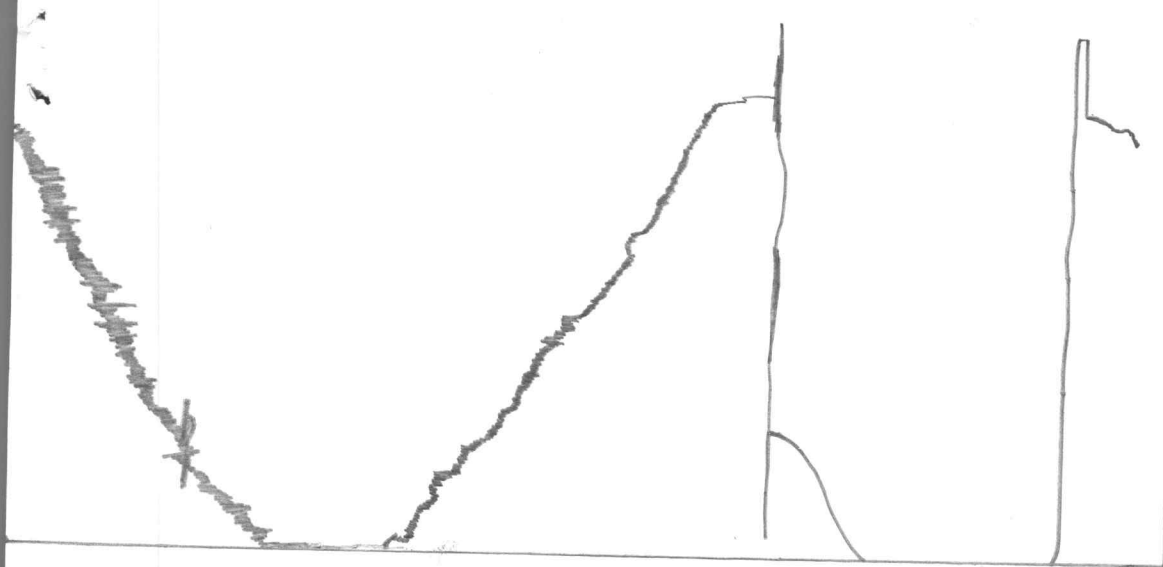

BEE FORMATION TESTING CO.

TEST TICKET

DATE

5-24-56

P. O. BOX 491

GREAT BEND, KANSAS

No

1628

CUSTOMER'S
ORDER NO.

NAME OF COMPANY

OKMAR OIL CO.

ADDRESS TO MAIL INVOICE

817 UNION NATH. BANK - WICHITA, KANSAS

ADDRESS TO MAIL PRESSURE CHARTS

SAME

LEASE

STABB

WELL NO.

#1

COUNTY

ELLIS

STATE

KANSAS

TESTER

J. C. Skinner

APPROVED

N. E. McNeil

DRILL STEM TEST NO.

2

SUCCESSFUL NO.

2

MIS-RUN NO.

0

FORMATION TESTED

KC

SIZE HOLE

7 7/8

TOOL JT.

4 1/2 FH

RUBBER SIZE

6 3/4 x 2 7/8 x 30

TEST TOOL SIZE

4 5/8

PACKER SET AT

3445'

ANCHOR SIZE

4 1/2 FH

TOTAL DEPTH WELL

3468'

LENGTH ANCHOR

23'

PRESSURE RECORDER CAP.

3000 x 3000

DRILL PIPE RUN: DRY

✓

WITH FLUID

RESULTS:

PACKER SET

2:48 A

M. TOOL OPEN

2:53 A

M. TOOL OPEN

30 MIN

HRS.

BLOW

WEAK 7 MIN BLOW

RECOVERY

8' ROTARY MUD

SHUT IN PRESSURE TIME

20 MIN

MUD WT.

10.1

VIS.

39

WATER
LOSS

18.0

BHP

550

IFP

0

FFP

0

HYDROSTATIC HEAD

1925

EXTRA EQUIPMENT

NONE

JARS

✓

NO.

✓

SIZE

✓

OPERATOR TIME

8

TOOL RENTAL TIME

BEE FORMATION TESTING CO.

SHALL NOT BE LIABLE FOR DAMAGE OF ANY KIND TO THE PROPERTY OR PERSONNEL OF THE PARTY FOR WHOM A TEST IS MADE, OR FROM ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH OR IN THE COURSE OF THE USE OF ITS EQUIPMENT, ALL OF WHICH LOSS OR DAMAGE IS ASSUMED BY THE CUSTOMER. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT THE COST OF THE PARTY FOR WHOM TEST IS MADE.

THANKS
