

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

6

Company MULL DRILLING COMPANY INCORPORATED

Lease and Well No. WILSON #B-1

County NESS State KANSAS Date 4-7-64

Formation Test No. #2 Total Depth 4410
 Interval Tested 4350 To 4410 Anchor Length 60'
 Size Hole 7 7/8 Size Drill Pipe 4 1/2 FH Size Packer 6 3/4
 Mud Weight 9.6 Viscosity 45 Bottom Hole Temp. 109 ° F
 Chokes: Top 1/2 Bottom 1/2 Ticket No. 6867

RECOVERY

WEAK BLOW FOR THIRTY-THREE MINUTES
 FLUSHED TOOL AFTER THIRTY-FIVE MINUTES..WEAK BLOW FOR
 TWO MINUTES

63' DRILLING MUD

Lease and Well No.

WILSON #B-1


16 16S 22W C NE NE

Formation Test No.

#2

Time: Each Square _____ minutes

Pressure: Each Square _____ psi

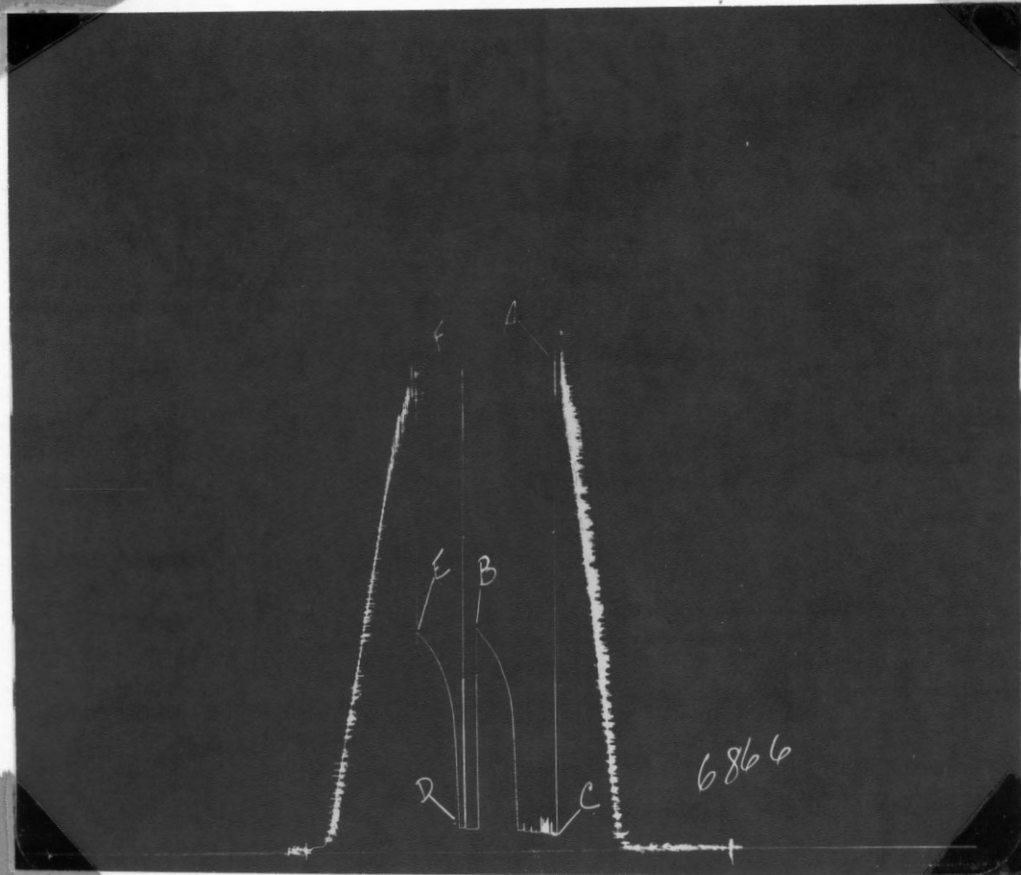

Tool Open _____ hr. 45 mins: Shut-in: Initial _____ hr. 30 mins: Final _____ hr. 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>2285</u>	<u>2379</u>
(B) Initial Shut-in Pressure	<u>1100</u>	<u>1089</u>
(C) Initial Flow Pressure	<u>90</u>	<u>55</u>
(D) Final Flow Pressure	<u>110</u>	<u>119</u>
(E) Final Shut-in Pressure	<u>1080</u>	<u>1061</u>
(F) Final Hydrostatic Pressure	<u>2270</u>	<u>2286</u>

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company MULL DRILLING COMPANY INCORPORATED

Lease and Well No. WILSON #B-1

County NESS

State

KANSAS

Date 4-7-64

Formation Test No. #3 Total Depth 4419

Interval Tested 4410 To 4419 Anchor Length 9'

Size Hole 7 7/8 Size Drill Pipe 4 1/2 FH Size Packer 6 3/4

Mud Weight 9.6 Viscosity 45 Bottom Hole Temp. ° F

Chokes: Top 1/2 Bottom 1/2 Ticket No. 6868

RECOVERY

WEAK STEADY BLOW THROUGHOUT TEST


220' MUDDY WATER

Lease and Well No. WILSON #B-1 16 16S 22W C/NE/NE

Formation Test No. #3

Time: Each Square _____ minutes

Pressure: Each Square _____ psi

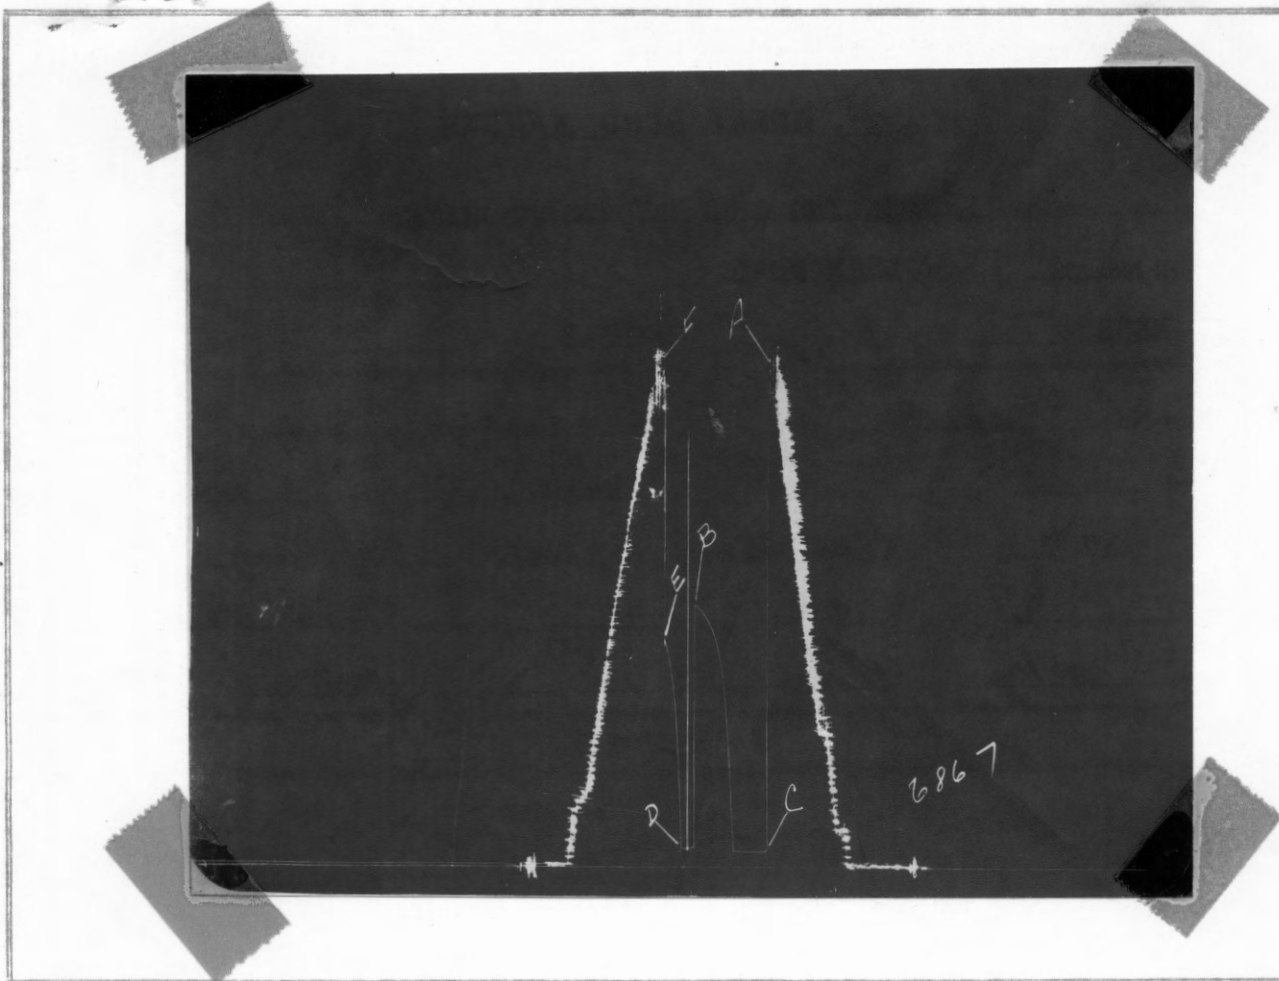

Tool Open _____ hr. 40 mins: Shut-in: Initial _____ hr. 30 mins: Final _____ hr. 10 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>2385</u>	<u>2434</u>
(B) Initial Shut-in Pressure	<u>1285</u>	<u>1272</u>
(C) Initial Flow Pressure	<u>80</u>	<u>73</u>
(D) Final Flow Pressure	<u>80</u>	<u>92</u>
(E) Final Shut-in Pressure	<u>1105</u>	<u>1098</u>
(F) Final Hydrostatic Pressure	<u>2370</u>	<u>2379</u>

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company MULL DRILLING COMPANY INCORPORATED

Lease and Well No. WILSON #B-1

County NESS State KANSAS Date 4-6-64

Formation Test No. #1 Total Depth 4329

Interval Tested 4274 To 4329 Anchor Length 55'

Size Hole 7 7/8 Size Drill Pipe 4 1/2 FH Size Packer 6 3/4

Mud Weight 9.8 Viscosity 43 Bottom Hole Temp. 108 ° F

Chokes: Top 1/2 Bottom 1/2 Ticket No. 6866

RECOVERY


WEAK BLOW FOR FORTY-NINE MINUTES
FLUSHED TOOL AFTER OPEN FIFTY MINUTES
WEAK BLOW FOR FOUR MINUTES

120' DRILLING MUD

Lease and Well No. WILSON #B-1 16 168 22W C NE NE Formation Test No. #1

Time: Each Square minutes

Pressure: Each Square psi

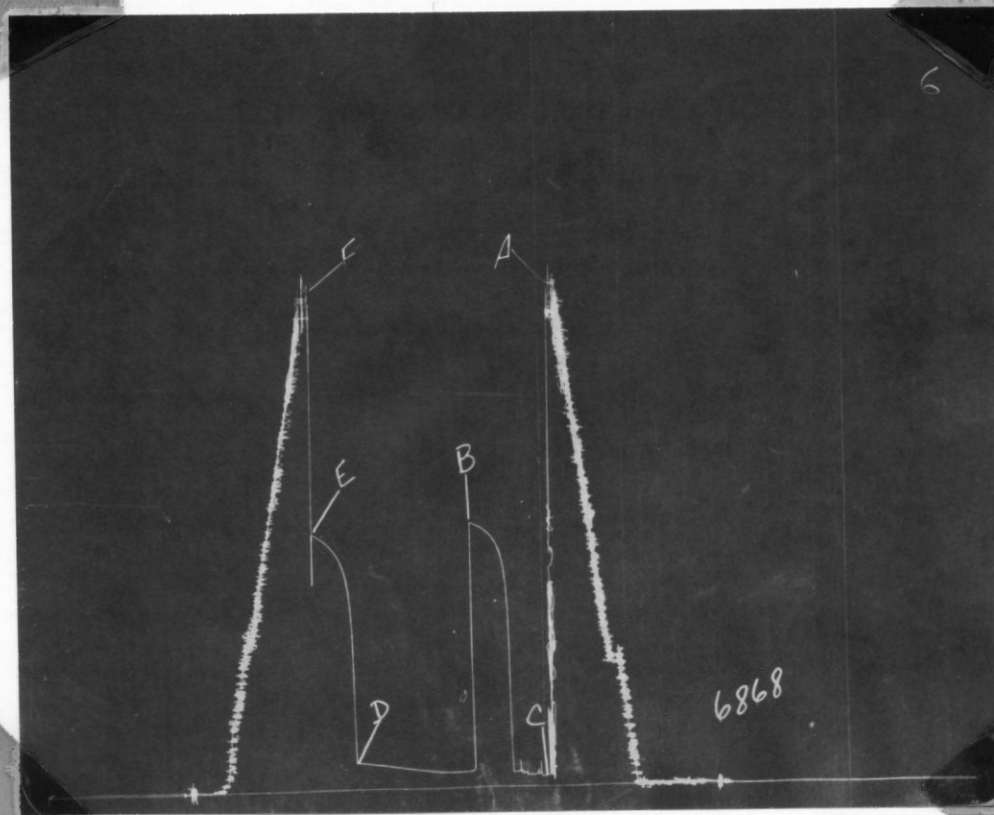

Tool Open 2 hr. 30 mins: Shut-in: Initial 30 mins: Final 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>2385</u>	<u>2425</u>
(B) Initial Shut-in Pressure	<u>1290</u>	<u>1281</u>
(C) Initial Flow Pressure	<u>65</u>	<u>46</u>
(D) Final Flow Pressure	<u>150</u>	<u>128</u>
(E) Final Shut-in Pressure	<u>1245</u>	<u>1235</u>
(F) Final Hydrostatic Pressure	<u>2380</u>	<u>2379</u>
