

SUPERIOR TESTERS, INC.

433 SOUTH WESTVIEW, DERBY, KANSAS

Date 10/20/71 Ticket No. 2481 Elevation _____

Total Depth 3250 Tested From 3233 To 3250 . Formation Tested Kansas City

Blow Strong through out test

Mud Wt. 9.8 Viscosity 38 Bottom Hole Temp 105

Size Bottom Choke 1/2" Size Top Choke 1/2"

Size Drill Pipe 4 1/2" Size Hole 7 7/8" Length Air Chamber - Ft.

Initial Shut in Time 45 Min Tool Open 60 Hr. 60 Min Final Shut in Time 45 Min

Recovery 50' heavy oil cut mud, 180'

froggy gassy oil

Office Corrected Pressure Reading

Initial Shut in Pressure 1071 Lbs

Initial Flow Pressure 44 88 Lbs

Final Flow Pressure 112 120 Lbs

Final Shut in Pressure 1047 Lbs

Initial Hydrostatic Pressure 1737 Lbs

Final Hydrostatic Pressure 1723 Lbs

Remarks _____

Witnessed By J. C. Musgrove

Tool Operator Art Budig

Location SW, SE, NE 8-19S-14W

County Barton

State Kansas

Name of Lease Schultz

Well No. 1


Test No. 1

Company Oleum Pipe

Company

2481

DST
#1

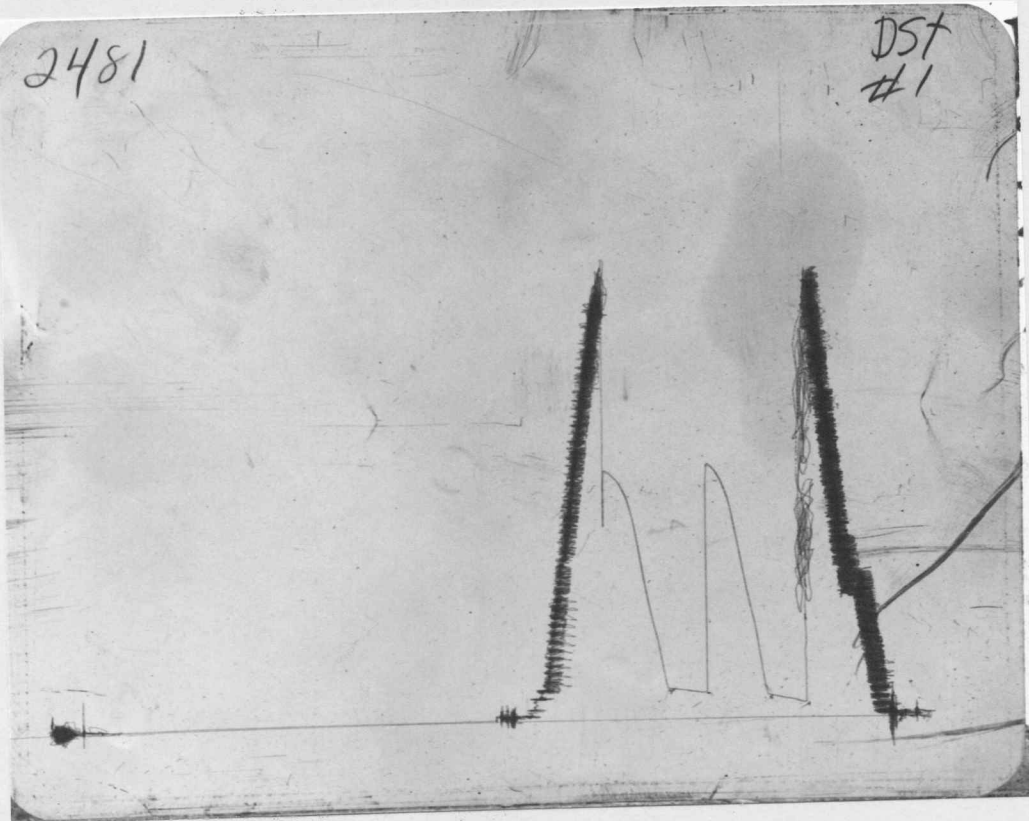

SUPERIOR TESTERS, INC.

433 SOUTH WESTVIEW, DERBY, KANSAS

Date 10/21/71 Ticket No. 2482 Elevation _____

Total Depth 3265 Tested From 3251 To 3265 Formation Tested Kansas City

Blow Very weak 7 minute blow

Mud Wt. 9.8 Viscosity 38 Bottom Hole Temp 102

Size Bottom Choke 1/2" Size Top Choke 1/2"

Size Drill Pipe 4 1/2" KH Size Hole 7 7/8" Length Air Chamber - Ft.

Initial Shut in Time 20 Min Tool Open 40 Hr 40 Min Final Shut in Time 20 Min

Recovery 5' of mud

Office Corrected Pressure Reading

Initial Shut in Pressure 40 Lbs

Initial Flow Pressure 32 Lbs

Final Flow Pressure 32 Lbs

Final Shut in Pressure 32 Lbs

Initial Hydrostatic Pressure 1776 Lbs

Final Hydrostatic Pressure 1758 Lbs

Remarks _____

Witnessed By J. C. Musgrove

Tool Operator Art Budig

Location SW, SE, NE 8-19S-14W

Schultz

Name of Lease

1

Well No.

2

Test No.

County Barton

State Kansas

Glenn Rube

Company

2482

DST
#2

