

Sun Oil Well Cementing, Inc.

DRILL STEM TEST DATA

P.O. Box 169

Great Bend, Kansas 67530

Lease	Sebes	Well No.	1	Date	10/26/76
County	Hodgeman Sec. 21	Twp.	22 Rng. 24	Elevation	
Company	L. G. Stephenson			Test No.	1
Contractor	Red Tiger #6			Zone Tested	Miss
Charge To	L. G. Stephenson			Ticket #	2245Tx
Approved By	James W. Spellman			Tester	Floyd

Initial Hydro Mud Press. 2597 P.S.I.

Initial Flow Press. 75 To 267 P.S.I. Initial Flow Period 60 Min.

Initial Shut-in Press. 1090 P.S.I. Initial Shut-in 45 Min.

Final Flow Press. 295 To 525 P.S.I. Final Flow Period 120 Min.

Final Shut-in Press. 910 P.S.I. Final Shut-in 45 Min.

Final Hydro Mud Press. 2475 P.S.I. TIME TOOL OPEN

Temperature 135 Deg.

Mud Weight 9.8 Viscosity 48

Fluid Loss 9.5

Interval Tested 4678 To 4724

Top Packer Depth 4673 Surface Choke Size

Bottom Packer Depth X 4678 Bottom Choke Size 5/8

Total Depth 4724 Main Hole Size 7 7/8

Drill Pipe Size Wt Rubber Size 6 3/4


Drill Collar I.D. Ft. Run

Blow Strong Decresasing to good


Recovery 6" clean oil 110' very slight oil cut watery mud 180' muddy water 120'

oil speck gassy water 240' muddy water 360' water. gassy.

TOP

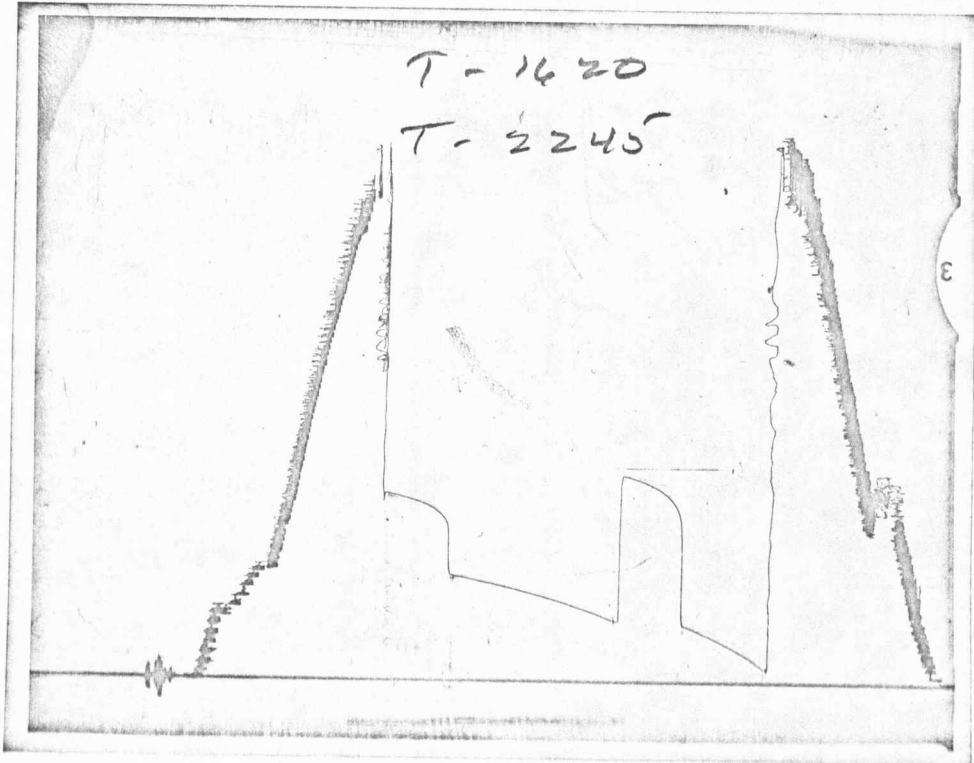

BOTTOM

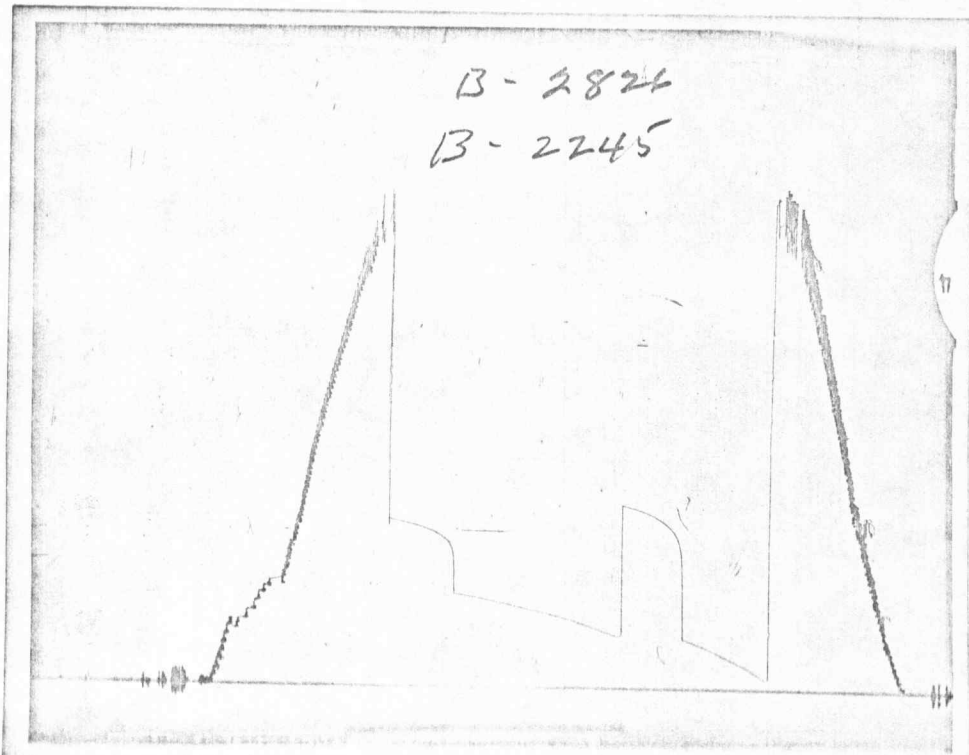

Sun Oil Well Cementing, Inc.

DRILL STEM TEST DATA

P.O. Box 169

Great Bend, Kansas 67530

Lease	Sebee	Well No.	1	Date	10/27/76
County	Hodgeman	Sec.	21	Twp.	22
		Rng.	24	Elevation	
Company	L. G. Stephenson			Test No.	2
Contractor	Red Tiger			Zone Tested	Cherokee
Charge To	L. G. Stephenson			Ticket #	2246Tx
Approved By	James Spellmen			Tester	Floyd Bowman

Initial Hydro Mud Press. 2526 P.S.I.

Initial Flow Press. 10 To 10 P.S.I. Initial Flow Period 30 Min.

Initial Shut-in Press. 30 P.S.I. Initial Shut-in 30 Min.

Final Flow Press. 10 To 10 P.S.I. Final Flow Period 30 Min.

Final Shut-in Press. 12 P.S.I. Final Shut-in 30 Min.

Final Hydro Mud Press. 2516 P.S.I. TIME TOOL OPEN

Temperature

Mud Weight 9.8 Viscosity 51

Fluid Loss 9.5

Interval Tested 4643 To 4658

Top Packer Depth 4643 Surface Choke Size

Bottom Packer Depth 4658 Bottom Choke Size 5/8

Total Depth 4751 Main Hole Size 7 7/8


Drill Pipe Size Wt Rubber Size 6 3/4

Drill Collar I.D. Ft. Run

Blow Very Weak Dead in 10 min.

Recovery 5' drilling mud

TOP

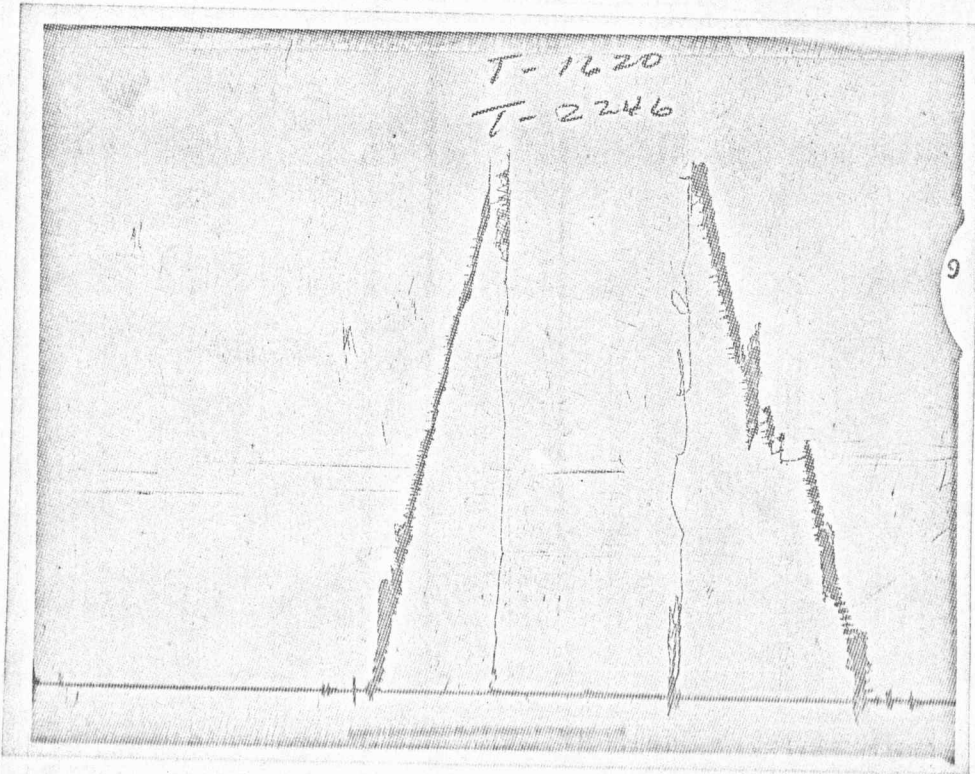

BOTTOM

