

Date 10-8-64

Ticket No. 4251

Company Hinkle Oil Co. Contractor Hellar Drlg.

Well No. 2 Lease Petrowsky County Pratt Sec. 10 Rg. 26 Tw. 12

Test No. 1 Size Hole 7 7/8 Tool Joint 4 1/2 X H

Anchor Length 60' Depth Well 3685'

Interval Tested From 3625' To 3685'

Size Choke 5/8 Tool Open 105 min.

IBHP Shut in time 30 min. FBHP Shut in time 30 min.


Blow Good thruout test

Recovery 300' Gas in pipe 550' Hvy. Gas cut watery mud with scum of oil

120' Gas cut water with scum of oil

Remarks _____

Approved Howell Tester Williams

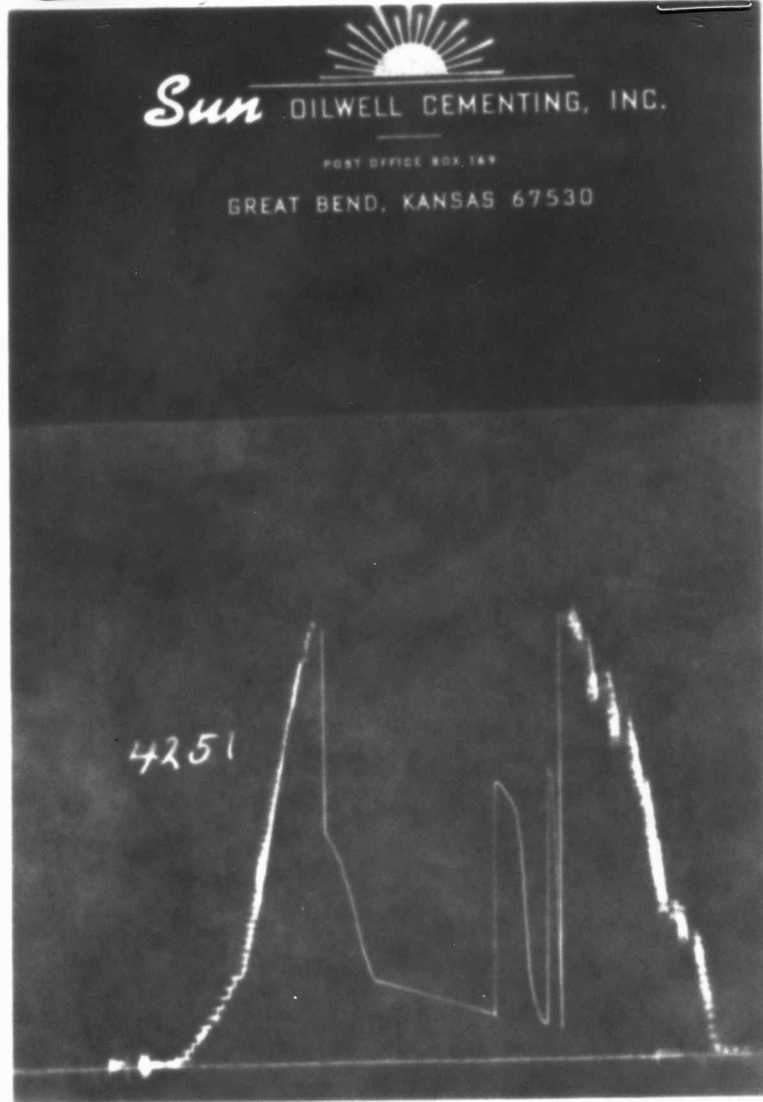

F. Final BHP

986#

Date 10-12-64

Ticket No. 4252

Company Hinkle Oil Co. Contractor Hellar Drlg.

Well No. 2 Lease Petrowsky County Pratt Sec. 10 Rg. 26 Tw. 12

Test No. 2 Size Hole 7 7/8 Tool Joint 4 1/2 X H

Anchor Length 5' Depth Well 4277'

Interval Tested From 4272' To 4277'

Size Choke 5/8 Tool Open 36 min.

IBHP Shut in time 30 min. FBHP Shut in time 30 min.

Blow Weak 5 min. flushed tool good surge

Recovery 100' Gas in pipe 25' Oil & Gas cut mud 20% Oil & Gas

Remarks _____


Aproved Howell Tester Williams



Sun OILWELL CEMENTING, INC.

POST OFFICE BOX 149

GREAT BEND, KANSAS 67530

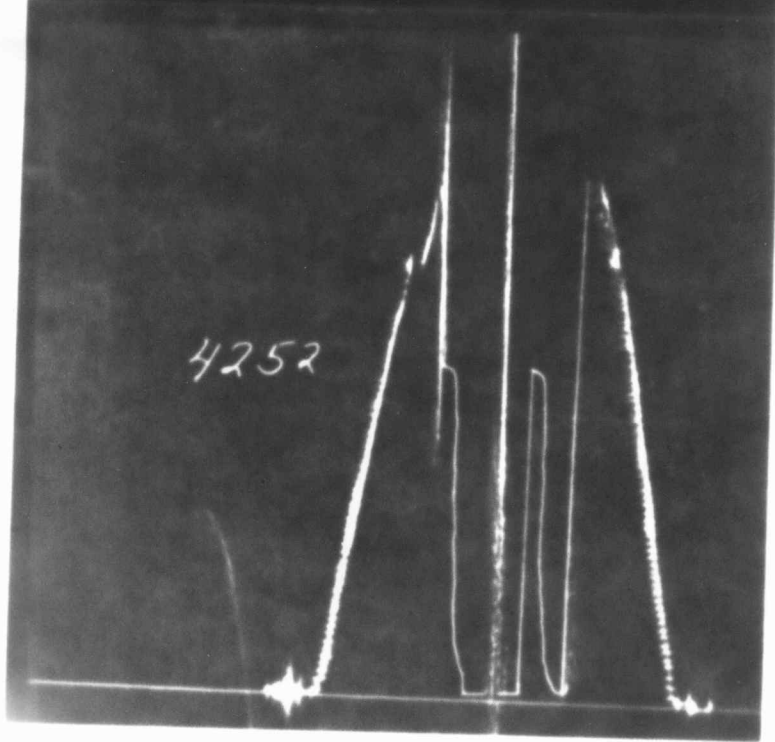

F. Final BHP

1458#

Date 10-13-64

Ticket No. 4253

Company Hinkle Oil Co. Contractor Hellar Drlg.

Well No. 2 Lease Petrowdky County Pratt Sec. 10 Rg. 26 Tw. 12

Test No. 3 Size Hole 7 7/8 Tool Joint 4 1/2 X H

Anchor Length 6' Depth Well 4283'

Interval Tested From 4277' To 4283'

Size Choke 5/8 Tool Open 95 min.


IBHP Shut in time 30 min. FBHP Shut in time 30 min.

Blow Strong thruout test

Recovery 2125' Gas in pipe 160' Clean gassy oil 120' Sl. Mud cut gassy oil

Remarks _____

Approved Howell Tester Williams

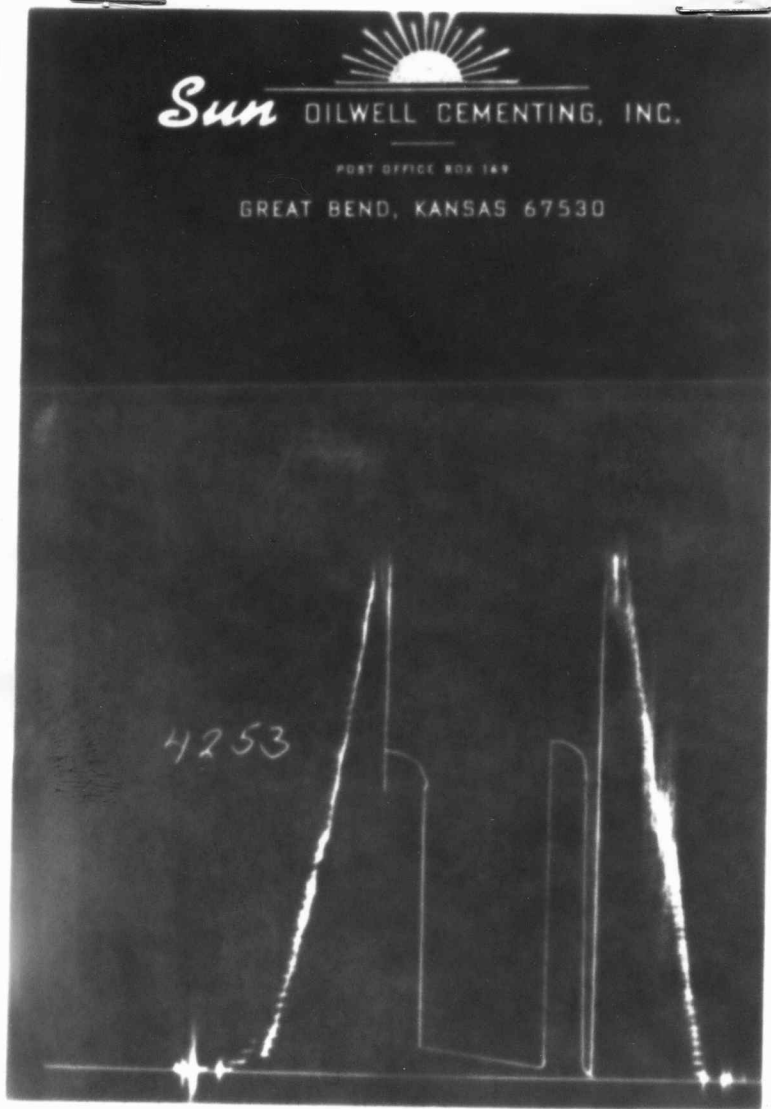

F. Final BHP

1405#
