

15-007-00697

MILLER TESTING COMPANY

Box 547

15-32s-13w

GREAT BEND, KANSAS

Company AYLWARD DRILLING COMPANYLease and Well No. LENKNER # 1County BARBER State KANSASDate MARCH 22, 1963

Formation Test No.	<u>1</u>	Total Depth	<u>3940</u>
Interval Tested	<u>3896</u>	To	<u>3940</u>
		Anchor Length	<u>44'</u>
Size Hole	<u>7 7/8</u>	Size Drill Pipe	<u>4 1/2 FH</u>
		Size Packer	<u>6 3/4</u>
Mud Weight	<u>9.8</u>	Viscosity	<u>4+</u>
		Bottom Hole Temp.	<u> </u> ° F
Chokes: Top	<u>1/2</u>	Bottom	<u>1/2</u>
		Ticket No.	<u>6462</u>

RECOVERY


INITIAL OPENING 10 MINUTES.

FAIR BLOW THROUGHOUT TEST.

310 FEET OF WATERY MUD

Lease and Well No. LENKNER # 1 15 32 13W C NW NWFormation Test No. 1

Pressure: Each Square _____ psi

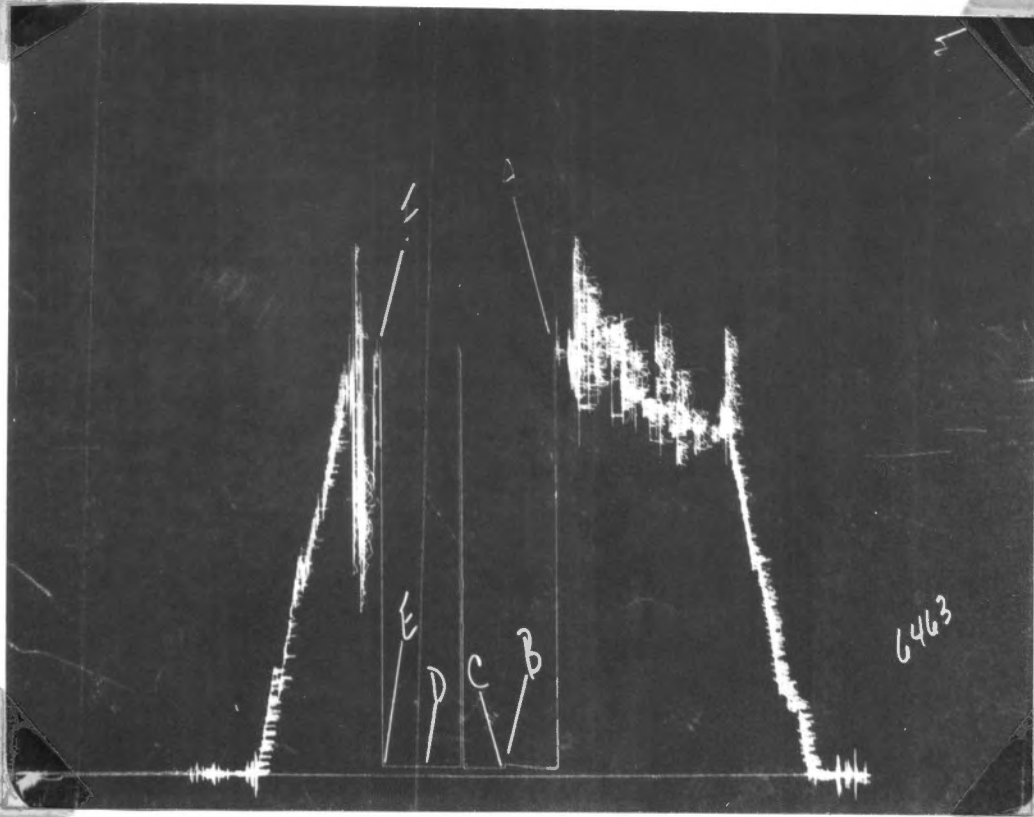

Tool Open 1 hr. _____ mins: Shut-in: Initial _____ hr. 30 mins: Final _____ hr. 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>2460</u>	<u>2449</u>
(B) Initial Shut-in Pressure	<u>67</u>	<u>69</u>
(C) Initial Flow Pressure	<u>22</u>	<u>47</u>
(D) Final Flow Pressure	<u>22</u>	<u>56</u>
(E) Final Shut-in Pressure	<u>22</u>	<u>56</u>
(F) Final Hydrostatic Pressure	<u>2401</u>	<u>2438</u>

6463

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company AYLWARD DRILLING COMPANY

Lease and Well No. LENKNER # 1

County BARBER

State KANSAS

Date MARCH 26, 1963

Formation Test No. 2 Total Depth 4440
Interval Tested 4410 To 4440 Anchor Length 30'
Size Hole 7 7/8 Size Drill Pipe 4 1/2 FH Size Packer 6 3/4
Mud Weight 9.7 Viscosity 43 Bottom Hole Temp. ° F
Chokes: Top 1/2 Bottom 1/2 Ticket No. 6463

RECOVERY

INITIAL OPENING 10 MINUTES.


WEAK BLOW FOR 10 MINUTES AND
DIED. FLUSHED TOOL AFTER 30
MINUTES.

30 FEET OF DRILLING MUD.

Lease and Well No. LENKNER # 1 15 32 13W C NW NW

Formation Test No. 2

Pressure: Each Square _____ psi

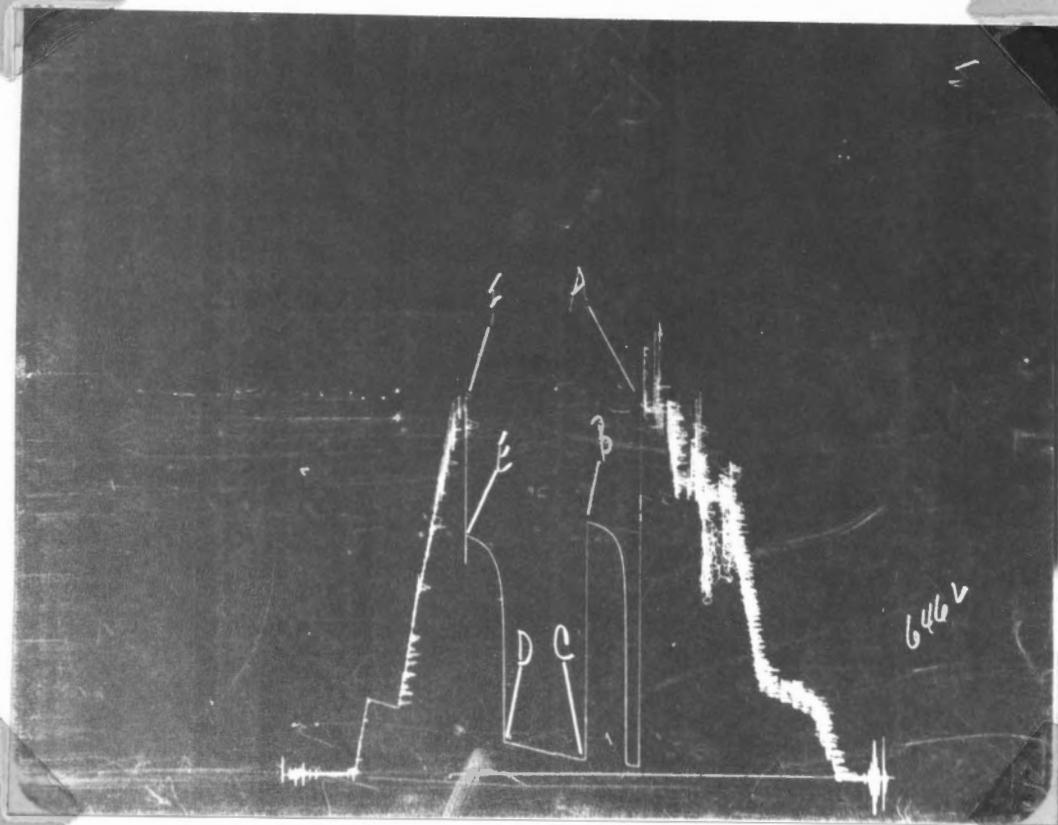

Tool Open 1 hr. _____ mins. Shut-in: Initial _____ hr. 30 mins. Final _____ hr. 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>2243</u>	<u>2144</u>
(B) Initial Shut-in Pressure	<u>1492</u>	<u>1448</u>
(C) Initial Flow Pressure	<u>156</u>	<u>78</u>
(D) Final Flow Pressure	<u>234</u>	<u>183</u>
(E) Final Shut-in Pressure	<u>1425</u>	<u>1370</u>
(F) Final Hydrostatic Pressure	<u>2235</u>	<u>2144</u>

6462

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company AYLWARD DRILLING COMPANY

Lease and Well No. LENKNER # 1

County BARBER State KANSAS Date MARCH 27, 1963

Formation Test No. 3 Total Depth 4469
Interval Tested 4449 To 4469 Anchor Length 20'
Size Hole 7 7/8 Size Drill Pipe 4 1/2 FH Size Packer 6 3/4
Mud Weight 10 Viscosity 56 Bottom Hole Temp. 118 ° F
Chokes: Top 1/2 Bottom 1/2 Ticket No. 6464

RECOVERY


INITIAL OPENING 10 MINUTES.
GOOD BLOW THROUGHOUT TEST.

65 FEET MUD

Lease and Well No. LENKNER # 1 15 32 13W C NW NW

Formation Test No. 3

Pressure: Each Square _____ psi

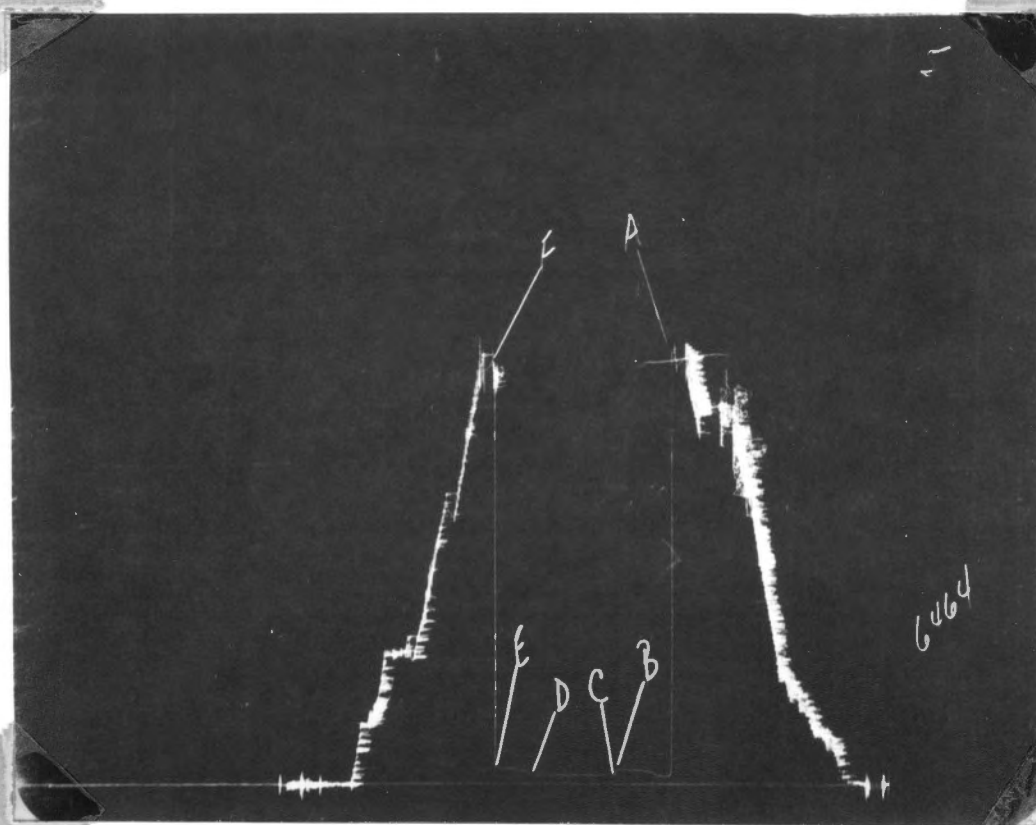

Tool Open 1 hr. _____ mins: Shut-in: Initial _____ hr. 30 mins: Final _____ hr. 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>2483</u>	<u>2472</u>
(B) Initial Shut-in Pressure	<u>67</u>	<u>78</u>
(C) Initial Flow Pressure	<u>44</u>	<u>49</u>
(D) Final Flow Pressure	<u>44</u>	<u>49</u>
(E) Final Shut-in Pressure	<u>89</u>	<u>89</u>
(F) Final Hydrostatic Pressure	<u>2460</u>	<u>2460</u>

6464
