

BEE FORMATION TESTING CO.

P. O. BOX 491

GREAT BEND, KANSAS

Nº 1519

DATE 11-8-56CUSTOMER'S
ORDER NO. 3476NAME OF COMPANY J. F. DARBYADDRESS TO MAIL INVOICE 1807 PHILTOWER BLDG. - TULSA 3, OKLA.ADDRESS TO MAIL PRESSURE CHARTS SAMELEASE FARREL WELL NO. #B-1 COUNTY GRAHAM STATE KANSASTESTER L.C. Skinner Jr APPROVED Meritt H BrownDRILL STEM TEST NO. 1 SUCCESSFUL NO. 1 MIS-RUN NO. 0 FORMATION TESTED K.C.SIZE HOLE 7 7/8 TOOL JT. 4 1/2 FHRUBBER SIZE 6 3/4 x 2 7/8 x 30 TEST TOOL SIZE 4 5/8PACKER SET AT 3696' ANCHOR SIZE 4 1/2 FHTOTAL DEPTH WELL 3718' LENGTH ANCHOR 22'PRESSURE RECORDER CAP. 3000 X 3000 DRILL PIPE RUN: DRY ✓ WITH FLUID


RESULTS:

PACKER SET 2:45 P M. TOOL OPEN 2:50 P M. TOOL OPEN 1 HRS.BLOW WEAK BLOW FOR 31 MIN THEN DIEDRECOVERY 4.0' SLIGHTLY OIL CUT MUDSHUT IN PRESSURE TIME 20 MIN. MUD WT. 9.9 VIS. 38 WATER LOSS 12.8BHP 785 IFP 0 FFP 0 HYDROSTATIC HEAD 1875EXTRA EQUIPMENT NONE JARS ✓ NO. ✓ SIZE ✓

OPERATOR TIME TOOL RENTAL TIME

BEE FORMATION TESTING CO.

SHALL NOT BE LIABLE FOR DAMAGE OF ANY KIND TO THE PROPERTY OR PERSONNEL OF THE PARTY FOR WHOM A TEST IS MADE, OR FROM ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH OR IN THE COURSE OF THE USE OF ITS EQUIPMENT, ALL OF WHICH LOSS OR DAMAGE IS ASSUMED BY THE CUSTOMER. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT THE COST OF THE PARTY FOR WHOM TEST IS MADE.

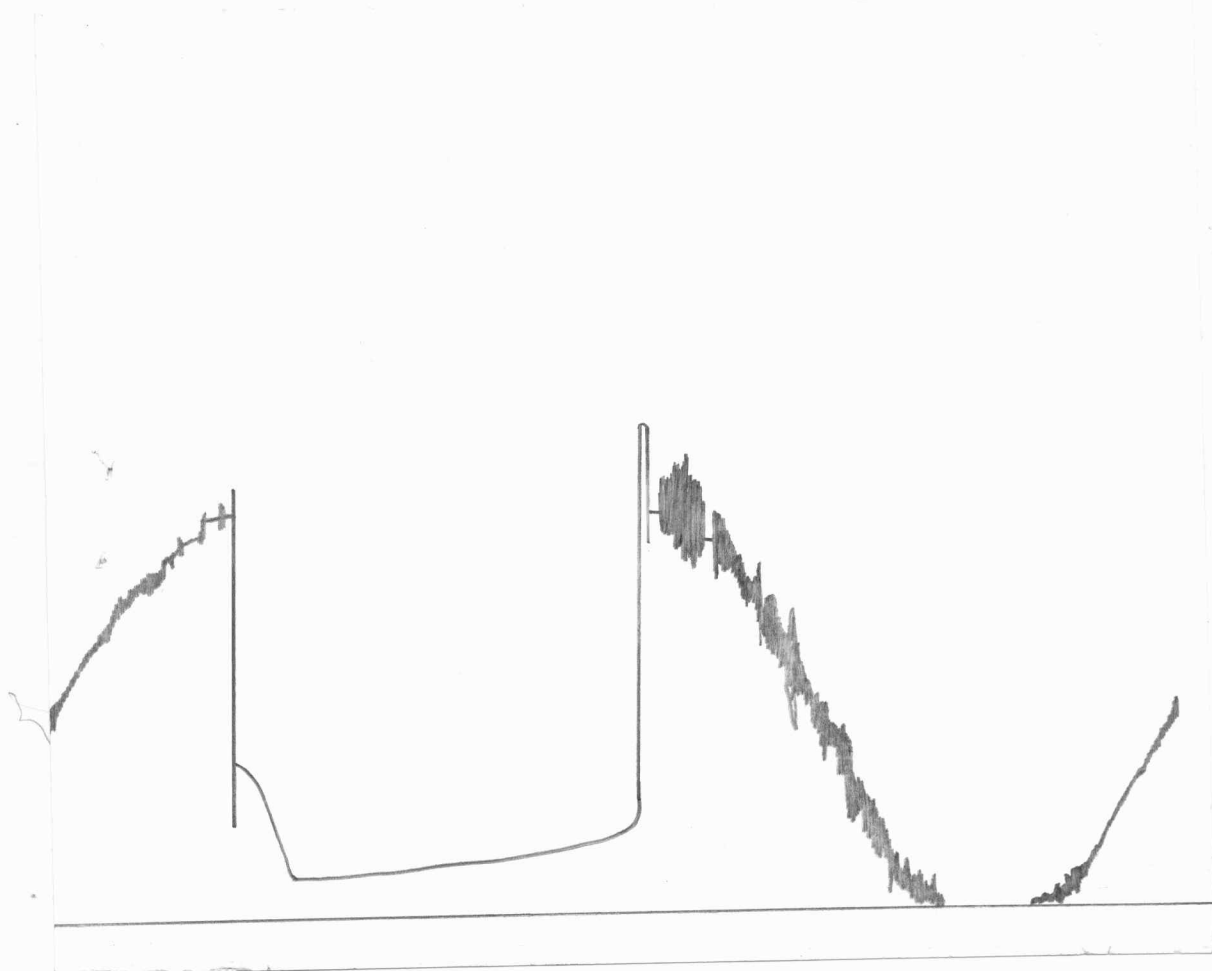

TEST TICKET

BEE FORMATION TESTING CO.

P. O. BOX 491

GREAT BEND, KANSAS

No 1720

DATE 11-9-56CUSTOMER'S
ORDER NO. 3477NAME OF COMPANY J. F. DarbyADDRESS TO MAIL INVOICE 1807 Phil Tower Bldg. Tulsa 3, OKLA.ADDRESS TO MAIL PRESSURE CHARTS SAMELEASE FARRELL WELL NO. 2B-1 COUNTY GRAHAM STATE KANSASTESTER D.K. WesthusinAPPROVED M. J. FoyDRILL STEM TEST NO. 2 SUCCESSFUL NO. 2 MIS-RUN NO. 0 FORMATION TESTED K.C.SIZE HOLE 7 7/8 TOOL JT. 4 1/2 F.H.RUBBER SIZE 6 3/4 - 2 1/4 - 2 1/4 TEST TOOL SIZE 4 1/2PACKER SET AT 3740 ANCHOR SIZE 4 1/2TOTAL DEPTH WELL 3760 LENGTH ANCHOR 20'PRESSURE RECORDER CAP. 3000-3000 DRILL PIPE RUN: DRY yes WITH FLUID —

RESULTS:

PACKER SET 7:00 A.M. TOOL OPEN 7:05 A.M. TOOL OPEN 1 1/4 hrs. HRS.BLOW Fair Steady Blow through out Test.RECOVERY 150' oil cut muddy salt water.SHUT IN PRESSURE TIME 30 MIN. MUD WT. 40 VIS. 92 WATER LOSS 9.9BHP 1195 IFP 0 FFP 65 HYDROSTATIC HEAD 2000"EXTRA EQUIPMENT NONE JARS — NO. — SIZE —OPERATOR TIME — TOOL RENTAL TIME —

BEE FORMATION TESTING CO.

SHALL NOT BE LIABLE FOR DAMAGE OF ANY KIND TO THE PROPERTY OR PERSONNEL OF THE PARTY FOR WHOM A TEST IS MADE, OR FROM ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH OR IN THE COURSE OF THE USE OF ITS EQUIPMENT, ALL OF WHICH LOSS OR DAMAGE IS ASSUMED BY THE CUSTOMER. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT THE COST OF THE PARTY FOR WHOM TEST IS MADE.

