

CONFIDENTIAL

CONFIDENTIAL

ORIGINAL

Form ACO-1

September 1999

Form Must Be Typed

KANSAS CORPORATION COMMISSION  
OIL & GAS CONSERVATION DIVISION  
**WELL COMPLETION FORM**  
WELL HISTORY - DESCRIPTION OF WELL & LEASE

Operator: License # 5447  
Name: OXY USA Inc.  
Address: P.O. Box 2528  
City/State/Zip: Liberal, KS 67905  
Purchaser: NA  
Operator Contact Person: Rafael Bacigalupo  
Phone: (620) 629-4200  
Contractor: Name: Murfin Drilling Co., Inc.  
License: 30606  
Wellsite Geologist: NA  
Designate Type of Completion:  
☒ New Well ☐ Re-Entry ☐ Workover  
☐ Oil ☐ SWD ☐ SIOW ☐ Temp. Abd.  
☒ Gas ☐ ENHR ☐ SIGW  
☐ Dry ☐ Other (Core, WSW, Expl, Cathodic, etc)  
If Workover/Re-entry: Old Well Info as follows:  
Operator: \_\_\_\_\_  
Well Name: \_\_\_\_\_

Original Comp. Date: \_\_\_\_\_ Original Total Depth: \_\_\_\_\_  
☐ Deepening ☐ Re-perf. ☐ Conv. To Enhr./SWD  
☐ Plug Back ☐ Plug Back Total Depth  
☐ Commingled ☐ Docket No. \_\_\_\_\_  
☐ Dual Completion ☐ Docket No. \_\_\_\_\_  
☐ Other (SWD or Enhr.?) ☐ Docket No. \_\_\_\_\_  
02/10/07 02/22/06 03/14/07  
Spud Date or ☐ Date Reached TD ☐ Completion Date or  
Recompletion Date ☐ Recompletion Date

API No. 15 - 175-22081-00-00  
County: Seward  
NE - SW - NE Sec 21 Twp. 34S S. R. 33W  
1900 feet from S / ☒ (circle one) Line of Section  
1750 feet from ☐ / W (circle one) Line of Section  
Footages Calculated from Nearest Outside Section Corner:  
(circle one) ☒ NE SE NW SW  
Lease Name: Bruns B Well #: 1  
Field Name: Eubank South  
Producing Formation: L Morrow  
Elevation: Ground: 2847 Kelly Bushing: 2858  
Total Depth: 6600 Plug Back Total Depth: 6126  
Amount of Surface Pipe Set and Cemented at 1693 feet  
Multiple Stage Cementing Collar Used? ☐ Yes ☒ No  
If yes, show depth set \_\_\_\_\_  
If Alternate II completion, cement circulated from \_\_\_\_\_  
feet depth to \_\_\_\_\_ w/ \_\_\_\_\_ sx cmt.

Drilling Fluid Management Plan Alt INH10-2808  
(Data must be collected from the Reserve Pit)  
Chloride content 2000 mg/l ppm Fluid volume 1650 bbls  
Dewatering method used Evaporation  
Location of fluid disposal if hauled offsite: \_\_\_\_\_  
Operator Name: \_\_\_\_\_  
Lease Name: \_\_\_\_\_ License No.: \_\_\_\_\_  
Quarter \_\_\_\_\_ Sec. \_\_\_\_\_ Twp. \_\_\_\_\_ S. R. ☐ East ☐ West  
County: \_\_\_\_\_ Docket No.: \_\_\_\_\_

INSTRUCTIONS: An original and two copies of this form shall be filed with the Kansas Corporation Commission, 130 S. Market - Room 2078, Wichita, Kansas 6702, within 120 days of the spud date, recompletion, workover or conversion of a well. Rule 82-3-130, 82-3-106 and 82-3-107 apply. Information of side two of this form will be held confidential for a period of 12 months if requested in writing and submitted with the form (see rule 82-3-107 for confidentiality in excess of 12 months). One copy of all wireline logs and geologist well report shall be attached with this form. ALL CEMENTING TICKETS MUST BE ATTACHED. Submit CP-4 form with all plugged wells. Submit CP-111 form with all temporarily abandoned wells.

All requirements of the statutes, rules and regulations promulgated to regulate the oil and gas industry have been fully complied with and the statements herein are complete and correct to the best of my knowledge.

Signature: \_\_\_\_\_  
Title: Capital Project Date 05/01/2007  
Subscribed and sworn to before me this 1 day of May  
20 07  
Notary Public: Anita Peterson  
Date Commission Expires: Oct. 1, 2009

ANITA PETERSON  
Notary Public - State of Kansas  
My Appt. Expires October 1, 2009

## KCC Office Use Only

Y Letter of Confidentiality Attached  
If Denied, Yes ☐ Date: \_\_\_\_\_  
✓ Wireline Log Received  
✓ Geologist Report Received  
\_\_\_\_ UIC Distribution

RECEIVED  
KANSAS CORPORATION COMMISSION

MAY 03 2007  
CONSERVATION DIVISION  
WICHITA, KS

## Side Two

Operator Name: OXY USA Inc. Lease Name: Bruns B Well #: 1  
 Sec. 21 Twp. 34 S. R. 33W ☐ East ☐ West County: Seward

**Instructions:** Show important tops and base of formations penetrated. Detail all cores. Report all final copies of drill stems tests giving interval tested, time tool open and closed, flowing and shut-in pressures, whether shut-in pressure reached static level, hydrostatic pressures, bottom hole temperature, fluid recovery, and flow rates if gas to surface test, along with final chart(s). Attach extra sheet if more space is needed. Attach copy of all Electric Wireline Logs surveyed. Attach final geological well site report.

Drill Stem Tests Taken ☐ Yes ☒ No  
 (Attach Additional Sheets)

Samples Sent to Geological Survey ☐ Yes ☒ No

Cores Taken ☐ Yes ☒ No

Electric Log Run ☒ Yes ☐ No  
 (Submit Copy)

List All E. Logs Run: Cement Bond Log  
 Microlog Long Spaced Sonic  
 Spectral Density Dual Spaced Neutron  
 High Resolution Induction

☒ Log Formation (Top), Depth and Datum ☐ Sample

| Name          | Top  | Datum |
|---------------|------|-------|
| Chase         | 2662 | 196   |
| Council Grove | 2997 | -139  |
| Wilbaunsee    | 3489 | -631  |
| Hebner Shale  | 4292 | -1434 |
| Toronto       | 4336 | -1478 |
| Lansing       | 4230 | -1672 |
| Kansas City   | 4859 | -2001 |

(See Side Three)

CASING RECORD ☒ New ☐ Used

Report all strings set-conductor, surface, intermediate, production, etc.

| Purpose of String | Size Hole Drilled | Size Casing Set(in. O.D.) | Weight Lbs./ft. | Setting Depth | Type of Cement | # Sacks Used | Type and Percent Additives |
|-------------------|-------------------|---------------------------|-----------------|---------------|----------------|--------------|----------------------------|
| Conductor         |                   |                           |                 |               | C              |              |                            |
| Surface           | 12 1/4            | 8 5/8                     | 24              | 1693          | C              | 585          | Poz C + additives          |
|                   |                   |                           |                 |               | C              | 195          | Class C + additives        |
| Production        | 7 7/8             | 5 1/2                     | 17              | 6595          | C              | 215          | Poz H + additives          |

## ADDITIONAL CEMENTING / SQUEEZE RECORD

| Purpose:                                | Depth Top Bottom | Type of Cement | #Sacks Used | Type and Percent Additives |
|-----------------------------------------|------------------|----------------|-------------|----------------------------|
| <input type="checkbox"/> Perforate      |                  |                |             |                            |
| <input type="checkbox"/> Protect Casing | -                |                |             |                            |
| <input type="checkbox"/> Plug Back TD   |                  |                |             |                            |
| <input type="checkbox"/> Plug off Zone  | -                |                |             |                            |

| Shots Per Foot                                             | PERFORATION RECORD - Bridge Plugs Set/type Specify Footage of Each Interval Perforated | Acid, Fracture, Shot, Cement Squeeze Record (Amount and Kind of Material Used)                                                                                               | Depth                              |
|------------------------------------------------------------|----------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------|
| 8                                                          | 6142-6156                                                                              | 2200 gals 17% FE acid + additives                                                                                                                                            |                                    |
|                                                            |                                                                                        | 12,894 gals 15# X-link foamed @ 75% N2; 20/40 Sand 70,000# 20/40 Sand                                                                                                        |                                    |
|                                                            | RBP @ 6126 (w/2 sx sand on top)                                                        |                                                                                                                                                                              |                                    |
| 8                                                          | 6068-6090                                                                              |                                                                                                                                                                              |                                    |
| 6                                                          | 6052-6058, 6034-6044                                                                   |                                                                                                                                                                              |                                    |
| TUBING RECORD Size Set At Packer At                        |                                                                                        | Liner Run <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No                                                                                                |                                    |
| Date of First, Resumed Production, SWD or Enhr. 04/03/2007 |                                                                                        | Producing Method <input checked="" type="checkbox"/> Flowing <input type="checkbox"/> Pumping <input type="checkbox"/> Gas Lift <input type="checkbox"/> Other (Explain) P&A |                                    |
| Estimated Production Per 24 Hours                          | Oil BBLS 0                                                                             | Gas Mcf 579                                                                                                                                                                  | Water Bbls 0 Gas-Oil Ratio Gravity |

Disposition of Gas

METHOD OF COMPLETION

Production Interval

☐ Vented ☒ Sold ☐ Used on Lease  
 (If vented, Submit ACO-18)

☐ Open Hole ☒ Perf. ☐ Dually Comp. ☐ Commingled

☐ Other (Specify) \_\_\_\_\_

**CONFIDENTIAL**

Side Three

Operator Name: OXY USA Inc. Lease Name: Bruns B Well #: 1  
Sec. 21 Twp. 34 S. R. 33W ☐ East ☐ West County: Seward

| Name          | Top  | Datum |
|---------------|------|-------|
| Marmaton      | 5185 | -2327 |
| Cherokee      | 5510 | -2652 |
| Atoka         | 5622 | -2764 |
| Morrow        | 5806 | -2948 |
| Chester       | 6064 | -3206 |
| St. Genevieve | 6427 | -3569 |
| TD            | 6600 |       |

KGCC  
MAY 01 2007  
CONFIDENTIAL

RECEIVED  
KANSAS CORPORATION COMMISSION

MAY 03 2007

CONSERVATION DIVISION  
WICHITA, KS



# Cementing Service Report

| Customer<br>OXY RESOURCE CALIFORNIA LLC                                                                                                                                        |       |                                           |                   |                                       |                | Job Number<br>2205553140                                  |                         |                                                                      |                      |                                            |  |                            |  |                      |  |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------|-------------------------------------------|-------------------|---------------------------------------|----------------|-----------------------------------------------------------|-------------------------|----------------------------------------------------------------------|----------------------|--------------------------------------------|--|----------------------------|--|----------------------|--|
| Well<br><b>BRUNS B-1</b><br>BRUISE-1                                                                                                                                           |       | Location (legal)                          |                   | Schlumberger Location<br>Perryton, TX |                | Job Start<br>2007-Feb-11                                  |                         |                                                                      |                      |                                            |  |                            |  |                      |  |
| Field                                                                                                                                                                          |       | Formation Name/Type                       |                   | Deviation<br>°                        |                | Bit Size<br>in                                            |                         | Well MD<br>1,659 ft                                                  |                      | Well TVD<br>ft                             |  |                            |  |                      |  |
| County<br>HASKELL                                                                                                                                                              |       | State/Province<br>KANSAS                  |                   | BHP<br>psi                            |                | BHST<br>°F                                                |                         | BHCT<br>°F                                                           |                      | Pore Press. Gradient<br>psi/ft             |  |                            |  |                      |  |
| Well Master:<br>0000022222                                                                                                                                                     |       | API / UWI:                                |                   | Casing/Liner                          |                |                                                           |                         |                                                                      |                      |                                            |  |                            |  |                      |  |
| Rig Name                                                                                                                                                                       |       | Drilled For<br>Oil & Gas                  |                   | Service Via                           |                | Depth, ft<br>1659                                         |                         | Size, in<br>8.63                                                     |                      | Weight, lb/ft                              |  | Grade                      |  | Thread               |  |
| Offshore Zone                                                                                                                                                                  |       | Well Class<br>New                         |                   | Well Type<br>Development              |                | Tubing/Drill Pipe                                         |                         |                                                                      |                      |                                            |  |                            |  |                      |  |
| Drilling Fluid Type                                                                                                                                                            |       | Max. Density<br>lb/gal                    |                   | Plastic Vt: cp                        |                | Depth,                                                    |                         | Size, in                                                             |                      | Weight, lb/ft                              |  | Grade                      |  | Thread               |  |
| Service Line<br>Cementing                                                                                                                                                      |       | Job Type<br>Cem Surface Casing            |                   | Perforations/Open Hole                |                |                                                           |                         |                                                                      |                      |                                            |  |                            |  |                      |  |
| Max. Allowed Tubing Pressure<br>psi                                                                                                                                            |       | Max. Allowed Ann. Pressure<br>psi         |                   | Wellhead Connection<br>8 5/8 HSM      |                | Top, ft                                                   |                         | Bottom, ft                                                           |                      | spf                                        |  | No. of Shots               |  | Total Interval<br>ft |  |
| Service Instructions<br>Cement 8 5/8 surface casing with<br>10 bbl fresh water,<br>585 SK 35:65 Poz/ C +6%D20 +2% S001 + 0.25 % D130<br>195 SK CLASS C + 2% S001 + 0.125% d130 |       |                                           |                   |                                       |                | Treat Down                                                |                         | Displacement<br>105.18 bbl                                           |                      | Packer Type                                |  | Packer Depth<br>ft         |  |                      |  |
|                                                                                                                                                                                |       |                                           |                   |                                       |                | Tubing Vol.<br>bbl                                        |                         | Casing Vol.<br>107.95 bbl                                            |                      | Annular Vol.<br>124.59 bbl                 |  | OpenHole Vol<br>246.94 bbl |  |                      |  |
|                                                                                                                                                                                |       |                                           |                   |                                       |                | Casing/Tubing Secured <input checked="" type="checkbox"/> |                         | 1 Hole Volume Circulated prior to Cementing <input type="checkbox"/> |                      | Casing Tools                               |  | Squeeze Job                |  |                      |  |
|                                                                                                                                                                                |       |                                           |                   |                                       |                | LIFT Pressure:<br>psi                                     |                         | Pipe Rotated <input type="checkbox"/>                                |                      | Pipe Reciprocated <input type="checkbox"/> |  | Shoe Type:                 |  | Squeeze Type         |  |
| No. Centralizers:                                                                                                                                                              |       | Top Plugs: 1                              |                   | Bottom Plugs:                         |                | Shoe Depth: ft                                            |                         | Tool Type:                                                           |                      |                                            |  |                            |  |                      |  |
| Cement Head Type: Single                                                                                                                                                       |       | Stage Tool Type                           |                   | Tool Depth: ft                        |                | Stage Tool Depth: ft                                      |                         | Tail Pipe Size: in                                                   |                      |                                            |  |                            |  |                      |  |
| Job Scheduled For:                                                                                                                                                             |       | Arrived on Location:<br>2007-Feb-11 18:30 |                   | Leave Location:<br>2007-Feb-11        |                | Collar Type:                                              |                         | Tail Pipe Depth: ft                                                  |                      |                                            |  |                            |  |                      |  |
|                                                                                                                                                                                |       |                                           |                   |                                       |                | Collar Depth: ft                                          |                         | Sqz Total Vol: bbl                                                   |                      |                                            |  |                            |  |                      |  |
| Date                                                                                                                                                                           | Time  | Treating Pressure<br>24 hr clock<br>psi   | Density<br>lb/gal | CMT RATE<br>bbl/min                   | CMT VOL<br>bbl | NRD RATE<br>bbl/min                                       | NRD VOLUME TOTAL<br>bbl | 0                                                                    | Message              |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:53 | 0                                         | 8.22              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:53 | 0                                         | 8.22              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:53 |                                           |                   |                                       |                |                                                           |                         |                                                                      | Start Job            |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:53 |                                           |                   |                                       |                |                                                           |                         |                                                                      | Start Pumping Spacer |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:53 | 0                                         | 8.21              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:53 |                                           |                   |                                       |                |                                                           |                         |                                                                      | Pressure Test Lines  |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:53 | 0                                         | 8.21              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:53 | 0                                         | 8.22              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:54 | 0                                         | 8.22              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:54 | 0                                         | 8.22              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:55 | 0                                         | 8.22              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:55 | 0                                         | 8.22              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:56 | 0                                         | 8.22              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:56 | 0                                         | 8.21              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:57 | 0                                         | 8.19              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:57 | 0                                         | 8.20              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:58 | 0                                         | 8.21              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:58 | 23                                        | 8.31              | 0.0                                   | 0.0            | 2.0                                                       | 0.5                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:59 | 23                                        | 8.31              | 0.0                                   | 0.0            | 1.9                                                       | 1.5                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 19:59 | 5                                         | 8.31              | 0.0                                   | 0.0            | 0.0                                                       | 2.1                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 20:00 | 1062                                      | 8.31              | 0.0                                   | 0.1            | 0.0                                                       | 2.2                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |
| 2007-Feb-11                                                                                                                                                                    | 20:00 | 1685                                      | 8.31              | 0.0                                   | 0.1            | 0.0                                                       | 2.2                     | 0                                                                    |                      |                                            |  |                            |  |                      |  |

KSC  
MAY 01 2007  
CONFIDENTIAL

RECEIVED  
KANSAS CORPORATION COMMISSION

MAY 03 2007

CONSERVATION DIVISION  
WICHITA, KS

| Well        |             |                   | Field   |          |         | Service Date |                  | Customer                    |                             | Job Number |
|-------------|-------------|-------------------|---------|----------|---------|--------------|------------------|-----------------------------|-----------------------------|------------|
| BRUISE #1   |             |                   |         |          |         | 0742-Feb-11  |                  | OXY RESOURCE CALIFORNIA LLC |                             | 2205553140 |
| Date        | Time        | Treating Pressure | Density | CMT RATE | CMT VOL | NRD RATE     | NRD VOLUME TOTAL | 0                           | Message                     |            |
|             | 24 hr clock | psi               | lb/gal  | bbl/min  | bbl     | bbl/min      | bbl              | 0                           |                             |            |
| 2007-Feb-11 | 20:01       | 9                 | 8.31    | 0.0      | 0.1     | 0.0          | 2.2              | 0                           |                             |            |
| 2007-Feb-11 | 20:01       | 142               | 5.94    | 4.2      | 1.3     | 4.0          | 2.8              | 0                           |                             |            |
| 2007-Feb-11 | 20:02       | 32                | 8.28    | 2.8      | 3.4     | 0.0          | 3.4              | 0                           |                             |            |
| 2007-Feb-11 | 20:02       | 50                | 8.30    | 2.8      | 4.8     | 2.8          | 4.1              | 0                           |                             |            |
| 2007-Feb-11 | 20:03       | 174               | 8.27    | 2.2      | 6.1     | 5.5          | 6.2              | 0                           |                             |            |
| 2007-Feb-11 | 20:03       | 174               | 8.29    | 3.0      | 7.2     | 5.5          | 8.7              | 0                           |                             |            |
| 2007-Feb-11 | 20:03       |                   |         |          |         |              |                  |                             | End Spacer                  |            |
| 2007-Feb-11 | 20:03       | 174               | 8.33    | 3.0      | 7.4     | 5.5          | 8.9              | 0                           |                             |            |
| 2007-Feb-11 | 20:03       |                   |         |          |         |              |                  |                             | Start Mixing Lead Slurry    |            |
| 2007-Feb-11 | 20:03       | 179               | 9.02    | 2.4      | 7.9     | 5.5          | 9.9              | 0                           |                             |            |
| 2007-Feb-11 | 20:03       |                   |         |          |         |              |                  |                             | Reset Total, Vol = 7.90 bbl |            |
| 2007-Feb-11 | 20:04       | 197               | 10.14   | 3.4      | 1.1     | 5.5          | 1.8              | 0                           |                             |            |
| 2007-Feb-11 | 20:04       | 206               | 11.18   | 3.4      | 2.7     | 5.2          | 4.5              | 0                           |                             |            |
| 2007-Feb-11 | 20:05       | 192               | 11.71   | 4.8      | 4.5     | 5.0          | 7.1              | 0                           |                             |            |
| 2007-Feb-11 | 20:05       | 188               | 11.65   | 4.9      | 6.9     | 5.5          | 9.8              | 0                           |                             |            |
| 2007-Feb-11 | 20:06       | 192               | 12.08   | 4.5      | 9.2     | 4.8          | 12.0             | 0                           |                             |            |
| 2007-Feb-11 | 20:06       | 192               | 13.65   | 4.8      | 11.6    | 3.8          | 14.5             | 0                           |                             |            |
| 2007-Feb-11 | 20:07       | 183               | 11.82   | 4.5      | 13.9    | 4.9          | 16.8             | 0                           |                             |            |
| 2007-Feb-11 | 20:07       | 188               | 11.70   | 4.0      | 16.3    | 5.1          | 19.3             | 0                           |                             |            |
| 2007-Feb-11 | 20:08       | 192               | 11.81   | 3.5      | 18.3    | 5.2          | 21.9             | 0                           |                             |            |
| 2007-Feb-11 | 20:08       | 188               | 11.85   | 4.1      | 20.4    | 5.3          | 24.6             | 0                           |                             |            |
| 2007-Feb-11 | 20:09       | 188               | 11.95   | 4.5      | 22.5    | 5.3          | 27.3             | 0                           |                             |            |
| 2007-Feb-11 | 20:09       | 188               | 12.07   | 4.4      | 24.7    | 5.2          | 29.9             | 0                           |                             |            |
| 2007-Feb-11 | 20:10       | 197               | 12.67   | 4.5      | 26.8    | 5.4          | 32.6             | 0                           |                             |            |
| 2007-Feb-11 | 20:10       | 215               | 12.32   | 4.3      | 29.0    | 5.2          | 35.3             | 0                           |                             |            |
| 2007-Feb-11 | 20:11       | 151               | 11.66   | 4.7      | 31.3    | 4.7          | 37.7             | 0                           |                             |            |
| 2007-Feb-11 | 20:11       | 146               | 11.47   | 4.8      | 33.7    | 4.8          | 40.1             | 0                           |                             |            |
| 2007-Feb-11 | 20:12       | 142               | 11.77   | 4.7      | 36.1    | 4.5          | 42.5             | 0                           |                             |            |
| 2007-Feb-11 | 20:12       | 197               | 12.77   | 5.0      | 38.5    | 5.3          | 45.0             | 0                           |                             |            |
| 2007-Feb-11 | 20:13       | 201               | 12.78   | 5.2      | 41.0    | 5.4          | 47.6             | 0                           |                             |            |
| 2007-Feb-11 | 20:13       | 188               | 12.18   | 5.2      | 43.5    | 5.3          | 50.3             | 0                           |                             |            |
| 2007-Feb-11 | 20:14       | 142               | 11.93   | 4.7      | 46.0    | 4.7          | 52.7             | 0                           |                             |            |
| 2007-Feb-11 | 20:14       | 156               | 11.76   | 5.1      | 48.4    | 4.8          | 55.1             | 0                           |                             |            |
| 2007-Feb-11 | 20:15       | 169               | 11.59   | 5.1      | 51.0    | 5.4          | 57.7             | 0                           |                             |            |
| 2007-Feb-11 | 20:15       | 165               | 11.50   | 5.3      | 53.6    | 5.4          | 60.4             | 0                           |                             |            |
| 2007-Feb-11 | 20:16       | 160               | 11.47   | 5.4      | 56.2    | 5.4          | 63.1             | 0                           |                             |            |
| 2007-Feb-11 | 20:16       | 160               | 11.56   | 5.3      | 58.9    | 5.4          | 65.8             | 0                           |                             |            |
| 2007-Feb-11 | 20:17       | 156               | 11.51   | 5.0      | 61.5    | 5.5          | 68.5             | 0                           |                             |            |
| 2007-Feb-11 | 20:17       | 156               | 11.40   | 5.5      | 64.2    | 5.5          | 71.2             | 0                           |                             |            |
| 2007-Feb-11 | 20:18       | 151               | 11.27   | 5.5      | 66.9    | 5.4          | 73.9             | 0                           |                             |            |
| 2007-Feb-11 | 20:18       | 169               | 12.24   | 5.4      | 69.6    | 5.3          | 76.5             | 0                           |                             |            |
| 2007-Feb-11 | 20:19       | 169               | 11.90   | 5.2      | 72.2    | 5.3          | 79.2             | 0                           |                             |            |
| 2007-Feb-11 | 20:19       | 160               | 11.34   | 5.5      | 75.0    | 5.4          | 81.8             | 0                           |                             |            |
| 2007-Feb-11 | 20:20       | 156               | 11.61   | 5.5      | 77.7    | 5.3          | 84.5             | 0                           |                             |            |
| 2007-Feb-11 | 20:20       | 165               | 11.69   | 5.5      | 80.4    | 5.3          | 87.1             | 0                           |                             |            |
| 2007-Feb-11 | 20:21       | 156               | 11.41   | 5.4      | 83.1    | 5.4          | 89.8             | 0                           |                             |            |
| 2007-Feb-11 | 20:21       | 156               | 11.17   | 5.5      | 85.9    | 5.4          | 92.4             | 0                           |                             |            |
| 2007-Feb-11 | 20:22       | 169               | 12.09   | 5.4      | 88.6    | 5.5          | 95.1             | 0                           |                             |            |
| 2007-Feb-11 | 20:22       | 169               | 12.11   | 5.4      | 91.3    | 5.4          | 97.9             | 0                           |                             |            |
| 2007-Feb-11 | 20:23       | 165               | 12.06   | 5.5      | 94.1    | 5.3          | 100.6            | 0                           |                             |            |
| 2007-Feb-11 | 20:23       | 160               | 11.99   | 5.5      | 96.8    | 5.2          | 103.2            | 0                           |                             |            |
| 2007-Feb-11 | 20:24       | 160               | 11.92   | 5.5      | 99.5    | 5.3          | 105.8            | 0                           |                             |            |
| 2007-Feb-11 | 20:24       | 160               | 11.89   | 5.5      | 102.3   | 5.3          | 108.5            | 0                           |                             |            |
| 2007-Feb-11 | 20:25       | 165               | 11.82   | 5.5      | 105.0   | 5.4          | 111.1            | 0                           |                             |            |

KCC  
MAY 01 2007  
CONFIDENTIAL

RECEIVED  
KANSAS CORPORATION COMMISSION

MAY 03 2007

CONSERVATION DIVISION  
Page 2 of 5  
WICHITA, KS

| Well        |             |                   | Field   |          |         | Service Date |                  | Customer                    |                               | Job Number |
|-------------|-------------|-------------------|---------|----------|---------|--------------|------------------|-----------------------------|-------------------------------|------------|
| BRUISE #1   |             |                   |         |          |         | 0742-Feb-11  |                  | OXY RESOURCE CALIFORNIA LLC |                               | 2205553140 |
| Date        | Time        | Treating Pressure | Density | CMT RATE | CMT VOL | NRD RATE     | NRD VOLUME TOTAL | 0                           | Message                       |            |
|             | 24 hr clock | psi               | lb/gal  | bbl/min  | bbl     | bbl/min      | bbl              | 0                           |                               |            |
| 2007-Feb-11 | 20:25       | 160               | 11.59   | 5.5      | 107.8   | 5.4          | 113.8            | 0                           |                               |            |
| 2007-Feb-11 | 20:26       | 165               | 12.08   | 5.5      | 110.5   | 5.3          | 116.5            | 0                           |                               |            |
| 2007-Feb-11 | 20:26       | 174               | 12.49   | 5.5      | 113.3   | 5.3          | 119.2            | 0                           |                               |            |
| 2007-Feb-11 | 20:27       | 179               | 12.47   | 5.5      | 116.0   | 5.3          | 121.8            | 0                           |                               |            |
| 2007-Feb-11 | 20:27       | 174               | 12.34   | 5.5      | 118.8   | 5.3          | 124.5            | 0                           |                               |            |
| 2007-Feb-11 | 20:28       | 174               | 12.27   | 5.5      | 121.5   | 5.3          | 127.1            | 0                           |                               |            |
| 2007-Feb-11 | 20:28       | 169               | 12.21   | 5.5      | 124.2   | 5.3          | 129.8            | 0                           |                               |            |
| 2007-Feb-11 | 20:29       | 165               | 12.03   | 5.5      | 127.0   | 5.3          | 132.4            | 0                           |                               |            |
| 2007-Feb-11 | 20:29       | 160               | 11.85   | 5.5      | 129.7   | 5.4          | 135.1            | 0                           |                               |            |
| 2007-Feb-11 | 20:30       | 156               | 11.73   | 5.5      | 132.5   | 5.4          | 137.8            | 0                           |                               |            |
| 2007-Feb-11 | 20:30       | 119               | 11.19   | 4.6      | 134.9   | 4.6          | 140.2            | 0                           |                               |            |
| 2007-Feb-11 | 20:31       | 151               | 13.40   | 4.6      | 137.1   | 4.5          | 142.4            | 0                           |                               |            |
| 2007-Feb-11 | 20:31       | 201               | 12.85   | 5.5      | 139.8   | 5.4          | 145.0            | 0                           |                               |            |
| 2007-Feb-11 | 20:32       | 156               | 11.89   | 5.5      | 142.5   | 5.4          | 147.7            | 0                           |                               |            |
| 2007-Feb-11 | 20:32       | 119               | 11.46   | 4.7      | 145.0   | 4.3          | 150.1            | 0                           |                               |            |
| 2007-Feb-11 | 20:33       | 146               | 11.78   | 5.2      | 147.5   | 5.1          | 152.5            | 0                           |                               |            |
| 2007-Feb-11 | 20:33       | 160               | 11.83   | 5.5      | 150.2   | 5.4          | 155.1            | 0                           |                               |            |
| 2007-Feb-11 | 20:34       | 165               | 12.25   | 5.5      | 152.9   | 5.3          | 157.9            | 0                           |                               |            |
| 2007-Feb-11 | 20:34       | 174               | 12.41   | 5.5      | 155.6   | 5.3          | 160.5            | 0                           |                               |            |
| 2007-Feb-11 | 20:35       | 174               | 12.40   | 5.5      | 158.4   | 5.3          | 163.2            | 0                           |                               |            |
| 2007-Feb-11 | 20:35       | 169               | 12.34   | 5.5      | 161.1   | 5.2          | 165.9            | 0                           |                               |            |
| 2007-Feb-11 | 20:36       | 169               | 12.25   | 5.5      | 163.9   | 5.4          | 168.6            | 0                           |                               |            |
| 2007-Feb-11 | 20:36       | 165               | 12.17   | 5.5      | 166.6   | 5.3          | 171.2            | 0                           |                               |            |
| 2007-Feb-11 | 20:37       | 169               | 12.21   | 5.5      | 169.4   | 5.3          | 173.9            | 0                           |                               |            |
| 2007-Feb-11 | 20:37       | 169               | 12.27   | 5.5      | 172.1   | 5.5          | 176.5            | 0                           |                               |            |
| 2007-Feb-11 | 20:38       | 169               | 12.25   | 5.5      | 174.9   | 5.4          | 179.2            | 0                           |                               |            |
| 2007-Feb-11 | 20:38       | 142               | 12.19   | 4.9      | 177.5   | 4.7          | 181.8            | 0                           |                               |            |
| 2007-Feb-11 | 20:39       | 142               | 12.17   | 4.9      | 179.9   | 4.8          | 184.1            | 0                           |                               |            |
| 2007-Feb-11 | 20:39       | 137               | 12.16   | 4.9      | 182.3   | 4.8          | 186.6            | 0                           |                               |            |
| 2007-Feb-11 | 20:40       | 156               | 12.83   | 4.9      | 184.8   | 4.7          | 188.9            | 0                           |                               |            |
| 2007-Feb-11 | 20:40       | 151               | 12.28   | 4.9      | 187.2   | 4.8          | 191.3            | 0                           |                               |            |
| 2007-Feb-11 | 20:41       | 165               | 11.92   | 5.5      | 189.9   | 5.4          | 193.9            | 0                           |                               |            |
| 2007-Feb-11 | 20:41       | 165               | 12.13   | 5.5      | 192.6   | 5.3          | 196.6            | 0                           |                               |            |
| 2007-Feb-11 | 20:42       | 169               | 12.28   | 5.5      | 195.4   | 5.3          | 199.3            | 0                           |                               |            |
| 2007-Feb-11 | 20:42       | 174               | 12.30   | 5.5      | 198.1   | 5.2          | 201.9            | 0                           |                               |            |
| 2007-Feb-11 | 20:43       | 169               | 12.33   | 5.5      | 200.9   | 5.3          | 204.6            | 0                           |                               |            |
| 2007-Feb-11 | 20:43       | 169               | 12.40   | 5.5      | 203.6   | 5.2          | 207.3            | 0                           |                               |            |
| 2007-Feb-11 | 20:44       | 156               | 12.37   | 5.2      | 206.2   | 5.1          | 209.8            | 0                           |                               |            |
| 2007-Feb-11 | 20:44       | 160               | 12.52   | 5.2      | 208.8   | 5.1          | 212.3            | 0                           |                               |            |
| 2007-Feb-11 | 20:44       |                   |         |          |         |              |                  |                             | End Lead Slurry               |            |
| 2007-Feb-11 | 20:44       | 142               | 12.46   | 4.8      | 210.3   | 4.7          | 213.8            | 0                           |                               |            |
| 2007-Feb-11 | 20:44       | 142               | 12.43   | 4.8      | 210.4   | 4.7          | 213.9            | 0                           |                               |            |
| 2007-Feb-11 | 20:44       |                   |         |          |         |              |                  |                             | Start Mixing Tail Slurry      |            |
| 2007-Feb-11 | 20:44       | 142               | 12.47   | 4.8      | 210.8   | 4.7          | 214.3            | 0                           |                               |            |
| 2007-Feb-11 | 20:44       |                   |         |          |         |              |                  |                             | Reset Total, Vol = 210.78 bbl |            |
| 2007-Feb-11 | 20:45       | 142               | 12.59   | 4.8      | 0.5     | 4.7          | 0.5              | 0                           |                               |            |
| 2007-Feb-11 | 20:45       | 165               | 12.98   | 5.1      | 3.0     | 5.0          | 2.9              | 0                           |                               |            |
| 2007-Feb-11 | 20:46       | 128               | 13.20   | 4.6      | 5.4     | 4.6          | 5.3              | 0                           |                               |            |
| 2007-Feb-11 | 20:46       | 128               | 13.62   | 4.0      | 7.3     | 3.9          | 7.1              | 0                           |                               |            |
| 2007-Feb-11 | 20:47       | 229               | 14.69   | 5.5      | 9.9     | 5.3          | 9.6              | 0                           |                               |            |
| 2007-Feb-11 | 20:47       | 247               | 14.98   | 5.5      | 12.6    | 5.3          | 12.3             | 0                           |                               |            |
| 2007-Feb-11 | 20:48       | 211               | 14.93   | 4.8      | 15.1    | 4.7          | 14.7             | 0                           |                               |            |
| 2007-Feb-11 | 20:48       | 188               | 14.64   | 4.7      | 17.4    | 4.6          | 17.0             | 0                           |                               |            |
| 2007-Feb-11 | 20:49       | 179               | 14.56   | 4.7      | 19.8    | 4.6          | 19.2             | 0                           |                               |            |

KCC  
MAY 01 2007  
CONFIDENTIAL

RECEIVED  
KANSAS CORPORATION COMMISSION

MAY 03 2007

| Well        |             |                   | Field   |          | Service Date |          | Customer                    |   | Job Number                   |
|-------------|-------------|-------------------|---------|----------|--------------|----------|-----------------------------|---|------------------------------|
| BRUISE #1   |             |                   |         |          | 0742-Feb-11  |          | OXY RESOURCE CALIFORNIA LLC |   | 2205553140                   |
| Date        | Time        | Treating Pressure | Density | CMT RATE | CMT VOL      | NRD RATE | NRD VOLUME TOTAL            | 0 | Message                      |
|             | 24 hr clock | psi               | lb/gal  | bbl/min  | bbl          | bbl/min  | bbl                         | 0 |                              |
| 2007-Feb-11 | 20:49       | 174               | 14.72   | 4.6      | 22.1         | 4.6      | 21.5                        | 0 |                              |
| 2007-Feb-11 | 20:50       | 146               | 14.71   | 4.3      | 24.3         | 4.3      | 23.7                        | 0 |                              |
| 2007-Feb-11 | 20:50       | 165               | 14.54   | 4.3      | 26.5         | 4.3      | 25.8                        | 0 |                              |
| 2007-Feb-11 | 20:51       | 160               | 14.55   | 4.4      | 28.6         | 4.3      | 27.9                        | 0 |                              |
| 2007-Feb-11 | 20:51       | 179               | 15.07   | 4.4      | 30.8         | 4.3      | 30.1                        | 0 |                              |
| 2007-Feb-11 | 20:52       | 247               | 14.97   | 5.5      | 33.2         | 5.4      | 32.4                        | 0 |                              |
| 2007-Feb-11 | 20:52       | 197               | 14.65   | 5.0      | 35.8         | 4.8      | 35.0                        | 0 |                              |
| 2007-Feb-11 | 20:53       | 206               | 14.91   | 5.0      | 38.3         | 4.9      | 37.4                        | 0 |                              |
| 2007-Feb-11 | 20:53       | 215               | 15.04   | 5.0      | 40.8         | 4.9      | 39.8                        | 0 |                              |
| 2007-Feb-11 | 20:54       | 215               | 15.12   | 5.0      | 43.3         | 4.9      | 42.3                        | 0 |                              |
| 2007-Feb-11 | 20:54       | 256               | 15.22   | 5.5      | 45.9         | 5.3      | 44.8                        | 0 |                              |
| 2007-Feb-11 | 20:55       | 133               | 15.52   | 3.4      | 48.0         | 3.4      | 47.0                        | 0 |                              |
| 2007-Feb-11 | 20:55       | 18                | 7.79    | 0.0      | 48.8         | 1.2      | 47.9                        | 0 |                              |
| 2007-Feb-11 | 20:55       |                   |         |          |              |          |                             |   | End Tail Slurry              |
| 2007-Feb-11 | 20:55       |                   |         |          |              |          |                             |   | Drop Top Plug                |
| 2007-Feb-11 | 20:55       | 18                | 7.09    | 0.0      | 48.8         | 1.2      | 47.9                        | 0 |                              |
| 2007-Feb-11 | 20:55       |                   |         |          |              |          |                             |   | Start Displacement           |
| 2007-Feb-11 | 20:55       | 18                | 5.93    | 0.0      | 48.8         | 1.3      | 47.9                        | 0 |                              |
| 2007-Feb-11 | 20:55       |                   |         |          |              |          |                             |   | Reset Total, Vol = 48.84 bbl |
| 2007-Feb-11 | 20:55       | 18                | 1.66    | 0.0      | 48.8         | 4.8      | 48.3                        | 0 |                              |
| 2007-Feb-11 | 20:55       | 18                | 2.03    | 0.0      | 0.0          | 6.7      | 0.1                         | 0 |                              |
| 2007-Feb-11 | 20:56       | 14                | 0.78    | 0.0      | 0.0          | 3.5      | 2.0                         | 0 |                              |
| 2007-Feb-11 | 20:56       | 14                | 0.62    | 0.0      | 0.0          | 3.9      | 4.0                         | 0 |                              |
| 2007-Feb-11 | 20:57       | 14                | 0.59    | 0.0      | 0.0          | 4.3      | 6.0                         | 0 |                              |
| 2007-Feb-11 | 20:57       | 14                | 0.59    | 0.0      | 0.0          | 4.6      | 8.1                         | 0 |                              |
| 2007-Feb-11 | 20:58       | 14                | 0.62    | 0.0      | 0.0          | 4.7      | 10.4                        | 0 |                              |
| 2007-Feb-11 | 20:58       | 128               | 11.54   | 5.3      | 0.7          | 4.5      | 12.4                        | 0 |                              |
| 2007-Feb-11 | 20:59       | 174               | 9.25    | 6.6      | 3.8          | 6.6      | 15.3                        | 0 |                              |
| 2007-Feb-11 | 20:59       | 137               | 8.55    | 6.6      | 7.1          | 6.7      | 18.6                        | 0 |                              |
| 2007-Feb-11 | 21:00       | 128               | 8.32    | 6.6      | 10.4         | 6.7      | 22.0                        | 0 |                              |
| 2007-Feb-11 | 21:00       | 124               | 8.25    | 6.6      | 13.7         | 6.7      | 25.3                        | 0 |                              |
| 2007-Feb-11 | 21:01       | 124               | 8.25    | 6.6      | 17.0         | 6.6      | 28.7                        | 0 |                              |
| 2007-Feb-11 | 21:01       | 124               | 8.24    | 6.6      | 20.4         | 6.6      | 32.0                        | 0 |                              |
| 2007-Feb-11 | 21:02       | 128               | 8.30    | 6.6      | 23.7         | 6.7      | 35.3                        | 0 |                              |
| 2007-Feb-11 | 21:02       | 128               | 8.30    | 6.6      | 27.0         | 2.8      | 37.7                        | 0 |                              |
| 2007-Feb-11 | 21:03       | 101               | 8.30    | 6.6      | 30.3         | 2.8      | 39.1                        | 0 |                              |
| 2007-Feb-11 | 21:03       | 133               | 8.29    | 6.6      | 33.6         | 4.0      | 41.1                        | 0 |                              |
| 2007-Feb-11 | 21:04       | 151               | 8.30    | 6.6      | 36.9         | 2.7      | 43.2                        | 0 |                              |
| 2007-Feb-11 | 21:04       | 165               | 8.30    | 6.6      | 40.2         | 2.8      | 44.5                        | 0 |                              |
| 2007-Feb-11 | 21:05       | 174               | 8.30    | 6.6      | 43.6         | 6.8      | 46.9                        | 0 |                              |
| 2007-Feb-11 | 21:05       | 201               | 8.31    | 6.7      | 46.9         | 6.8      | 50.3                        | 0 |                              |
| 2007-Feb-11 | 21:06       | 220               | 8.31    | 6.6      | 50.2         | 6.7      | 53.6                        | 0 |                              |
| 2007-Feb-11 | 21:06       | 224               | 8.31    | 6.6      | 53.5         | 4.0      | 56.6                        | 0 |                              |
| 2007-Feb-11 | 21:07       | 243               | 8.30    | 6.6      | 56.8         | 6.7      | 59.1                        | 0 |                              |
| 2007-Feb-11 | 21:07       | 266               | 8.30    | 6.6      | 60.1         | 6.7      | 62.4                        | 0 |                              |
| 2007-Feb-11 | 21:08       | 211               | 8.30    | 5.1      | 63.3         | 5.3      | 65.7                        | 0 |                              |
| 2007-Feb-11 | 21:08       | 252               | 8.30    | 5.2      | 65.9         | 5.2      | 68.3                        | 0 |                              |
| 2007-Feb-11 | 21:09       | 261               | 8.30    | 5.2      | 68.5         | 5.2      | 71.0                        | 0 |                              |
| 2007-Feb-11 | 21:09       | 252               | 8.30    | 5.2      | 71.1         | 5.2      | 73.6                        | 0 |                              |
| 2007-Feb-11 | 21:10       | 298               | 8.31    | 5.2      | 73.7         | 5.2      | 76.2                        | 0 |                              |
| 2007-Feb-11 | 21:10       | 334               | 8.30    | 5.2      | 76.3         | 5.2      | 78.8                        | 0 |                              |
| 2007-Feb-11 | 21:11       | 343               | 8.30    | 5.2      | 78.9         | 5.2      | 81.4                        | 0 |                              |
| 2007-Feb-11 | 21:11       | 339               | 8.30    | 5.2      | 81.5         | 5.2      | 84.0                        | 0 |                              |
| 2007-Feb-11 | 21:12       | 348               | 8.31    | 5.2      | 84.1         | 5.2      | 86.7                        | 0 |                              |

| Well<br>BRUISE #1                     |                        |                             | Field                   |                                                                   | Service Date<br>0742-Feb-11 |                                           | Customer<br>OXY RESOURCE CALIFORNIA LLC |                                                   | Job Number<br>2205553140 |  |
|---------------------------------------|------------------------|-----------------------------|-------------------------|-------------------------------------------------------------------|-----------------------------|-------------------------------------------|-----------------------------------------|---------------------------------------------------|--------------------------|--|
| Date                                  | Time<br>24 hr<br>clock | Treating<br>Pressure<br>psi | Density<br>lb/gal       | CMT RATE<br>bbl/min                                               | CMT VOL<br>bbl              | NRD RATE<br>bbl/min                       | NRD<br>VOLUME<br>TOTAL<br>bbl           | 0                                                 | Message                  |  |
| 2007-Feb-11                           | 21:12                  | 362                         | 8.31                    | 3.8                                                               | 86.6                        | 4.5                                       | 89.2                                    | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:13                  | 403                         | 8.31                    | 4.2                                                               | 88.7                        | 4.3                                       | 91.3                                    | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:13                  | 371                         | 8.31                    | 4.2                                                               | 90.8                        | 4.2                                       | 93.4                                    | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:14                  | 375                         | 8.30                    | 4.2                                                               | 92.9                        | 4.2                                       | 95.5                                    | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:14                  | 398                         | 8.30                    | 4.2                                                               | 95.0                        | 4.2                                       | 97.7                                    | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:15                  | 380                         | 8.30                    | 2.5                                                               | 96.3                        | 2.5                                       | 99.0                                    | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:15                  | 375                         | 8.30                    | 2.5                                                               | 97.6                        | 2.5                                       | 100.3                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:16                  | 417                         | 8.30                    | 2.5                                                               | 98.8                        | 2.5                                       | 101.5                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:16                  | 462                         | 8.30                    | 2.5                                                               | 100.1                       | 2.5                                       | 102.8                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:17                  | 407                         | 8.30                    | 2.4                                                               | 101.3                       | 2.5                                       | 104.0                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:17                  | 467                         | 8.30                    | 2.4                                                               | 102.5                       | 2.5                                       | 105.3                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:18                  | 458                         | 8.31                    | 2.4                                                               | 103.7                       | 2.5                                       | 106.5                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:18                  | 490                         | 8.30                    | 2.4                                                               | 104.9                       | 2.4                                       | 107.7                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:19                  | 499                         | 8.31                    | 2.4                                                               | 106.1                       | 2.4                                       | 108.9                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:19                  | 476                         | 8.30                    | 2.4                                                               | 107.3                       | 2.4                                       | 110.1                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:20                  | 1085                        | 8.25                    | 0.0                                                               | 107.9                       | 0.0                                       | 110.9                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:20                  | 1080                        | 8.28                    | 0.0                                                               | 107.9                       | 0.0                                       | 110.9                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:21                  | 1080                        | 8.28                    | 0.0                                                               | 107.9                       | 0.0                                       | 110.9                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:21                  | 1080                        | 8.28                    | 0.0                                                               | 107.9                       | 0.0                                       | 110.9                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:22                  | 430                         | 8.28                    | 0.0                                                               | 107.9                       | 0.0                                       | 110.9                                   | 0                                                 |                          |  |
| 2007-Feb-11                           | 21:22                  | 18                          | 8.28                    | 0.0                                                               | 107.9                       | 0.0                                       | 110.9                                   | 0                                                 |                          |  |
| <b>Post Job Summary</b>               |                        |                             |                         |                                                                   |                             |                                           |                                         |                                                   |                          |  |
| Average Pump Rates, bpm               |                        |                             |                         | Volume of Fluid Injected, bbl                                     |                             |                                           |                                         |                                                   |                          |  |
| Slurry                                | N2                     | Mud                         | Maximum Rate            | Total Slurry                                                      | Mud                         | Spacer                                    | N2                                      |                                                   |                          |  |
| 5                                     |                        |                             | 6                       | 267                                                               |                             | 10                                        |                                         |                                                   |                          |  |
| Treating Pressure Summary, psi        |                        |                             |                         | Breakdown Fluid                                                   |                             |                                           |                                         |                                                   |                          |  |
| Maximum                               | Final                  | Average                     | Bump Plug to            | Breakdown                                                         | Volume                      |                                           |                                         | Density                                           |                          |  |
| 500                                   |                        | 250                         | 1080                    |                                                                   | bbl                         |                                           |                                         | 8.34 lb/gal                                       |                          |  |
| Avg. N2 Percent                       | Designed Slurry Volume | Displacement                | Mix Water Temp          | <input checked="" type="checkbox"/> Cement Circulated to Surface? |                             | Volume                                    |                                         | 5 bbl                                             |                          |  |
| %                                     | 273.6 bbl              | 105.18 bbl                  | °F                      | <input type="checkbox"/> Washed Thru Perfs                        |                             | To                                        |                                         | ft                                                |                          |  |
| Customer or Authorized Representative |                        |                             | Schlumberger Supervisor |                                                                   |                             |                                           |                                         |                                                   |                          |  |
| Willimon, Wes                         |                        |                             | Flanagan, Patrick       |                                                                   |                             | <input type="checkbox"/> Circulation Lost |                                         | <input checked="" type="checkbox"/> Job Completed |                          |  |

**KCC**  
MAY 01 2007  
CONFIDENTIAL


**RECEIVED**  
KANSAS CORPORATION COMMISSION

**MAY 03 2007**

CONSERVATION DIVISION  
WICHITA, KS

MAY 03 2007

|                 |                                      |                 |                             |
|-----------------|--------------------------------------|-----------------|-----------------------------|
| <b>Well</b>     | Bruis B-1                            | <b>Client</b>   | Oxy Resource California LLC |
| <b>Field</b>    |                                      | <b>SIR No.</b>  |                             |
| <b>Engineer</b> | CONSERVATION DIVISION<br>WICHITA, KS | <b>Job Type</b> | 8 5/8" surface              |
| <b>Country</b>  | United States                        | <b>Job Date</b> | 02-11-2007                  |

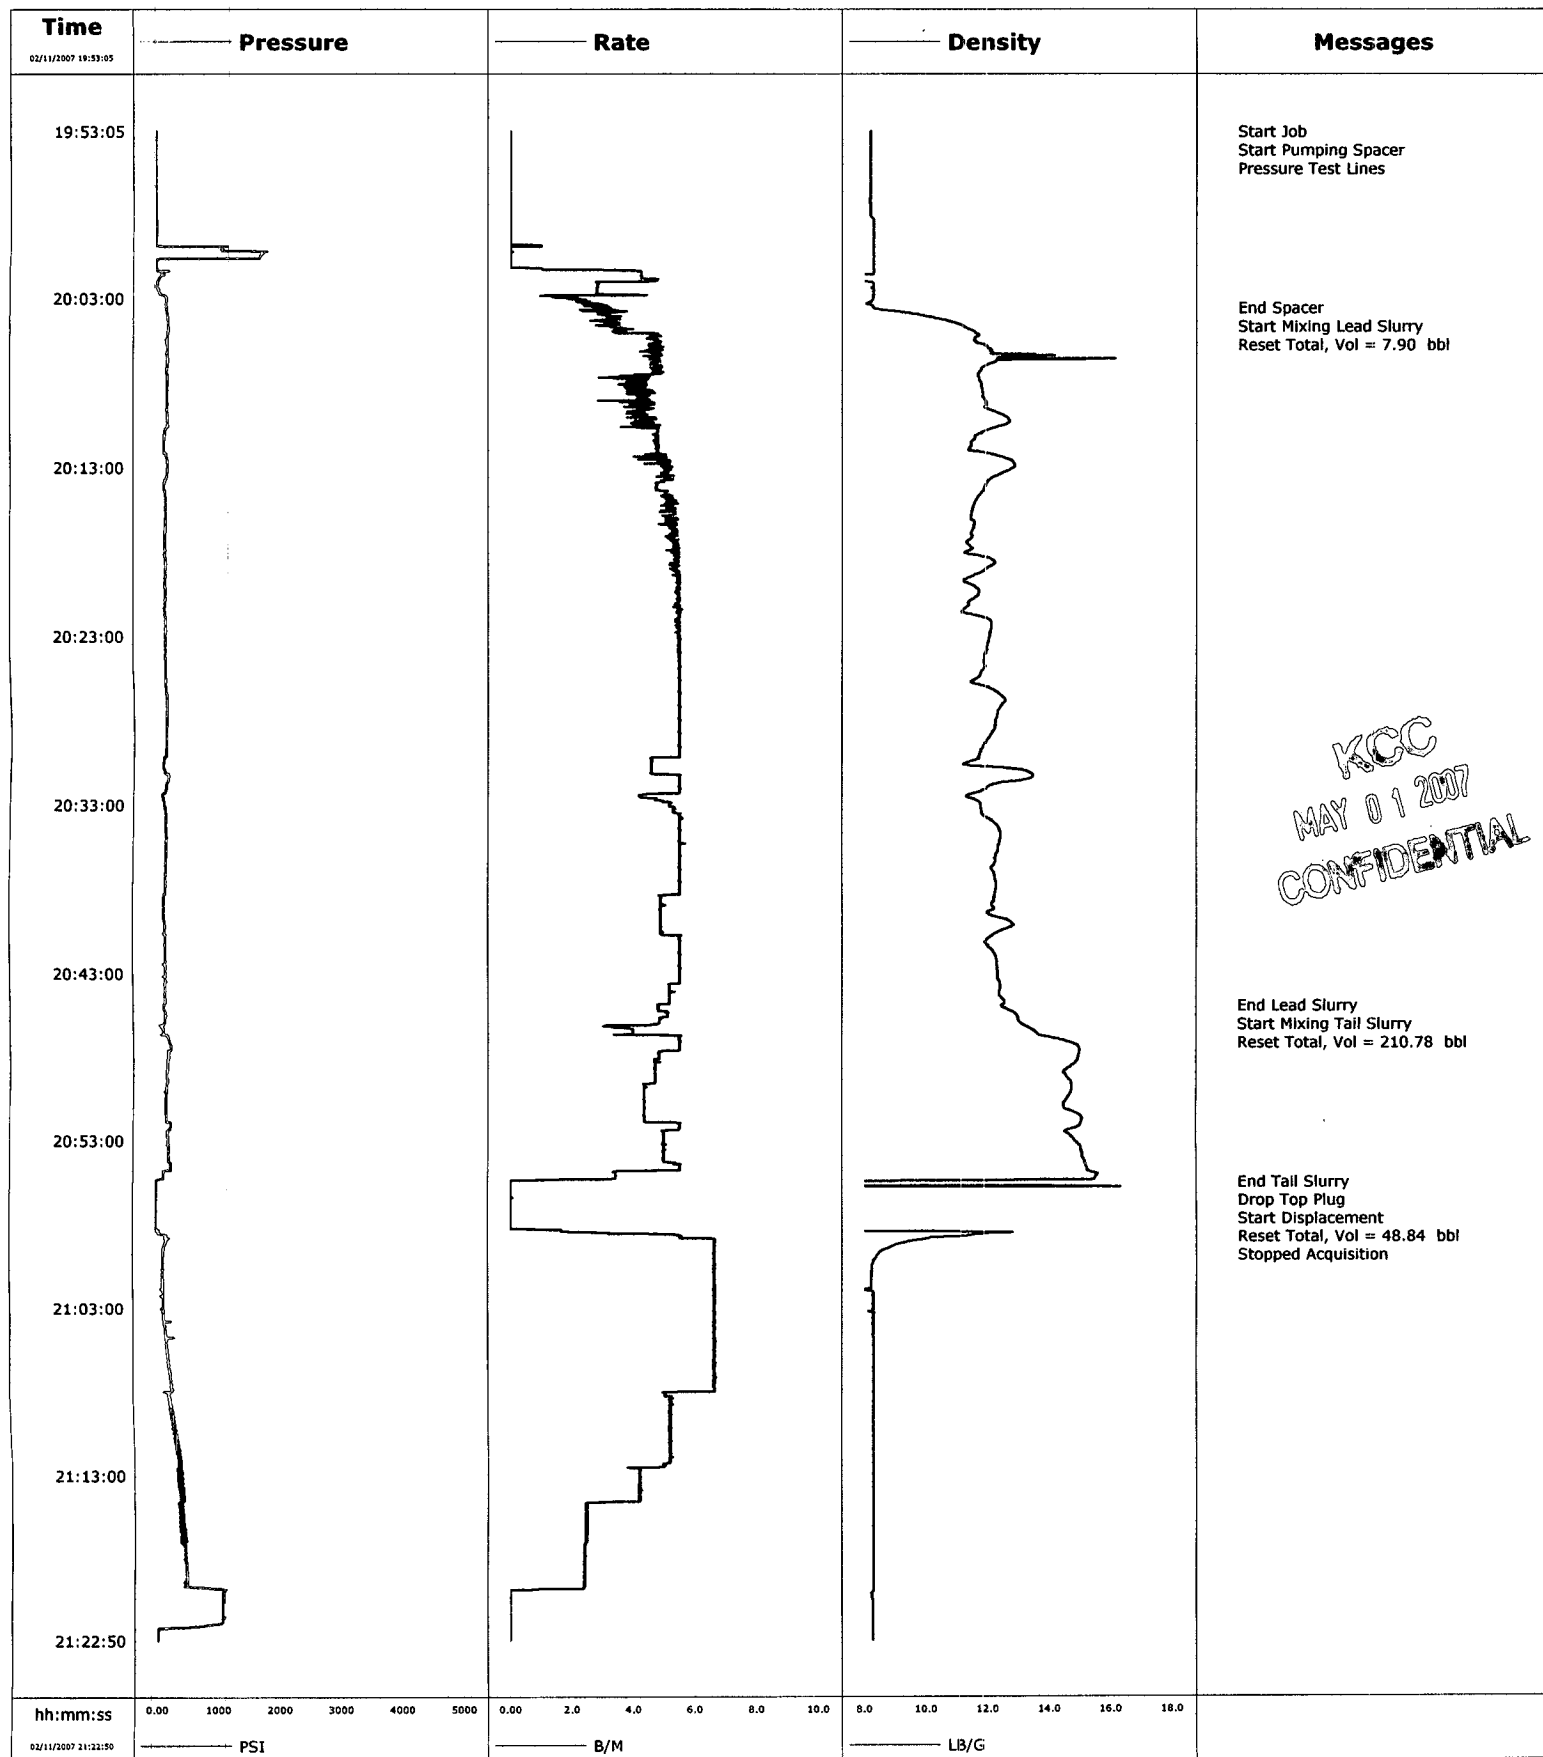



# Cementing Service Report

|                                                                                                                                                                                 |      |                                          |                   |                                       |                |                                                           |                     |                                                                                 |                      |                                            |  |                              |  |                      |  |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------|------------------------------------------|-------------------|---------------------------------------|----------------|-----------------------------------------------------------|---------------------|---------------------------------------------------------------------------------|----------------------|--------------------------------------------|--|------------------------------|--|----------------------|--|
| Customer<br>OXY RESOURCE CALIFORNIA LLC                                                                                                                                         |      |                                          |                   |                                       |                | Job Number<br>2205553097                                  |                     |                                                                                 |                      |                                            |  |                              |  |                      |  |
| Well<br>BRUNS B-1                                                                                                                                                               |      | Location (legal)<br>SEC 21-T34S-R33W     |                   | Schlumberger Location<br>Perryton, TX |                | Job Start<br>2007-Feb-23                                  |                     |                                                                                 |                      |                                            |  |                              |  |                      |  |
| Field<br>SALLEY                                                                                                                                                                 |      | Formation Name/Type                      |                   | Deviation<br>°                        |                | Bit Size<br>7.88 in                                       |                     | Well MD<br>6,595 ft                                                             |                      | Well TVD<br>6,595 ft                       |  |                              |  |                      |  |
| County<br>SEWARD                                                                                                                                                                |      | State/Province<br>KANSAS                 |                   | BHP<br>psi                            |                | BHST<br>138 °F                                            |                     | BHCT<br>°F                                                                      |                      | Pore Press. Gradient<br>psi/ft             |  |                              |  |                      |  |
| Well Master:<br>0630889305                                                                                                                                                      |      | API / UWI:<br>15175220810000             |                   | Casing/Liner                          |                |                                                           |                     |                                                                                 |                      |                                            |  |                              |  |                      |  |
| Rig Name<br>MURFIN 20                                                                                                                                                           |      | Drilled For<br>Oil & Gas                 |                   | Service Via                           |                | Depth, ft<br>6595                                         |                     | Size, in<br>5.5                                                                 |                      | Weight, lb/ft<br>17                        |  | Grade<br>N80                 |  | Thread<br>8RD        |  |
| Offshore Zone                                                                                                                                                                   |      | Well Class<br>New                        |                   | Well Type<br>Development              |                | Tubing/Drill Pipe                                         |                     |                                                                                 |                      |                                            |  |                              |  |                      |  |
| Drilling Fluid Type                                                                                                                                                             |      | Max. Density<br>lb/gal                   |                   | Plastic Viscosity<br>cp               |                | Depth, ft                                                 |                     | Size, in                                                                        |                      | Weight, lb/ft                              |  | Grade                        |  | Thread               |  |
| Service Line<br>Cementing                                                                                                                                                       |      | Job Type<br>Cem Surface Casing           |                   | Perforations/Open Hole                |                |                                                           |                     |                                                                                 |                      |                                            |  |                              |  |                      |  |
| Max. Allowed Tubing Pressure<br>psi                                                                                                                                             |      | Max. Allowed Ann. Pressure<br>psi        |                   | Wellhead Connection<br>5 1/2 HSM      |                | Top, ft                                                   |                     | Bottom, ft                                                                      |                      | spf                                        |  | No. of Shots                 |  | Total Interval<br>ft |  |
| Service Instructions<br>20 bbls CW100<br>215 sks 50/50 POZ/H+3%M117+2%D20+5ppsD42+5ppsD53+0.25%D46<br>+0.25%D65+0.25%D112 (25sks for rodent holes)<br>Displace with fresh water |      |                                          |                   |                                       |                | Treat Down<br>Casing                                      |                     | Displacement<br>105.18 bbl                                                      |                      | Packer Type                                |  | Packer Depth<br>ft           |  |                      |  |
|                                                                                                                                                                                 |      |                                          |                   |                                       |                | Tubing Vol.<br>bbl                                        |                     | Casing Vol.<br>107.95 bbl                                                       |                      | Annular Vol.<br>124.59 bbl                 |  | Open Hole Vol.<br>246.94 bbl |  |                      |  |
|                                                                                                                                                                                 |      |                                          |                   |                                       |                | Casing/Tubing Secured <input checked="" type="checkbox"/> |                     | 1 Hole Volume Circulated prior to Cementing <input checked="" type="checkbox"/> |                      | Casing Tools                               |  | Squeeze Job                  |  |                      |  |
|                                                                                                                                                                                 |      |                                          |                   |                                       |                | Lift Pressure:<br>580 psi                                 |                     | Pipe Rotated <input type="checkbox"/>                                           |                      | Pipe Reciprocated <input type="checkbox"/> |  | Shoe Type:                   |  | Squeeze Type         |  |
| No. Centralizers:                                                                                                                                                               |      | Top Plugs: 1                             |                   | Bottom Plugs: 0                       |                | Shoe Depth: 5818 ft                                       |                     | Tool Type:                                                                      |                      | Stage Tool Type                            |  | Tool Depth: ft               |  |                      |  |
| Cement Head Type: Single                                                                                                                                                        |      | Stage Tool Depth: ft                     |                   | Tail Pipe Size: in                    |                | Collar Type:                                              |                     | Tail Pipe Depth: ft                                                             |                      | Collar Depth: 5775 ft                      |  | Sqz Total Vol: bbl           |  |                      |  |
| Job Scheduled For:                                                                                                                                                              |      | Arrived on Location:<br>2007-Feb-23 7:30 |                   | Leave Location:<br>2007-Feb-23        |                | Collar Depth: 5775 ft                                     |                     | Sqz Total Vol: bbl                                                              |                      | Casing Tools                               |  | Squeeze Job                  |  |                      |  |
| Date                                                                                                                                                                            | Time | Treating Pressure<br>psi                 | Density<br>lb/gal | CMT RATE<br>bbl/min                   | CMT VOL<br>bbl | CS NRD RATE<br>bbl/min                                    | CS NRD TOTAL<br>bbl | 0                                                                               | Message              |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:31 | -5                                       | 8.35              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:31 | -5                                       | 8.35              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:31 |                                          |                   |                                       |                |                                                           |                     |                                                                                 | Start Job            |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:31 | -5                                       | 8.35              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                 | 0                                                                               | Start Pumping Spacer |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:31 | -5                                       | 8.35              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                 | 0                                                                               | Pressure Test Lines  |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:31 | -5                                       | 8.35              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:32 | -5                                       | 8.35              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:32 | -5                                       | 8.35              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:33 | -5                                       | 8.37              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:33 | -5                                       | 8.35              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:34 | -5                                       | 3.94              | 0.0                                   | 0.0            | 0.0                                                       | 0.0                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:34 | -5                                       | 8.35              | 0.0                                   | 0.0            | 0.1                                                       | 0.4                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:35 | 37                                       | 8.35              | 0.0                                   | 0.0            | 3.2                                                       | 0.4                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:35 | 41                                       | 8.34              | 0.0                                   | 0.0            | 0.0                                                       | 0.9                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:36 | 105                                      | 8.34              | 2.5                                   | 0.7            | 2.6                                                       | 1.5                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:36 | 9                                        | 8.34              | 0.0                                   | 1.4            | 0.0                                                       | 2.3                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:37 | 1616                                     | 8.34              | 0.0                                   | 1.4            | 0.1                                                       | 2.3                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:37 | 2046                                     | 8.34              | 0.0                                   | 1.4            | 0.0                                                       | 2.3                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:38 | 14                                       | 8.34              | 0.0                                   | 1.4            | 0.0                                                       | 2.3                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |
| 2007-Feb-23                                                                                                                                                                     | 9:38 | 220                                      | 8.35              | 2.4                                   | 1.6            | 2.5                                                       | 2.6                 | 0                                                                               |                      |                                            |  |                              |  |                      |  |

RECEIVED  
KANSAS CORPORATION COMMISSION

MAY 03 2007

CONSERVATION DIVISION

Wichita, KS

| Well        |             |                   | Field   |          |         | Service Date |              | Customer                    |                                  | Job Number |
|-------------|-------------|-------------------|---------|----------|---------|--------------|--------------|-----------------------------|----------------------------------|------------|
| BRUNS #B-1  |             |                   | SALLEY  |          |         | 0754-Feb-23  |              | OXY RESOURCE CALIFORNIA LLC |                                  | 2205553097 |
| Date        | Time        | Treating Pressure | Density | CMT RATE | CMT VOL | CS NRD RATE  | CS NRD TOTAL | 0                           | Message                          |            |
|             | 24 hr clock | psi               | lb/gal  | bbl/min  | bbl     | bbl/min      | bbl          | 0                           |                                  |            |
| 2007-Feb-23 | 9:39        | 105               | 8.34    | 2.4      | 2.8     | 2.5          | 3.8          | 0                           |                                  |            |
| 2007-Feb-23 | 9:39        | 69                | 8.34    | 1.6      | 3.7     | 1.6          | 4.8          | 0                           |                                  |            |
| 2007-Feb-23 | 9:40        | 128               | 8.34    | 3.0      | 5.1     | 3.1          | 6.2          | 0                           |                                  |            |
| 2007-Feb-23 | 9:40        | 142               | 8.34    | 3.0      | 6.6     | 3.1          | 7.8          | 0                           |                                  |            |
| 2007-Feb-23 | 9:41        | 124               | 8.34    | 3.0      | 8.1     | 3.1          | 9.3          | 0                           |                                  |            |
| 2007-Feb-23 | 9:41        | 142               | 8.34    | 3.0      | 9.6     | 3.1          | 10.9         | 0                           |                                  |            |
| 2007-Feb-23 | 9:42        | 124               | 8.34    | 3.0      | 11.2    | 3.1          | 12.5         | 0                           |                                  |            |
| 2007-Feb-23 | 9:42        | 146               | 8.34    | 3.1      | 12.7    | 3.2          | 14.0         | 0                           |                                  |            |
| 2007-Feb-23 | 9:43        | 128               | 8.34    | 3.0      | 14.2    | 3.1          | 15.6         | 0                           |                                  |            |
| 2007-Feb-23 | 9:43        | 146               | 8.34    | 3.0      | 15.7    | 3.1          | 17.1         | 0                           |                                  |            |
| 2007-Feb-23 | 9:44        | 0                 | 8.34    | 0.0      | 17.1    | 1.5          | 18.7         | 0                           |                                  |            |
| 2007-Feb-23 | 9:44        | 55                | 8.34    | 0.0      | 17.1    | 1.7          | 18.7         | 0                           |                                  |            |
| 2007-Feb-23 | 9:45        | 151               | 8.34    | 3.0      | 18.5    | 3.1          | 20.2         | 0                           |                                  |            |
| 2007-Feb-23 | 9:45        | 169               | 8.34    | 3.0      | 20.0    | 3.1          | 21.7         | 0                           |                                  |            |
| 2007-Feb-23 | 9:46        | 151               | 10.08   | 3.0      | 21.6    | 2.8          | 23.2         | 0                           |                                  |            |
| 2007-Feb-23 | 9:46        | 160               | 3.55    | 3.0      | 23.1    | 0.0          | 23.6         | 0                           |                                  |            |
| 2007-Feb-23 | 9:47        | 160               | 8.67    | 3.0      | 24.6    | 3.2          | 24.7         | 0                           |                                  |            |
| 2007-Feb-23 | 9:47        | 137               | 9.38    | 3.0      | 26.1    | 2.2          | 26.3         | 0                           |                                  |            |
| 2007-Feb-23 | 9:48        | 9                 | 3.03    | 0.0      | 26.3    | 0.0          | 26.6         | 0                           |                                  |            |
| 2007-Feb-23 | 9:48        | -5                | 8.90    | 0.0      | 26.3    | 0.0          | 26.6         | 0                           |                                  |            |
| 2007-Feb-23 | 9:49        | -5                | 8.73    | 0.0      | 26.3    | 0.0          | 26.6         | 0                           |                                  |            |
| 2007-Feb-23 | 9:49        | -5                | 8.71    | 0.0      | 26.3    | 0.0          | 26.6         | 0                           |                                  |            |
| 2007-Feb-23 | 9:50        | -5                | 8.72    | 0.0      | 26.3    | 0.0          | 26.6         | 0                           |                                  |            |
| 2007-Feb-23 | 9:50        | -5                | 10.31   | 0.0      | 26.3    | 4.6          | 27.6         | 0                           |                                  |            |
| 2007-Feb-23 | 9:51        | -5                | 12.53   | 0.0      | 26.3    | 3.6          | 29.6         | 0                           |                                  |            |
| 2007-Feb-23 | 9:51        | 41                | 13.14   | 0.0      | 26.3    | 0.0          | 30.6         | 0                           |                                  |            |
| 2007-Feb-23 | 9:52        | 64                | 14.01   | 0.0      | 26.3    | 2.5          | 31.4         | 0                           |                                  |            |
| 2007-Feb-23 | 9:52        | -9                | 14.08   | 0.0      | 26.3    | 0.0          | 32.0         | 0                           |                                  |            |
| 2007-Feb-23 | 9:53        | -9                | 14.07   | 0.0      | 26.3    | 0.0          | 32.0         | 0                           |                                  |            |
| 2007-Feb-23 | 9:53        | -5                | 13.98   | 0.0      | 26.3    | 5.1          | 34.3         | 0                           |                                  |            |
| 2007-Feb-23 | 9:54        | -9                | 13.98   | 0.0      | 26.3    | 5.1          | 36.9         | 0                           |                                  |            |
| 2007-Feb-23 | 9:54        | -5                | 14.00   | 0.0      | 26.3    | 5.0          | 39.4         | 0                           |                                  |            |
| 2007-Feb-23 | 9:55        | 73                | 13.98   | 0.0      | 26.3    | 3.4          | 41.9         | 0                           |                                  |            |
| 2007-Feb-23 | 9:55        | 69                | 13.95   | 0.0      | 26.3    | 2.3          | 43.1         | 0                           |                                  |            |
| 2007-Feb-23 | 9:56        | 92                | 13.89   | 0.0      | 26.3    | 2.8          | 44.4         | 0                           |                                  |            |
| 2007-Feb-23 | 9:56        | -14               | 13.62   | 0.0      | 26.3    | 1.7          | 45.7         | 0                           |                                  |            |
| 2007-Feb-23 | 9:57        | -5                | 13.46   | 0.0      | 26.3    | 0.0          | 45.8         | 0                           |                                  |            |
| 2007-Feb-23 | 9:57        | 32                | 11.57   | 0.0      | 26.3    | 0.0          | 45.8         | 0                           |                                  |            |
| 2007-Feb-23 | 9:58        | 60                | 9.91    | 0.0      | 26.3    | 0.0          | 45.8         | 0                           |                                  |            |
| 2007-Feb-23 | 9:58        | 201               | 11.29   | 3.0      | 27.5    | 2.5          | 46.6         | 0                           |                                  |            |
| 2007-Feb-23 | 9:59        | 275               | 12.81   | 4.4      | 29.2    | 4.1          | 48.0         | 0                           |                                  |            |
| 2007-Feb-23 | 9:59        | 325               | 13.90   | 5.5      | 31.8    | 5.3          | 50.5         | 0                           |                                  |            |
| 2007-Feb-23 | 10:00       | 316               | 14.01   | 5.6      | 34.6    | 5.4          | 53.2         | 0                           |                                  |            |
| 2007-Feb-23 | 10:00       | 293               | 14.48   | 5.6      | 37.4    | 5.4          | 55.8         | 0                           |                                  |            |
| 2007-Feb-23 | 10:01       | 270               | 14.49   | 5.6      | 40.1    | 5.4          | 58.5         | 0                           |                                  |            |
| 2007-Feb-23 | 10:01       | 211               | 13.65   | 5.6      | 43.0    | 5.5          | 61.3         | 0                           |                                  |            |
| 2007-Feb-23 | 10:02       | 183               | 13.38   | 5.6      | 44.9    | 5.4          | 63.1         | 0                           |                                  |            |
| 2007-Feb-23 | 10:02       |                   |         |          |         |              |              |                             | actual cement vol tail away 16.9 |            |
| 2007-Feb-23 | 10:02       | 137               | 13.53   | 5.6      | 45.8    | 5.4          | 63.9         | 0                           |                                  |            |
| 2007-Feb-23 | 10:02       | 169               | 13.81   | 5.6      | 18.5    | 5.5          | 19.5         | 0                           |                                  |            |
| 2007-Feb-23 | 10:03       | 174               | 13.78   | 5.6      | 21.3    | 5.5          | 22.2         | 0                           |                                  |            |
| 2007-Feb-23 | 10:03       | 174               | 13.76   | 5.7      | 24.1    | 5.5          | 25.0         | 0                           |                                  |            |
| 2007-Feb-23 | 10:04       | 160               | 13.59   | 5.7      | 27.0    | 5.5          | 27.7         | 0                           |                                  |            |

KGCC  
MAY 01 2007  
CONFIDENTIAL

RECEIVED  
KANSAS CORPORATION COMMISSION

MAY 03 2007

CONSERVATION DIVISION  
WICHITA, KS

| Well        |                        |                             | Field             |                     | Service Date   |                        | Customer                    |        | Job Number                   |
|-------------|------------------------|-----------------------------|-------------------|---------------------|----------------|------------------------|-----------------------------|--------|------------------------------|
| BRUNS #B-1  |                        |                             | SALLEY            |                     | 0754-Feb-23    |                        | OXY RESOURCE CALIFORNIA LLC |        | 2205553097                   |
| Date        | Time<br>24 hr<br>clock | Treating<br>Pressure<br>psi | Density<br>lb/gal | CMT RATE<br>bbl/min | CMT VOL<br>bbl | CS NRD RATE<br>bbl/min | CS NRD<br>TOTAL<br>bbl      | 0<br>0 | Message                      |
| 2007-Feb-23 | 10:04                  | 160                         | 13.78             | 5.7                 | 29.8           | 5.6                    | 30.5                        | 0      |                              |
| 2007-Feb-23 | 10:05                  | 179                         | 14.17             | 5.7                 | 32.7           | 5.6                    | 33.3                        | 0      |                              |
| 2007-Feb-23 | 10:05                  | 151                         | 14.20             | 5.3                 | 35.5           | 5.2                    | 36.0                        | 0      |                              |
| 2007-Feb-23 | 10:06                  | 160                         | 14.12             | 5.3                 | 38.1           | 5.2                    | 38.6                        | 0      |                              |
| 2007-Feb-23 | 10:06                  | 146                         | 13.90             | 5.3                 | 40.7           | 5.2                    | 41.2                        | 0      |                              |
| 2007-Feb-23 | 10:07                  | 133                         | 13.92             | 5.3                 | 43.4           | 5.2                    | 43.8                        | 0      |                              |
| 2007-Feb-23 | 10:07                  | 133                         | 13.51             | 5.3                 | 46.0           | 5.0                    | 46.3                        | 0      |                              |
| 2007-Feb-23 | 10:08                  | 82                          | 13.61             | 0.0                 | 47.8           | 3.7                    | 48.6                        | 0      |                              |
| 2007-Feb-23 | 10:08                  | -18                         | 13.21             | 0.0                 | 47.8           | 0.4                    | 50.5                        | 0      |                              |
| 2007-Feb-23 | 10:09                  | -18                         | 13.20             | 0.0                 | 47.8           | 0.0                    | 50.5                        | 0      |                              |
| 2007-Feb-23 | 10:09                  | -18                         | 11.18             | 0.0                 | 47.8           | 0.0                    | 50.7                        | 0      |                              |
| 2007-Feb-23 | 10:10                  | -18                         | 9.39              | 0.0                 | 47.8           | 5.2                    | 52.5                        | 0      |                              |
| 2007-Feb-23 | 10:10                  | -5                          | 9.33              | 0.0                 | 47.8           | 4.9                    | 55.0                        | 0      |                              |
| 2007-Feb-23 | 10:11                  | -5                          | 9.31              | 0.0                 | 47.8           | 5.1                    | 57.5                        | 0      |                              |
| 2007-Feb-23 | 10:11                  | -5                          | 9.28              | 0.0                 | 47.8           | 5.0                    | 60.1                        | 0      |                              |
| 2007-Feb-23 | 10:12                  | 32                          | 9.12              | 0.0                 | 47.8           | 7.5                    | 63.1                        | 0      |                              |
| 2007-Feb-23 | 10:12                  | 27                          | 9.05              | 0.0                 | 47.8           | 7.3                    | 66.8                        | 0      |                              |
| 2007-Feb-23 | 10:13                  | 27                          | 9.01              | 0.0                 | 47.8           | 7.0                    | 70.5                        | 0      |                              |
| 2007-Feb-23 | 10:13                  | 27                          | 8.98              | 0.0                 | 47.8           | 7.1                    | 74.1                        | 0      |                              |
| 2007-Feb-23 | 10:13                  | 37                          | 8.91              | 0.0                 | 47.8           | 4.9                    | 74.8                        | 0      |                              |
| 2007-Feb-23 | 10:13                  |                             |                   |                     |                |                        |                             |        | Drop Top Plug                |
| 2007-Feb-23 | 10:13                  |                             |                   |                     |                |                        |                             |        | Start Displacement           |
| 2007-Feb-23 | 10:13                  | 37                          | 8.86              | 0.0                 | 47.8           | 4.3                    | 74.8                        | 0      |                              |
| 2007-Feb-23 | 10:13                  |                             |                   |                     |                |                        |                             |        | End Spacer                   |
| 2007-Feb-23 | 10:13                  | 37                          | 8.79              | 1.6                 | 47.8           | 2.6                    | 75.1                        | 0      |                              |
| 2007-Feb-23 | 10:14                  | 23                          | 9.05              | 0.0                 | 47.8           | 4.3                    | 75.9                        | 0      |                              |
| 2007-Feb-23 | 10:14                  | 14                          | 9.15              | 0.0                 | 47.8           | 6.2                    | 79.0                        | 0      |                              |
| 2007-Feb-23 | 10:15                  | 37                          | 8.92              | 0.0                 | 47.8           | 7.9                    | 82.8                        | 0      |                              |
| 2007-Feb-23 | 10:15                  | 41                          | 8.51              | 0.0                 | 47.8           | 2.8                    | 85.7                        | 0      |                              |
| 2007-Feb-23 | 10:16                  | 55                          | 8.41              | 0.0                 | 47.8           | 3.2                    | 87.2                        | 0      |                              |
| 2007-Feb-23 | 10:16                  | 5                           | 8.66              | 0.0                 | 47.8           | 3.1                    | 89.0                        | 0      |                              |
| 2007-Feb-23 | 10:17                  | -14                         | 8.37              | 0.0                 | 47.8           | 0.8                    | 90.0                        | 0      |                              |
| 2007-Feb-23 | 10:17                  |                             |                   |                     |                |                        |                             |        | Reset Total, Vol = 47.76 bbl |
| 2007-Feb-23 | 10:17                  | -9                          | 8.35              | 0.0                 | 0.0            | 0.0                    | 0.0                         | 0      |                              |
| 2007-Feb-23 | 10:17                  | -14                         | 8.37              | 0.0                 | 0.0            | 0.0                    | 0.0                         | 0      |                              |
| 2007-Feb-23 | 10:18                  | -9                          | 8.37              | 0.0                 | 0.0            | 0.0                    | 0.0                         | 0      |                              |
| 2007-Feb-23 | 10:18                  | 50                          | 8.32              | 0.2                 | 0.1            | 5.4                    | 1.0                         | 0      |                              |
| 2007-Feb-23 | 10:19                  | 50                          | 8.33              | 0.0                 | 0.1            | 5.5                    | 3.7                         | 0      |                              |
| 2007-Feb-23 | 10:19                  | 46                          | 8.32              | 0.0                 | 0.1            | 5.6                    | 6.4                         | 0      |                              |
| 2007-Feb-23 | 10:20                  | 46                          | 8.33              | 0.0                 | 0.1            | 5.6                    | 9.2                         | 0      |                              |
| 2007-Feb-23 | 10:20                  | 50                          | 8.33              | 0.0                 | 0.1            | 5.7                    | 12.1                        | 0      |                              |
| 2007-Feb-23 | 10:21                  | 46                          | 8.34              | 0.0                 | 0.1            | 5.7                    | 14.9                        | 0      |                              |
| 2007-Feb-23 | 10:21                  | 46                          | 8.34              | 0.0                 | 0.1            | 5.6                    | 17.7                        | 0      |                              |
| 2007-Feb-23 | 10:22                  | 50                          | 8.33              | 0.0                 | 0.1            | 5.7                    | 20.5                        | 0      |                              |
| 2007-Feb-23 | 10:22                  | 50                          | 8.33              | 0.0                 | 0.1            | 5.7                    | 23.3                        | 0      |                              |
| 2007-Feb-23 | 10:23                  | 46                          | 8.34              | 0.0                 | 0.1            | 5.6                    | 26.1                        | 0      |                              |
| 2007-Feb-23 | 10:23                  | 46                          | 8.33              | 0.0                 | 0.1            | 5.6                    | 28.9                        | 0      |                              |
| 2007-Feb-23 | 10:24                  | 50                          | 8.33              | 0.0                 | 0.1            | 5.7                    | 31.7                        | 0      |                              |
| 2007-Feb-23 | 10:24                  | 50                          | 8.33              | 0.0                 | 0.1            | 5.6                    | 34.5                        | 0      |                              |
| 2007-Feb-23 | 10:25                  | 46                          | 8.34              | 0.0                 | 0.1            | 5.6                    | 37.3                        | 0      |                              |
| 2007-Feb-23 | 10:25                  | 50                          | 8.34              | 0.0                 | 0.1            | 5.6                    | 40.1                        | 0      |                              |
| 2007-Feb-23 | 10:26                  | 46                          | 8.34              | 0.0                 | 0.1            | 5.7                    | 43.0                        | 0      |                              |
| 2007-Feb-23 | 10:26                  | 46                          | 8.33              | 0.0                 | 0.1            | 5.6                    | 45.8                        | 0      |                              |
| 2007-Feb-23 | 10:27                  | 46                          | 8.33              | 0.0                 | 0.1            | 5.6                    | 48.6                        | 0      |                              |

KCC  
MAY 01 2007  
CONFIDENTIAL

RECEIVED  
KANSAS CORPORATION COMMISSION

MAY 03 2007

CONSERVATION DIVISION  
WICHITA, KS

| Well        |             |                   | Field   |          | Service Date |             | Customer                    |   | Job Number |
|-------------|-------------|-------------------|---------|----------|--------------|-------------|-----------------------------|---|------------|
| BRUNS #B-1  |             |                   | SALLEY  |          | 0754-Feb-23  |             | OXY RESOURCE CALIFORNIA LLC |   | 2205553097 |
| Date        | Time        | Treating Pressure | Density | CMT RATE | CMT VOL      | CS NRD RATE | CS NRD TOTAL                | 0 | Message    |
|             | 24 hr clock | psi               | lb/gal  | bbl/min  | bbl          | bbl/min     | bbl                         | 0 |            |
| 2007-Feb-23 | 10:27       | 50                | 8.33    | 0.0      | 0.1          | 5.7         | 51.4                        | 0 |            |
| 2007-Feb-23 | 10:28       | -18               | 8.33    | 0.0      | 0.1          | 0.1         | 53.6                        | 0 |            |
| 2007-Feb-23 | 10:28       | 46                | 8.35    | 0.0      | 0.1          | 3.0         | 53.7                        | 0 |            |
| 2007-Feb-23 | 10:29       | 46                | 8.33    | 0.0      | 0.1          | 5.6         | 56.4                        | 0 |            |
| 2007-Feb-23 | 10:29       | 46                | 8.33    | 0.0      | 0.1          | 5.6         | 59.2                        | 0 |            |
| 2007-Feb-23 | 10:30       | 50                | 8.33    | 0.0      | 0.1          | 5.7         | 62.0                        | 0 |            |
| 2007-Feb-23 | 10:30       | 46                | 8.33    | 0.0      | 0.1          | 5.7         | 64.9                        | 0 |            |
| 2007-Feb-23 | 10:31       | 46                | 8.33    | 0.0      | 0.1          | 5.6         | 67.7                        | 0 |            |
| 2007-Feb-23 | 10:31       | 50                | 8.33    | 0.0      | 0.1          | 5.7         | 70.5                        | 0 |            |
| 2007-Feb-23 | 10:32       | 50                | 8.33    | 0.0      | 0.1          | 5.7         | 73.3                        | 0 |            |
| 2007-Feb-23 | 10:32       | 46                | 8.33    | 0.0      | 0.1          | 5.6         | 76.1                        | 0 |            |
| 2007-Feb-23 | 10:33       | 46                | 8.33    | 0.0      | 0.1          | 5.6         | 78.9                        | 0 |            |
| 2007-Feb-23 | 10:33       | 50                | 8.33    | 0.0      | 0.1          | 5.7         | 81.8                        | 0 |            |
| 2007-Feb-23 | 10:34       | 50                | 8.33    | 0.0      | 0.1          | 5.7         | 84.6                        | 0 |            |
| 2007-Feb-23 | 10:34       | 46                | 8.33    | 0.0      | 0.1          | 5.6         | 87.4                        | 0 |            |
| 2007-Feb-23 | 10:35       | 50                | 8.33    | 0.0      | 0.1          | 5.7         | 90.2                        | 0 |            |
| 2007-Feb-23 | 10:35       | 50                | 8.33    | 0.0      | 0.1          | 5.7         | 93.0                        | 0 |            |
| 2007-Feb-23 | 10:36       | 46                | 8.33    | 0.0      | 0.1          | 5.6         | 95.9                        | 0 |            |
| 2007-Feb-23 | 10:36       | 46                | 8.33    | 0.0      | 0.1          | 5.6         | 98.7                        | 0 |            |
| 2007-Feb-23 | 10:37       | 50                | 8.33    | 0.0      | 0.1          | 5.7         | 101.5                       | 0 |            |
| 2007-Feb-23 | 10:37       | 50                | 8.33    | 0.0      | 0.1          | 5.7         | 104.3                       | 0 |            |
| 2007-Feb-23 | 10:38       | 46                | 8.33    | 0.0      | 0.1          | 5.6         | 107.1                       | 0 |            |
| 2007-Feb-23 | 10:38       | 50                | 8.33    | 0.0      | 0.1          | 5.6         | 109.9                       | 0 |            |
| 2007-Feb-23 | 10:39       | 50                | 8.33    | 0.0      | 0.1          | 5.7         | 112.8                       | 0 |            |
| 2007-Feb-23 | 10:39       | 46                | 8.33    | 0.0      | 0.1          | 5.6         | 115.6                       | 0 |            |
| 2007-Feb-23 | 10:40       | 50                | 8.33    | 0.0      | 0.1          | 3.7         | 117.8                       | 0 |            |
| 2007-Feb-23 | 10:40       | 114               | 8.33    | 4.5      | 1.7          | 4.6         | 119.7                       | 0 |            |
| 2007-Feb-23 | 10:41       | 206               | 8.33    | 4.6      | 4.0          | 4.7         | 122.1                       | 0 |            |
| 2007-Feb-23 | 10:41       | 261               | 8.33    | 4.6      | 6.3          | 4.7         | 124.4                       | 0 |            |
| 2007-Feb-23 | 10:42       | 275               | 8.33    | 4.7      | 8.6          | 4.7         | 126.8                       | 0 |            |
| 2007-Feb-23 | 10:42       | 316               | 8.33    | 4.7      | 10.9         | 4.8         | 129.2                       | 0 |            |
| 2007-Feb-23 | 10:43       | 385               | 8.33    | 4.7      | 13.2         | 4.7         | 131.6                       | 0 |            |
| 2007-Feb-23 | 10:43       | 385               | 8.33    | 4.7      | 15.6         | 4.8         | 133.9                       | 0 |            |
| 2007-Feb-23 | 10:44       | 439               | 8.33    | 4.7      | 17.9         | 4.8         | 136.3                       | 0 |            |
| 2007-Feb-23 | 10:44       | 467               | 8.33    | 4.8      | 20.3         | 4.8         | 138.7                       | 0 |            |
| 2007-Feb-23 | 10:45       | 458               | 8.33    | 3.0      | 22.0         | 2.7         | 140.6                       | 0 |            |
| 2007-Feb-23 | 10:45       | 430               | 8.33    | 2.7      | 23.4         | 2.8         | 142.0                       | 0 |            |
| 2007-Feb-23 | 10:46       | 430               | 8.33    | 2.2      | 24.7         | 2.3         | 143.3                       | 0 |            |
| 2007-Feb-23 | 10:46       | 439               | 8.33    | 2.1      | 25.8         | 2.2         | 144.4                       | 0 |            |
| 2007-Feb-23 | 10:47       | 458               | 8.33    | 2.1      | 26.8         | 2.2         | 145.5                       | 0 |            |
| 2007-Feb-23 | 10:47       | 471               | 8.33    | 2.1      | 27.9         | 2.2         | 146.6                       | 0 |            |
| 2007-Feb-23 | 10:48       | 490               | 8.33    | 2.1      | 29.0         | 2.1         | 147.7                       | 0 |            |
| 2007-Feb-23 | 10:48       | 504               | 8.33    | 2.1      | 30.0         | 2.2         | 148.8                       | 0 |            |
| 2007-Feb-23 | 10:49       | 531               | 8.33    | 2.1      | 31.1         | 2.1         | 149.9                       | 0 |            |
| 2007-Feb-23 | 10:49       | 540               | 8.33    | 2.1      | 32.1         | 2.1         | 150.9                       | 0 |            |
| 2007-Feb-23 | 10:50       | 549               | 8.33    | 2.0      | 33.1         | 2.1         | 152.0                       | 0 |            |
| 2007-Feb-23 | 10:50       | 471               | 8.32    | 0.0      | 34.1         | 1.1         | 153.0                       | 0 |            |
| 2007-Feb-23 | 10:51       | 453               | 8.32    | 0.0      | 34.1         | 0.0         | 153.0                       | 0 |            |
| 2007-Feb-23 | 10:51       | 462               | 8.32    | 0.0      | 34.1         | 0.0         | 153.0                       | 0 |            |
| 2007-Feb-23 | 10:52       | 458               | 8.32    | 0.0      | 34.1         | 0.0         | 153.0                       | 0 |            |
| 2007-Feb-23 | 10:52       | 453               | 8.34    | 0.0      | 34.1         | 0.0         | 153.0                       | 0 |            |
| 2007-Feb-23 | 10:53       | 449               | 8.35    | 0.0      | 34.1         | 0.0         | 153.0                       | 0 |            |
| 2007-Feb-23 | 10:53       | 444               | 8.37    | 0.0      | 34.1         | 0.0         | 153.0                       | 0 |            |
| 2007-Feb-23 | 10:54       | -9                | 8.35    | 0.0      | 34.1         | 0.0         | 153.0                       | 0 |            |

KCC  
MAY 01 2007  
CONFIDENTIAL

RECEIVED  
KANSAS CORPORATION COMMISSION

MAY 03 2007

CONSERVATION DIVISION  
Page 4 of 5  
WICHITA, KS

|                                       |                        |                   |                         |                |                                                        |                                                                                            |              |             |         |
|---------------------------------------|------------------------|-------------------|-------------------------|----------------|--------------------------------------------------------|--------------------------------------------------------------------------------------------|--------------|-------------|---------|
| Well                                  |                        | Field             |                         | Service Date   |                                                        | Customer                                                                                   |              | Job Number  |         |
| BRUNS #B-4                            |                        | SALLEY            |                         | 0754-Feb-23    |                                                        | OXY RESOURCE CALIFORNIA LLC                                                                |              | 2205553097  |         |
| Date                                  | Time                   | Treating Pressure | Density                 | CMT RATE       | CMT VOL                                                | CS NRD RATE                                                                                | CS NRD TOTAL | 0           | Message |
|                                       | 24 hr clock            | psi               | lb/gal                  | bbl/min        | bbl                                                    | bbl/min                                                                                    | bbl          | 0           |         |
| 2007-Feb-23                           | 10:54                  | -9                | 8.32                    | 0.0            | 34.1                                                   | 0.7                                                                                        | 153.1        | 0           |         |
| Post Job Summary                      |                        |                   |                         |                |                                                        |                                                                                            |              |             |         |
| Average Pump Rates, bpm               |                        |                   |                         |                | Volume of Fluid Injected, bbl                          |                                                                                            |              |             |         |
| Slurry                                | N2                     | Mud               | Maximum Rate            |                | Total Slurry                                           | Mud                                                                                        | Spacer       | N2          |         |
| 4                                     |                        |                   | 6                       |                | 52.4                                                   | 0                                                                                          | 20           |             |         |
| Treating Pressure Summary, psi        |                        |                   |                         |                | Breakdown Fluid                                        |                                                                                            |              |             |         |
| Maximum                               | Final                  | Average           | Bump Plug to            | Breakdown      | Volume                                                 |                                                                                            | Density      |             |         |
| 580                                   |                        | 200               |                         |                |                                                        |                                                                                            | bbl          | 8.34 lb/gal |         |
| Avg. N2 Percent                       | Designed Slurry Volume |                   | Displacement            | Mix Water Temp | <input type="checkbox"/> Cement Circulated to Surface? |                                                                                            | Volume       |             |         |
| %                                     | 52.4 bbl               |                   | 153 bbl                 | °F             | <input type="checkbox"/> Washed Thru Perfs             |                                                                                            | To           | ft          |         |
| Customer or Authorized Representative |                        |                   | Schlumberger Supervisor |                |                                                        | <input type="checkbox"/> CirculationLost <input checked="" type="checkbox"/> Job Completed |              |             |         |
| Franzone, Tony                        |                        |                   | Flanagan, Patrick       |                |                                                        |                                                                                            |              |             |         |


KCC  
MAY 01 2007  
CONFIDENTIAL

RECEIVED  
KANSAS CORPORATION COMMISSION

MAY 03 2007

CONSERVATION DIVISION  
WICHITA, KS

|                 |               |                                                     |                             |
|-----------------|---------------|-----------------------------------------------------|-----------------------------|
| <b>Well</b>     | Bruns B-1     | <b>Client</b>                                       | Oxy Resource California LLC |
| <b>Field</b>    | Salley        | <b>SIR No.</b>                                      |                             |
| <b>Engineer</b> |               | <b>Job Type</b>                                     | 5 1/2" casing               |
| <b>Country</b>  | United States | <b>Job Date</b>                                     | 02-23-2007                  |
|                 |               | MAY 01 2007<br>CONSERVATION DIVISION<br>WICHITA, KS |                             |

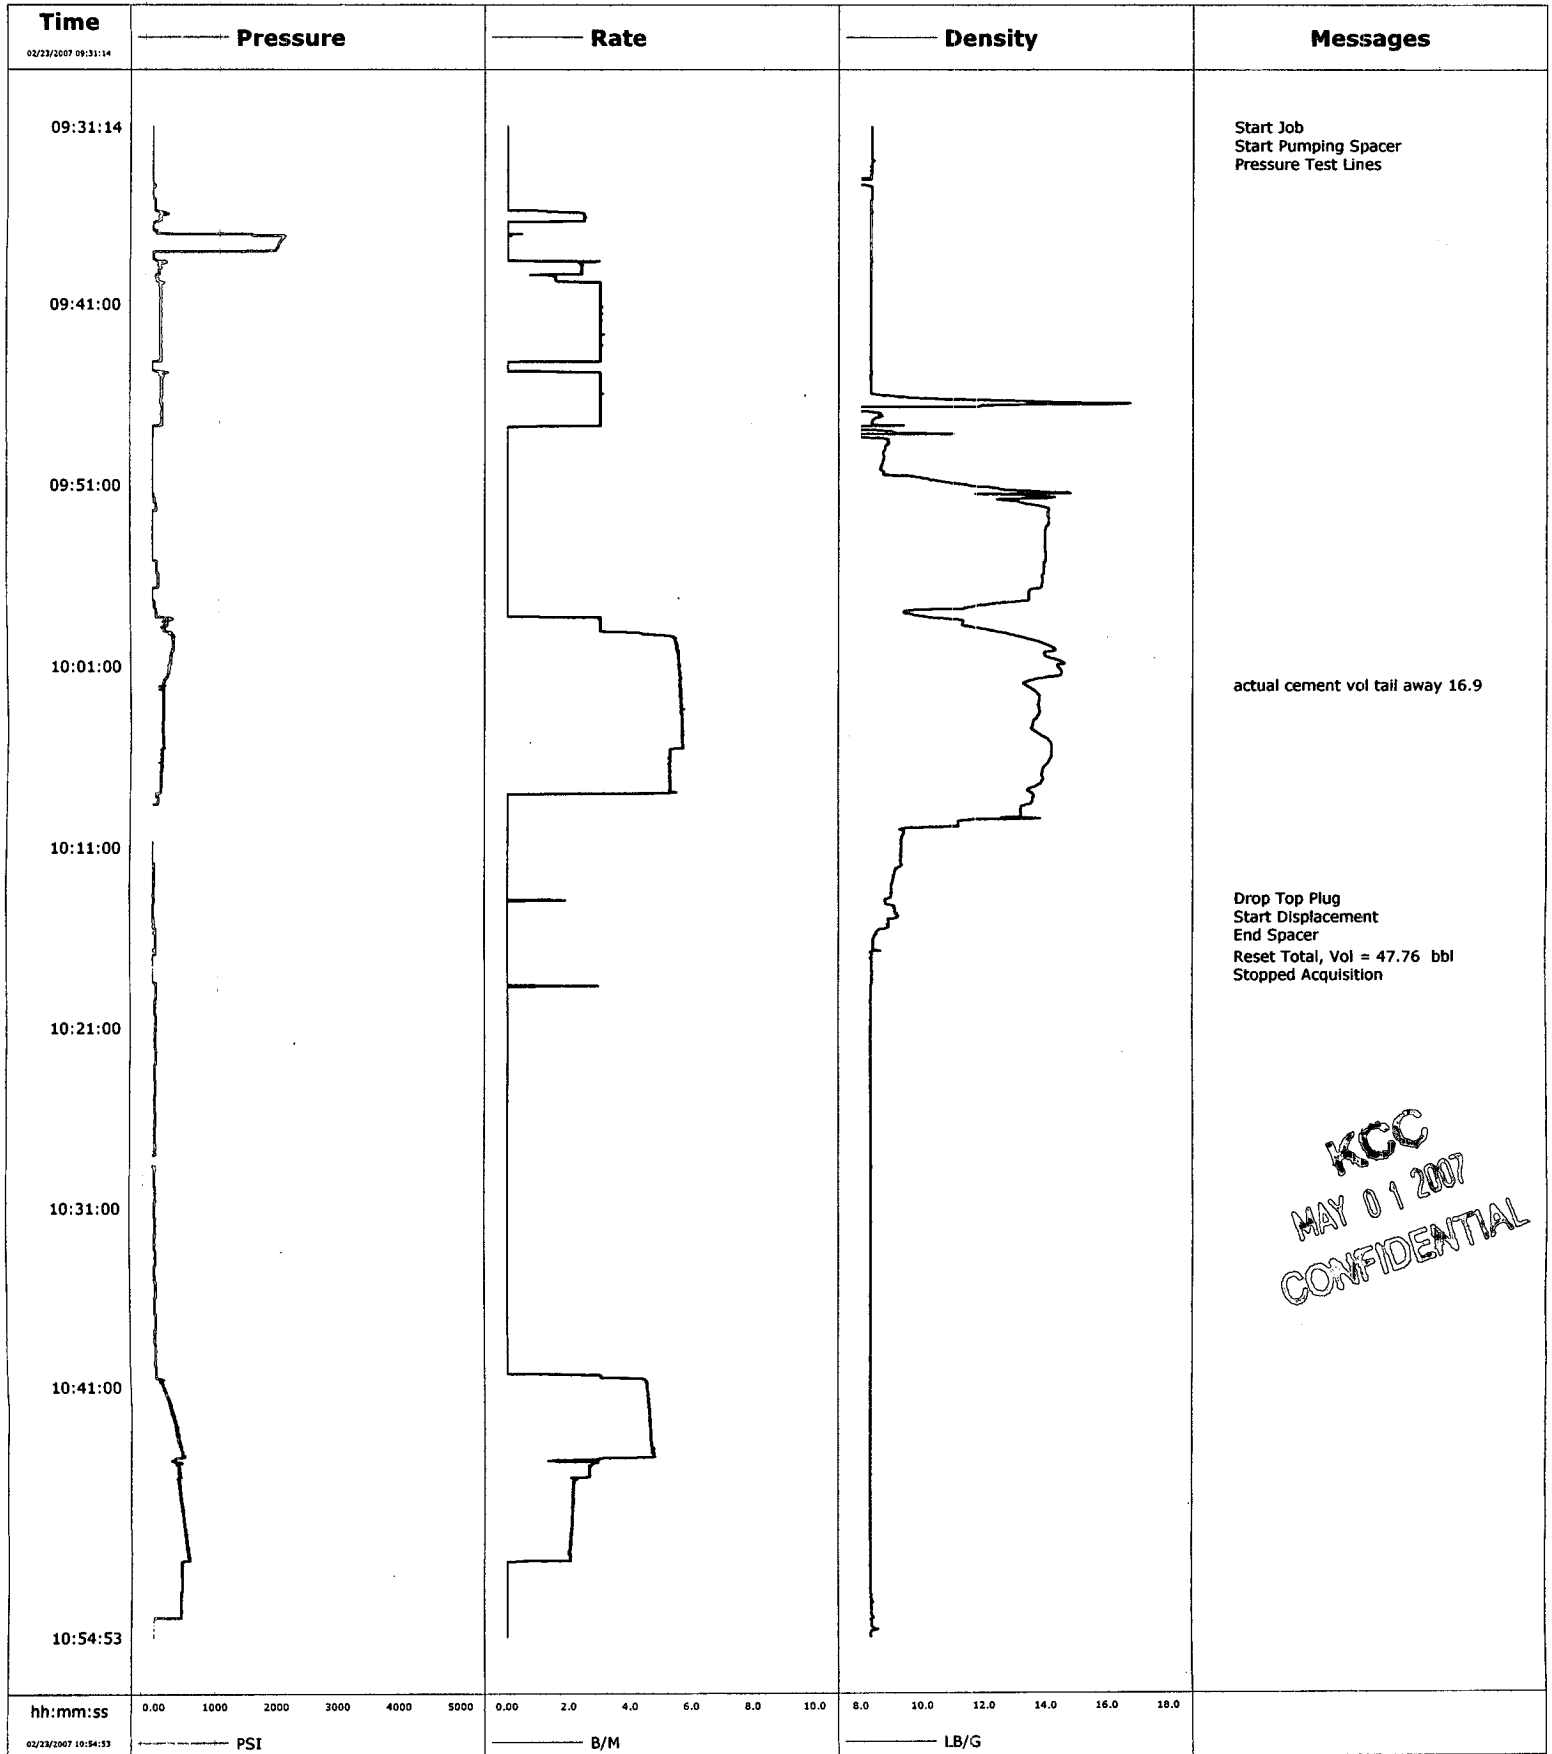

**KCC**  
MAY 01 2007  
CONFIDENTIAL


RECEIVED  
KANSAS CORPORATION COMMISSION

MAY 03 2007

CONSERVATION DIVISION  
WICHITA, KS

**Well** Bruns B-1  
**Field** Salley<sup>1</sup>  
**Engineer**  
**Country** United States

**Client** Oxy Resource California LLC  
**SIR No.**  
**Job Type** 5 1/2" casing  
**Job Date** 02-23-2007

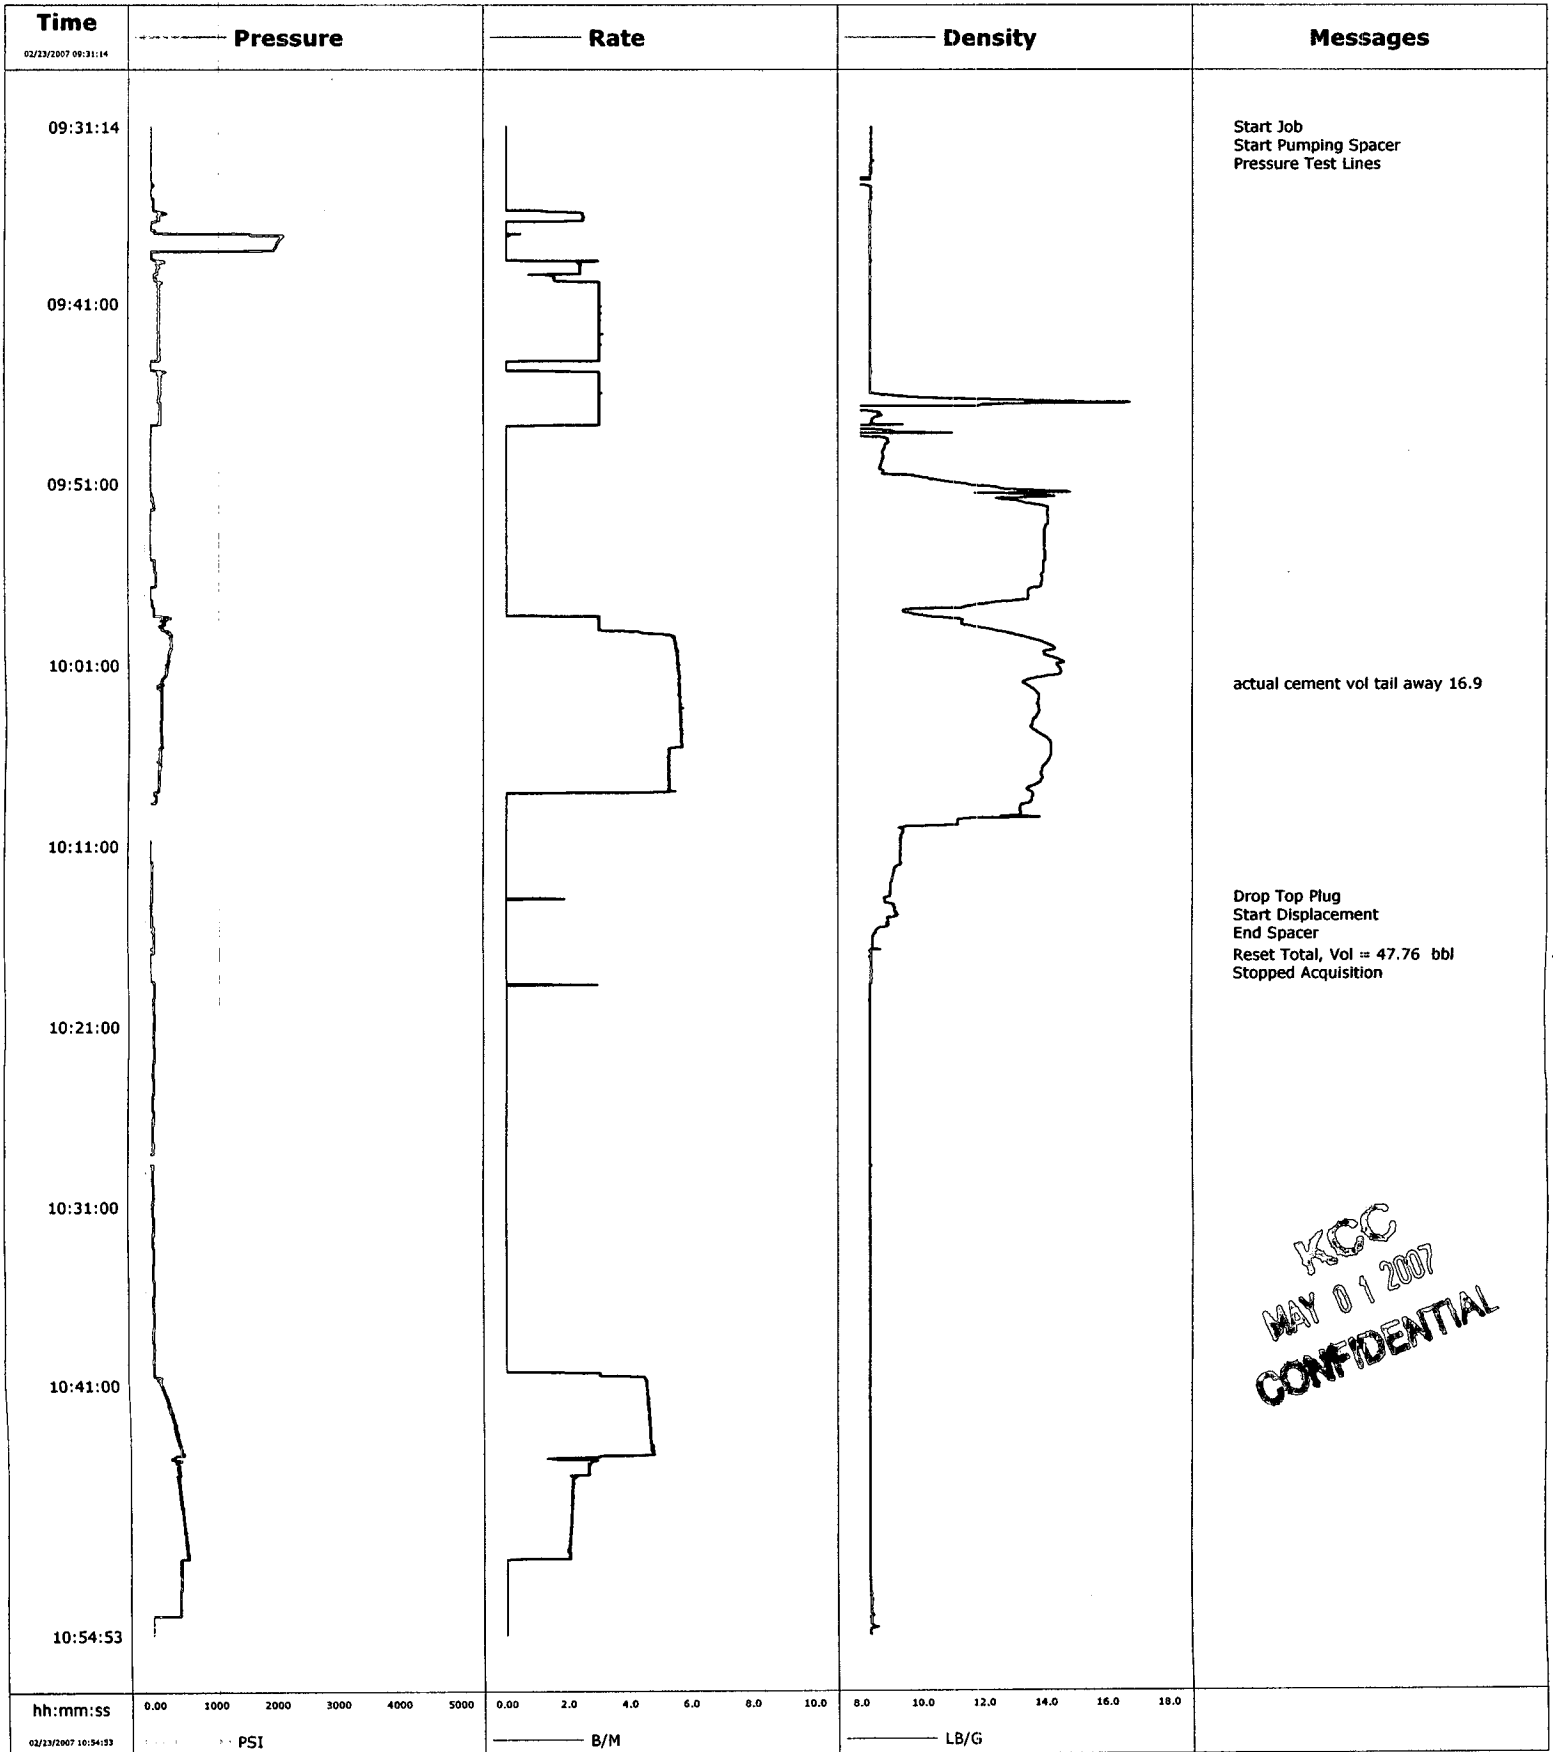

KCC  
MAY 01 2007  
CONFIDENTIAL

| <b>Well Information</b>        |            |                    |              |
|--------------------------------|------------|--------------------|--------------|
| <b>Company:</b>                | Oxy        | <b>Stage:</b>      | Single       |
| <b>Well Name:</b>              | Bruns      | <b>Job Type:</b>   | Surface      |
| <b>Well Number:</b>            | B-1        | <b>Job Date:</b>   | 2/23/2007    |
| <b>Spacer and Water</b>        |            |                    |              |
| Spacer(bbls)                   | 20         | Spcr Hydro(PSI)    | 280.76       |
| CW100                          |            | Total Water(bbls)  | 274.40       |
| <b>Cement Totals</b>           |            |                    |              |
| Lead sks                       | 0          | Lead CF            | 0            |
| Yeild                          | 0          | Lead(bbls)         | 0.00         |
| Water req.                     | 0          | BBLS Water         | 0.00         |
| Weight                         | 0          | Lead Height(ft)    | 0.00         |
|                                |            | Lead Hydro(PSI)    | 0.00         |
|                                |            | Excess(bbls)       | 0.00         |
| <b>Tail sks</b>                | <b>190</b> | <b>Tail CF</b>     | <b>294.5</b> |
| Yeild                          | 1.55       | Tail BBLS          | 52.450       |
| Water req                      | 1526.5     | BBLS Water         | 36.345       |
| Weight                         | 13.8       | Tail Height(ft)    | 1667.76      |
| Class C + 2%S1 + 0.125PPS D130 |            | Tail Hydro(PSI)    | 1196.78      |
| <b>Capacity Information</b>    |            |                    |              |
| Casing ID                      | 4.892      | bbls/ft casing     | 0.0232       |
| Casing OD                      | 5.500      | bbls/ft annular    | 0.0309       |
| Casing Weight                  | 17         | Casing cap.(bbls)  | 153.31       |
| Open Hole ID                   | 7 7/8      | Displacement(bbls) | 152.32       |
| Casing length                  | 6594.79    | Shoe Cap.(bbls)    | 0.99         |
| Shoe length                    | 42.54      | Annular cap.(bbls) | 203.65       |
| Annular length                 | 6600       | Hole Cap.(bbls)    | 397.37       |
| <b>Bump &amp; Lift</b>         |            |                    |              |
| Displ Fluid Wt.                | 8.33       | Disp Hydro(PSI)    | 2838.17      |
| Drilling Fluid Wt.             | 9.10       | Lift(PSI)          | 692.55       |
|                                |            | Casing Lift(PSI)   | 5032.50      |

25 SKS for Rat/Mouse Holes  
7 BBLs (3.5 BBLs per hole)

1 / PRIMARY / 5300 / 6200 / none / 0.0

KCC  
MAY 01 2007  
CONFIDENTIAL

RECEIVED  
KANSAS CORPORATION COMMISSION

MAY 03 2007

CONSERVATION DIVISION  
WICHITA, KS
