WELLBORE SCHEMATIC

Current

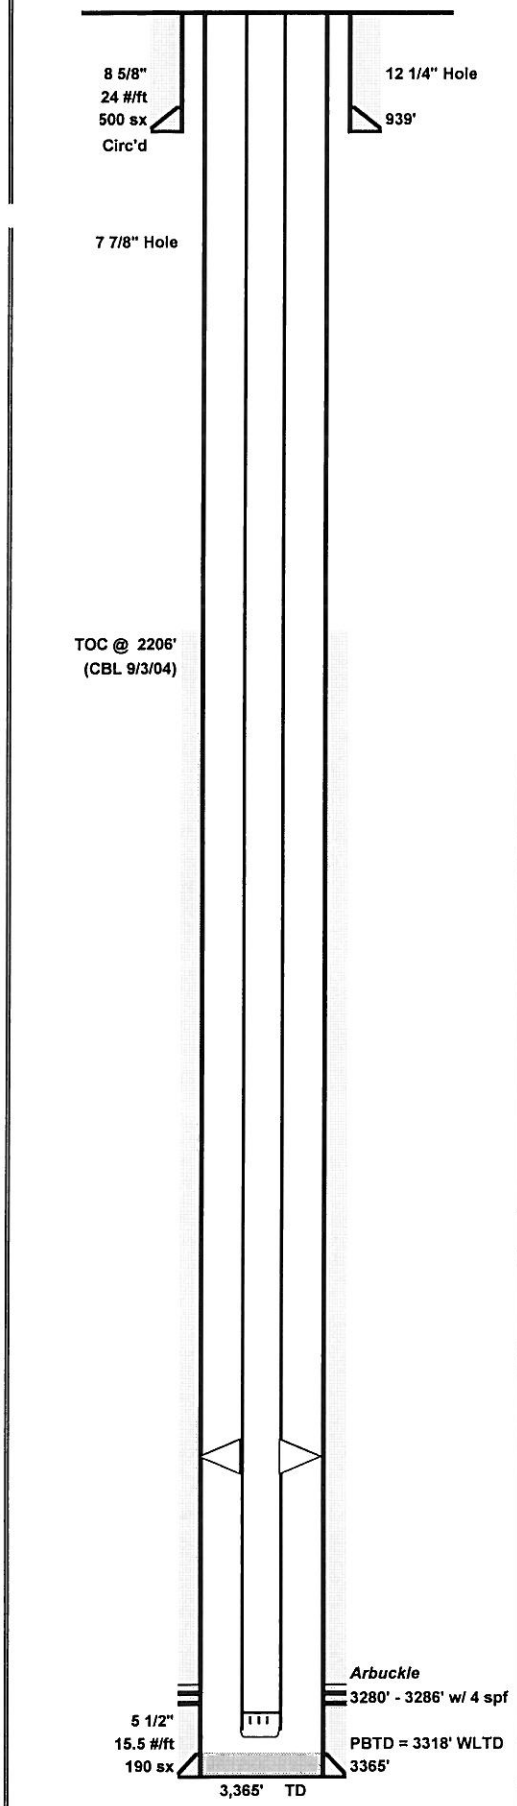

Lease:	Wieland Unit			Well No.	5-11
API No.	15-051-25322-0000			Status	Producer
Location:	655' FNL, 2160' FEL, NE/4, Sec. 1, T13S, R16W				
County:	Ellis	State:	KS	Field:	Fairport
TD	3365'	GL	1886'	Spud Date:	8/12/2006
PBTD	3318'	KB	1891'	Comp Date:	
Current Perfs/OH:	3280' - 3286'	Current Zone:	Arbuckle		

Surface Equipment

Unit Make:	Emsco	Unit Size:	DB 320-298-100
Unit S/N:	6039	Unit Rotation:	
SPM:	15.5	Stroke Length: 86"	Unit Sheave:
Prime Mover:	40 Hp Westinghouse	Motor Sheave:	
Motor S/N:	6907	Motor RPM:	1110

Casing Breakdown

	Size	Grade / Wt	Depth	Cement
Surface	8 5/8"	24 #/ft	939'	500 sx
Production	5 1/2"	15.5 #/ft	3365'	190 sx
Production				
Production				
Liner				

Tubing Breakdown

Qty	Description	Footage
	KB	3.00'
1	20' x 2 7/8" 6.5# J-55 EUE 8rd Tbg sub	10.00'
95 jts	2 7/8" 6.5# J-55 EUE 8rd Tbg	2943.80'
	TAC @ 2980' KB	3.00'
10 jts	2 7/8" 6.5# J-55 EUE 8rd Tbg	309.90'
	2 1/4" Tbg Pump Bbl w/ SN @ 3291' KB	21.33'
1	15' x 2 7/8" OPMA	15.00'
	TOTAL	3306.03'

Rod Breakdown

Qty	Description	Footage
1	1 1/2" x 22' PR	22.00'
2	7/8" x 8' pony rods	16.00'
60	7/8" Norris 78 SR's	1500.00'
71	3/4" Norris 78 SR's	1775.00'
	Plunger	
	TOTAL	3313.00'

Comments

PREPARED BY:	JH	UPDATED:	7/12/2012
