DRILL STEM TEST REPORT

TRILOBITE TESTING, INC.

Becker Oil Cororation
Box 1150
Ponca City OK 74602-1150
ATTN: Clyde M. Becker Jr.

19-24s-23w Hodgeman,KS
Oliphant #1
Job Ticket: 41274 **DST#: 1**
Test Start: 2012.05.15 @ 11:15:00

GENERAL INFORMATION:

Formation: **?**
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 13:21:45
Time Test Ended: 16:39:45

Test Type: Conventional Bottom Hole (Initial)
Tester: Harley Davidson
Unit No: 58

Interval: 4724.00 ft (KB) To 4767.00 ft (KB) (TVD)
Total Depth: 4767.00 ft (KB) (TVD)
Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2456.00 ft (KB)
2445.00 ft (CF)
KB to GR/CF: 11.00 ft

Serial #: 8355 **Inside**

Press@RunDepth:	psig @	4725.00 ft (KB)		Capacity:	8000.00 psig
Start Date:	2012.05.15	End Date:	2012.05.15	Last Calib.:	2012.05.15
Start Time:	11:15:35	End Time:	16:39:44	Time On Btm:	
				Time Off Btm:	

TEST COMMENT: IF- Weak surface blow that died after 5 min, Flushed tool, weak surface blow.
ISI- No blow back.
FF- No blow.
FSI- No blow back.

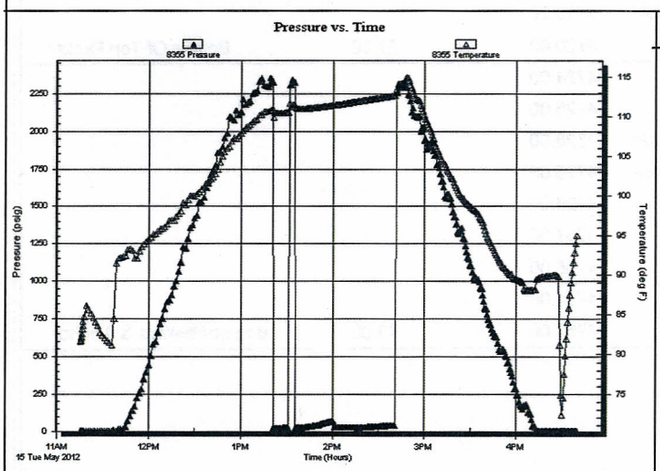

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation

Recovery

Length (ft)	Description	Volume (bbl)
10.00	100% mud	0.14

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
