All wellwork requires rod BOP and tbg BOP during workovers.

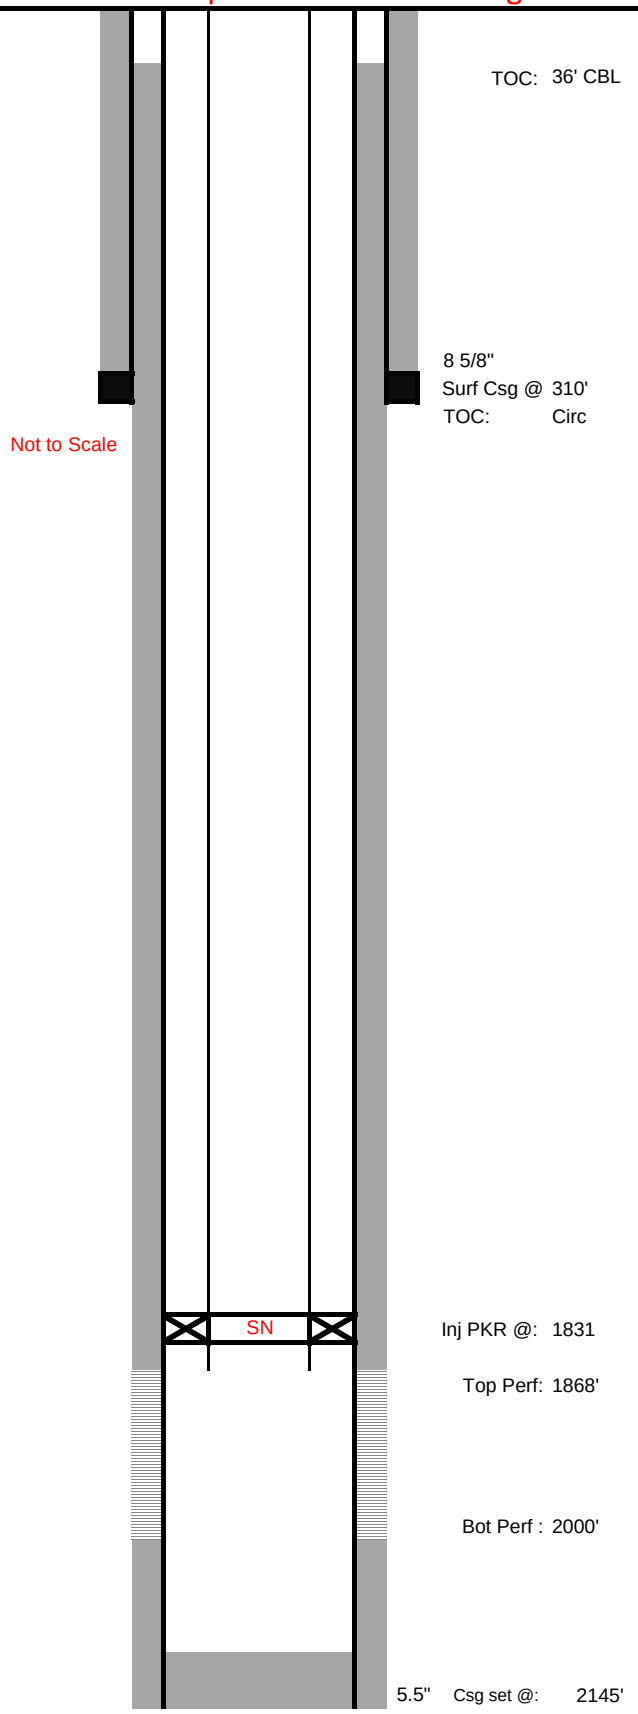

Wellbore Dia			Daves Unit #36-10 SWD		
Status	Producing		Operator	Stelbar Oil Corp	
Lease	Daves Unit		Zone	Stalnaker Inj Zone	
Field	Daves Unit		API	15-035-24482-00-00.	
State:	Kansas		Docket #	D-31,397	
Location	1175' FNL & 1658' FEL; SW/4, SE/4 NW/4, NE/4 Sec 10-30S-4E, Cowley County, KS:				
Reference:					
KB	1,225	TVD	2155'	Orig PBTD	2125'
GL	1,218	MTD	2155'	SN	1831

Casing	Weight/Grade	Depth	Cmt Sx	Hole	TOC
N/A Conductor					
8 5/8"	23#/J-55	310'	185	12 1/4"	Circ
5.5"	14#/J-55	2145'	310	7 7/8"	Circ 30 sx but cmt fell back to 36' CBL

Spud	12/4/2012		Top Perf	1868'	
Completion	1/7/2013		Bot Perf	2000'	

12/13/12: Perf 1980-2000, 1965-80, 1950-65, 1910-30, 1868-1883' W 19 gm chrgs @ 4 JSPF & 90 Deg Phasing. 380 Total Shots:

12/13/12: Acid Stim w/ 2500 gal 15% NEFE Acid with 300ea 7/8" Perf Balls; and 3350 ga; 2% KCL flush. Formation broke down @ 1100psi & went on vacuum with Acid at top perf. Minimal ball action.

Date sketch checked	**2/28/12**	by:	WHB	
Date tubulars checked	**2/28/13**	by:	WHB	

Current Tubulars

Tubing String Size	Grade	# Jnts	Type	Length, ft	Depth, ft
			KBE	7.00	7.00
2 3/8"	J-55	56	IPC Tbg	1823.60	1830.60
Baker 2 3/8" X 5 1/2" Injection Paker				3.00	1833.60
			Bottom of Tbg String:		1833.60

Rods String Size	Grade	# Rods	Length, ft	Depth, ft
