Geologic Report

Drilling Time and Sample Log

Operator	**American Warrior, Inc.**		Elevation 2155'
Lease	**Baumgarten Unit**	No. **1-24**	KB DF GL 2149'
API #	**15-135-25676-0000**		Casing Record Surface 8 5/8" @ 227' Production 5 1/2" @ 4245'
Field	**Wunder**		Electrical Surveys None
Location	**2550' FSL & 335' FEL**		
Sec. **24**	Twp. **18s**	Rge. **22w**	
County	**Ness**	State **Kansas**	

Formation	Log Tops	Sample Tops	Struct Comp
Anhydrite		1419' +736	-4
Base		1452' +703	
Heebner		3618' -1463	FL
Lansing		3662' -1507	+2
BKc		3976' -1821	
Pawnee		4058' -1903	
Fort Scott		4134' -1979	+6
Cherokee		4155' -2000	+8
Mississippian		4228' -2073	+5
Total Depth		4246' -2091	

Reference Well For Structural Comparison Galloway Drilling Co. Roth #1
1980' FSL & 660' FEL Sec. 24 T18s R22w Ness Co. Kansas

Drilling Contractor Petromark Drilling, LLC. Rig #1

Commenced	11-22-2013	Completed	12-1-2013
Samples Saved From	3900'	To	RTD
Drilling Time Kept From	3500'	To	RTD
Samples Examined From	3900'	To	RTD
Geological Supervision From	3900'	To	RTD

Displacement 3600' Mud Type Chemical

Summary and Recommendations

The location for the Baumgarten Unit #1-24 was found via 3-D seismic survey. The new well ran structurally as expected via the survey. One drill stem test was conducted which recovered commercial amounts of oil from the Mississippian Osage Formation. After all gathered data had been examined the decision was made to run 5 1/2 inch production to further evaluate the Baumgarten Unit #1-24 well.

Respectfully Submitted,
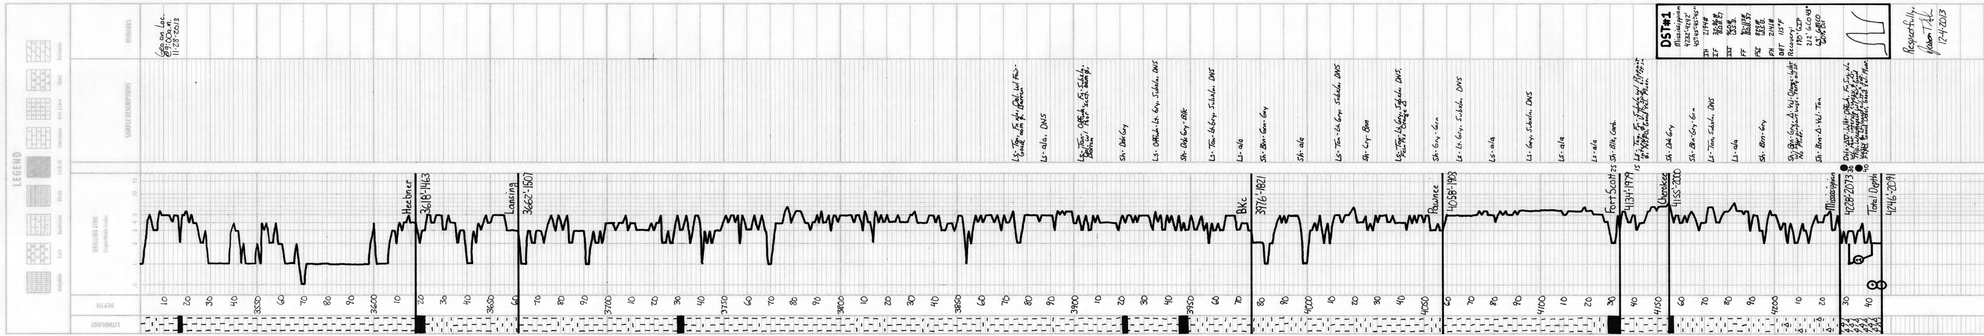
Jason T. Alm
Hard Rock Consulting, Inc.
