Geologic Report

Drilling Time and Sample Log

Hard Rock Consulting, Inc.

Operator	**American Warrior, Inc.**		Elevation KB 2120' DF GL 2112'
Lease	**GS**	No. **1-33**	
API #	**15-135-25806-0000**		Casing Record Surface 8 5/8" @ 1358' Production 5 1/2" @ 4221'
Field	**Bazine**		
Location	**740' FNL & 520' FWL**		Electrical Surveys None
Sec. **33**	Twp. **18s**	Rge. **21w**	
County **Ness**	State **Kansas**		

Formation	Log Tops	Sample Tops	Struct Comp
Anhydrite		1352' +768	-1
Base		1386' +734	
Heebner		3580' -1460	-1
Lansing		3626' -1506	+1
BKc		3948' -1828	+1
Pawnee		4027' -1907	+1
Fort Scott		4102' -1982	+1
Cherokee		4118' -1998	FL
Mississippian		4198' -2078	
Osage		4204' -2084	FL
Total Depth		4222' -2102	

Reference Well For Structural Comparison **Colorado Oil & Gas Corp. Miner #1 C NW NW Sec. 33 T18s R21w Ness Co. Kansas**

Drilling Contractor	**Discovery Drilling Co. Inc.**		**Rig #3**
Commenced	**8-27-2014**	Completed	**9-5-2014**
Samples Saved From	**3000'**	To	RTD
Drilling Time Kept From	**3500'**	To	RTD
Samples Examined From	**3900'**	To	RTD
Geological Supervision From	**3900'**	To	RTD

Displacement **3500'** Mud Type **Chemical**

Summary and Recommendations

The location for the GS #1-33 was found via 3-D seismic survey. The new well ran structurally as expected via the survey. One Drill Stem Test was conducted, results were inconclusive due to plugging of test tool. After all gathered data had been examined the decision was made to run 5 1/2 inch production casing to further evaluate the GS #1-33 well.

Respectfully Submitted,
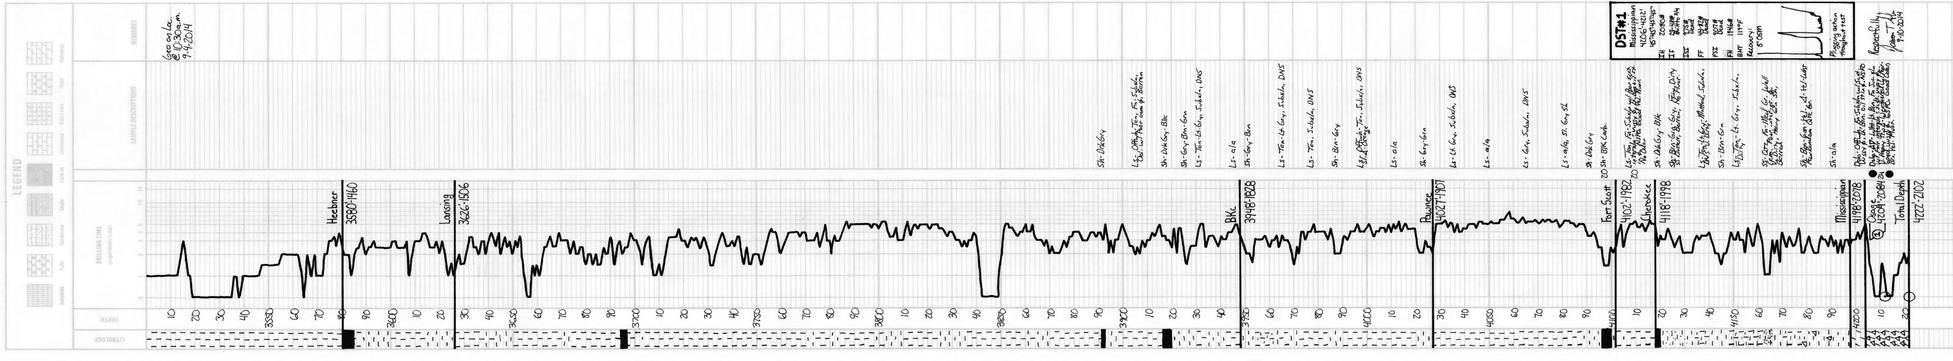
Jason T. Alm
Hard Rock Consulting, Inc.
