DRILL STEM TEST REPORT

TRILOBITE TESTING, INC

Ron's Oil Operations Inc
1889 200th AVE
Penokee KS 67659

ATTN: Chris Bean

22-9s-24w Graham,KS

Ron Nickelson #22-1

Job Ticket: 64882 **DST#: 2**

Test Start: 2015.12.03 @ 01:27:00

GENERAL INFORMATION:

Formation: **LKC "E-F"**
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 03:50:00
Time Test Ended: 09:12:15

Test Type: Conventional Straddle (Reset)
Tester: Cody Bloedorn
Unit No: 73

Interval: 3864.00 ft (KB) To 3894.00 ft (KB) (TVD)
Total Depth: 4056.00 ft (KB) (TVD)
Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2439.00 ft (KB)
2433.00 ft (CF)
KB to GR/CF: 6.00 ft

Serial #: 8940 **Outside**

Press@RunDepth: psig @ 3865.00 ft (KB)
Start Date: 2015.12.03 End Date: 2015.12.03
Start Time: 01:27:05 End Time: 09:12:14

Capacity: 8000.00 psig
Last Calib.: 2015.12.03
Time On Btm:
Time Off Btm:

TEST COMMENT: 60 - IF- 2 1/2" blow
45 - ISI- No return
45 - FF- 1/2" blow
45 - FSI- No return

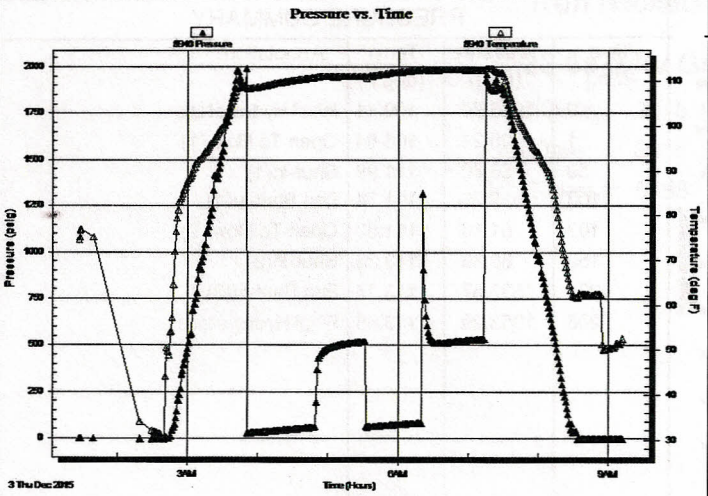

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation

Recovery

Length (ft)	Description	Volume (bbl)
129.00	WM - Oil spots, 2%W, 98%M	1.81

* Recovery from multiple tests

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
