001534
CRD NO.

PRO-STAKE LLC
Construction Site Staking

12790
INVOICE NO.

P.O. Box 2324 Garden City, Kansas 67846
Office/Fax: (620) 276-6159 – Cell: (620) 272-1499
burt@pro-stakellc.kscoxmail.com

Culbreath Oil & Gas Company, Inc.
OPERATOR

Logan County, KS	5	15s	34w
COUNTY	Sec.	Twp.	Rng.

Sowers 1-5
LEASE NAME

926' FSL - 1398' FEL
LOCATION SPOT

2912.6'
GR. ELEVATION

SCALE: 1" = 1000'
DATE STAKED: Sept. 16th, 2015
MEASURED BY: Kent c.
DRAWN BY: Norby S.
AUTHORIZED BY: Kevin H.
DATE REVISED:

N

LEGEND

- irr. well
- water hydrant
- tank battery
- staked loc.
- prod. well / aband. well
- house
- building
- gas line
- water line
- transmission powerline
- 3 phase powerline
- single phase powerline
- fence
- gravel / sand rd.
- gravel trail / lease rd.
- dirt rd.
- dirt trail / lease rd.
- Hwy / blacktop rd.

DIRECTIONS: From the West side of Russell Springs, KS at the intersection of Hwy 25 & Broadway St. – Now go 0.8 miles East on Broadway St. – Now go 8.5 miles South on 270 Rd. – Now go 1 mile East on Gold Rd. – Now go 1 mile East on lease rd. to the NW corner of section 5-15s-34w – Now go 0.5 mile South & East on lease rd. – Now go approx. 3470 S-SE & East through pasture with cattle to ingress stake South into – Now go approx.1570' South through pasture with cattle, into staked location.

Final ingress must be verified with landowner or operator.
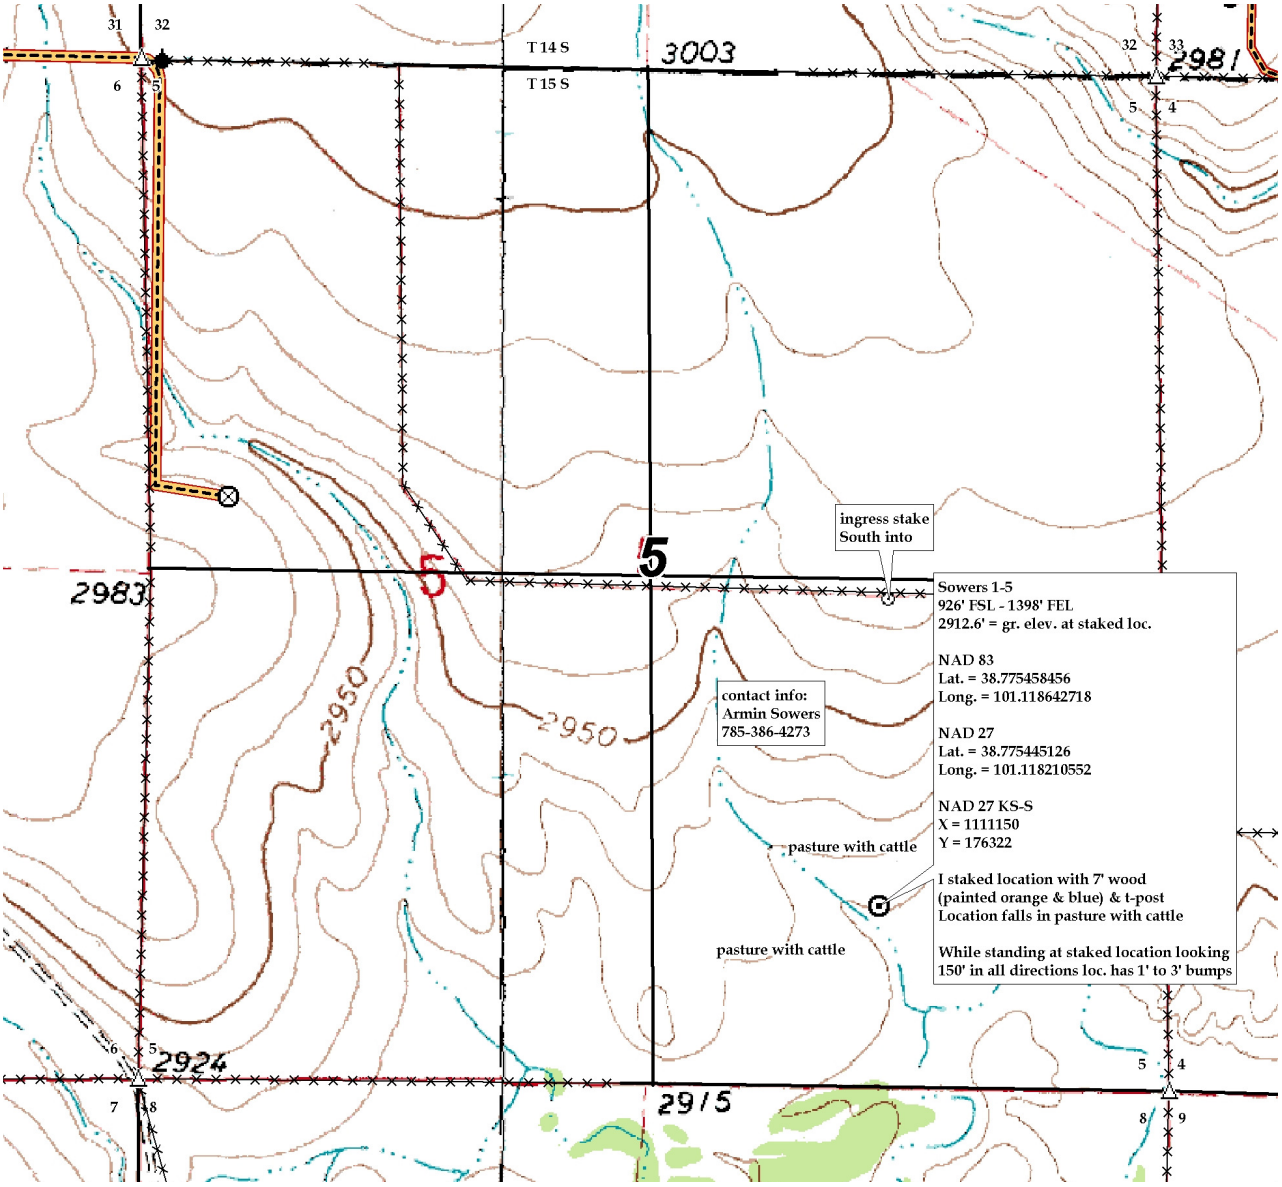
This drawing does not constitute a monumented survey or a land survey plat.
This drawing is for construction purposes only.
