WELLBORE SCHEMATIC

PROPOSED

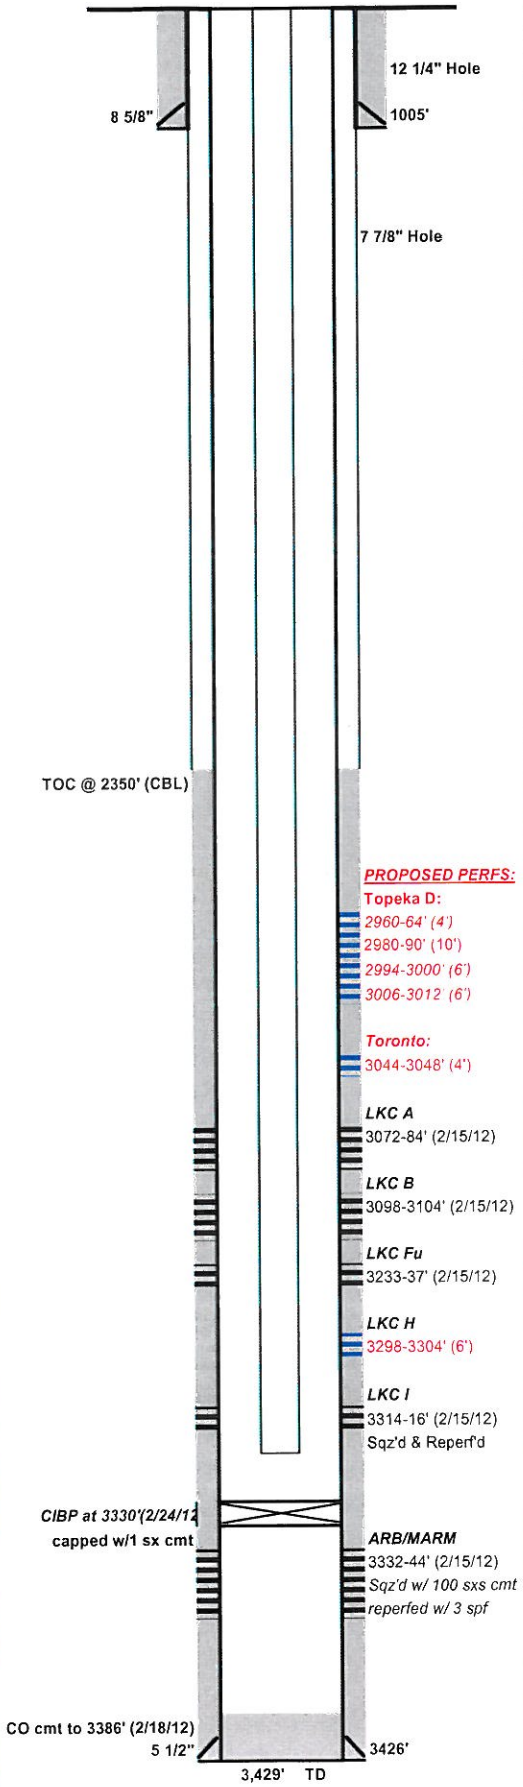

Lease:	Schmitt			Well No.	8-9
API No.	15-051-26236				
Location:	979' FSL, 3515' FEL. SE NW SE SW. T13S R16W Sec. 1				
County:	Ellis	State:	KS	Field:	Fairport
TD	3429'	KB	1936'	Spud Date:	2/4/2012
PBTD	3330'	GL	1928'	Comp Date:	2/28/2012
Current Perfs/OH:	3072-84', 3098-3104', 3233-37', 3314-16'	Current Zone:		LKC A, LKC B, LKC Fu, LKC I	

Surface Equipment

Unit Make:		Unit Size:	
Unit S/N:		Unit Rotation:	
SPM:	Stroke Length:	Unit Sheave:	
Prime Mover:		Motor Sheave:	
Motor S/N:		Motor RPM:	

Casing Breakdown

	Size	Grade / Wt	Depth	Cement
Surface	8 5/8"	24 #/ft	1005'	500 sxs
Production	5 1/2"	15.5 #/ft	3426'	195 sxs
Production				
Production				
Liner				

Completion Assembly

Qty	Description	Footage
101	2-7/8" tbg	3280.0'
	TOTAL	3280.00'

Rod Detail

Qty	Description	Footage
1	26' x 1-1/2" Polish Rod	26.00'
1	4' x 1" Pony	4.00'
1	2" x 1" Pony	2.00'
130	1" rods, 1" pins	3250.00'
1	Rotor	15.50'
	1 - 15-1400 (95 BBL/100 RPM) PCP	
	TOTAL	3297.50'

Comments

2/15/12: Perf'd LKC & Marm/Arb zones with 3 SPF & 120° phasing

ARB/MARM & LKC I sqz'd 2/16/12 w/ 50 sxs h2o loss + 50 sxs NEAT. Pavg=600# @ 4 BPM, Pfinal=1500#

PREPARED BY:	LMCV	UPDATED:	8/31/2018
