WELLBORE SCHEMATIC

CURRENT

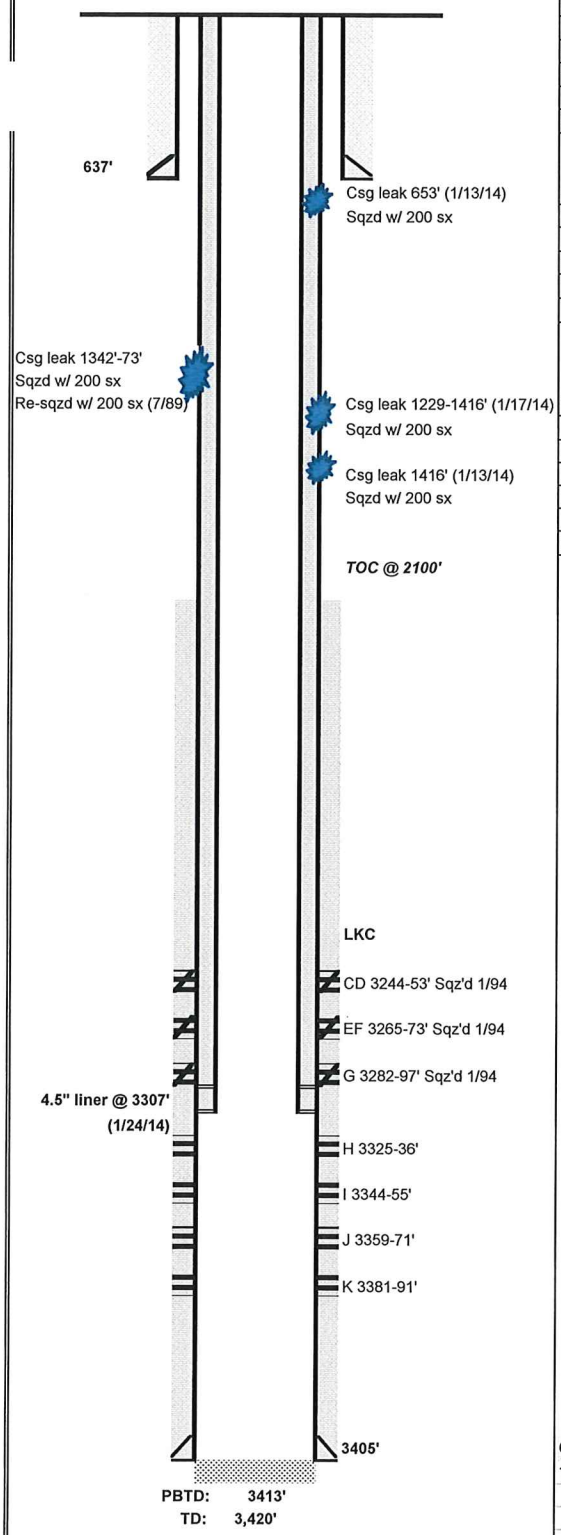

Lease:	West Hiss LKC Unit			Well No.	#5
API No.	15-009-07177			Status	PR
Location:	C N2 SW NE, Sec. 36, T20S-R14W				
County:	Barton	State:	KS	Field:	Pritchard
TD:	3420'	GL	1907'	Spud Date:	10/9/1947
PBTD	3413'	KB	2016'	Comp Date:	11/10/1947
Current Perfs/OH:	LKC	Current Zone:	LKC		

Surface Equipment

Unit Make:		Unit Size:	
Unit S/N:		Unit Rotation:	
SPM:	Stroke Length:	Unit Sheave:	
Prime Mover:		Motor Sheave:	
Motor S/N:		Motor RPM:	

Casing Breakdown

	Size	Grade / Wt	Depth	Hole Size	Cement
Surface	8-5/8"	J-55/24#	637'		200 sxs
Production	5-1/2"	H-40/14#	3405'		200 sxs
Production					
Production					
Liner	4-1/2"	11.5#	3307'		150 sxs

Tubing Breakdown

Qty	Description	Footage
102	2-3/8" Tbg	3174.10'
	2-3/8" x 4-1/2" TAC @ 3176.85'	2.75'
3	2-3/8" Tbg	92.72'
1	2-3/8" x 2-1/4" x 14' x 18' TP @3287.57	18.00'
1	2-3/8" MA	15.00'
	TOTAL	3302.57'

Rod Breakdown

Qty	Description	Footage
	1-1/4" x 16' PR w/ 10' liner	10
3	7/8" pony rods: 8', 6', 4'	18
130	7/8" rods	3250
	ON/OFF tool	
	TOTAL	3278.00'

Comments

1/27/14: Tagged cmt at 2830', drilled hard cmt to 3015'. DO to 3266', circulate clean. POH

PREPARED BY:	LMCV	UPDATED:	6/23/2016
