Well Name: Janssen #1
Company: Hess Oil Company
Location: 5-18s-7w
Rice county Kansas
Date: 8-17-99

TRILOBITE TESTING L.L.C.

OPERATOR : Hess Oil Company — DATE 8-15-99
WELL NAME: Janssen #1 — KB 1730.00 ft — TICKET NO: 11881 — DST #1
LOCATION : 5-18s-7w Rice co KS — GR 1725.00 ft — FORMATION: Lansing
INTERVAL : 2996.00 To 3028.00 ft — TD 3028.00 ft — TEST TYPE: CONV

RECORDER DATA

Mins		Field	1	2	3	4
PF 30	Rec.	13308	13308	24174		
SI 30	Range(Psi)	4700.0	4700.0	3925.0	0.0	0.0
SF 5	Clock(hrs)	12	12	12		
FS 0	Depth(ft)	3000.0	3000.0	3023.0	0.0	0.0

TIME DATA----------
PF Fr. 2344 to 2414 hr
IS Fr. 2414 to 2444 hr
SF Fr. 2444 to 0100 hr
FS Fr. to hr

	Field	1	2	3	4
A. Init Hydro	1441.0	1443.0	0.0	0.0	0.0
B. First Flow	49.0	75.0	0.0	0.0	0.0
B1. Final Flow	49.0	75.0	0.0	0.0	0.0
C. In Shut-in	713.0	812.0	0.0	0.0	0.0
D. Init Flow	0.0	0.0	0.0	0.0	0.0
E. Final Flow	0.0	0.0	0.0	0.0	0.0
F. Fl Shut-in	0.0	0.0	0.0	0.0	0.0
G. Final Hydro	1394.0	1379.0	0.0	0.0	0.0
Inside/Outside	o	o	i		

T STARTED 2230 hr
T ON BOTM 2340 hr
T OPEN 2344 hr
T PULLED 0100 hr
T OUT 0202 hr

RECOVERY
Tot Fluid 120.00 ft of 120.00 ft in DC and 0.00 ft in DP
120.00 ft of Thin mud
0.00 ft of
0.00 ft of
0.00 ft of
0.00 ft of
0.00 ft of
0.00 ft of
0.00 ft of
SALINITY 0.00 P.P.M. A.P.I. Gravity 0.00

TOOL DATA----------

Tool Wt.	2100.00 lbs
Wt Set On Packer	20000.00 lbs
Wt Pulled Loose	60000.00 lbs
Initial Str Wt	44000.00 lbs
Unseated Str Wt	44000.00 lbs
Bot Choke	0.75 in
Hole Size	7.88 in
D Col. ID	2.25 in
D. Pipe ID	3.80 in
D.C. Length	213.00 ft
D.P. Length	2772.00 ft

BLOW DESCRIPTION
Initial Flow:
Slid tool 15' when opening and lost 20' of mud down hole
5" blow decreasing to 4", bled off blow, no blow
Final Flow:
No blow, flushed tool, no blow after surge


MUD DATA----------

Mud Type	Chemical
Weight	9.00 lb/ci
Vis.	40.00 S/L
W.L.	9.60 in3
F.C.	0.00 in
Mud Drop	
Amt. of fill	0.00 ft
Btm. H. Temp.	110.00 F
Hole Condition	
% Porosity	0.00
Packer Size	6.75 in
No. of Packers	2
Cushion Amt.	0.00
Cushion Type	
Reversed Out	
Tool Chased	
Tester	Paul Simpson
Co. Rep.	Ken LeBlanc
Contr.	Mallard
Rig #	
Unit #	
Pump T.	

SAMPLES:
SENT TO:

Test Successful: Y

CHART PAGE

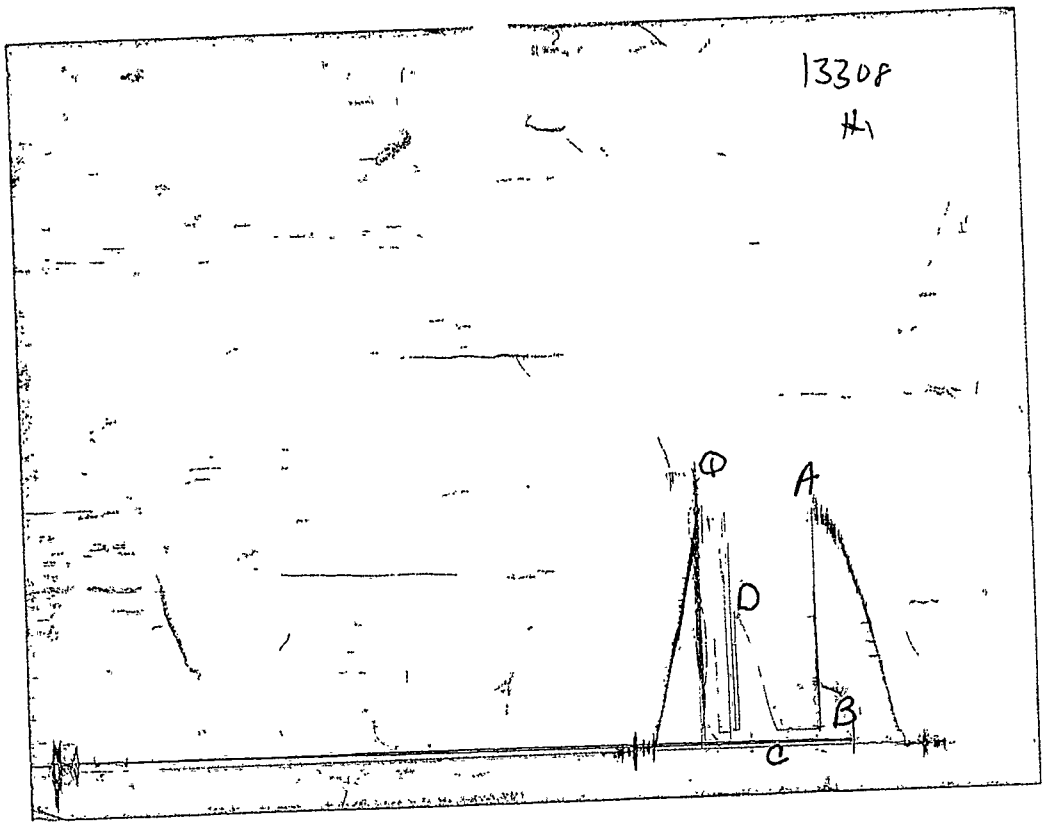

This is a photocopy of the actual AK-1 recorder chart
