Eliza	#1	#1	Gulf Oil Corp.
LEASE	WELL NO.	TEST NO.	COMPANY

Halliburton
OIL WELL CEMENTING COMPANY

LOCATION	26 - 10 - 20
FIELD	Wildcat
COUNTY	Rooks
STATE	Kansas
CONTRACTOR	Herndon Drilling Co.

MUD DATA

Kind	Starch	
Weight	9.9	lbs.-gal.
Viscosity	33.5	sec.
Filter Loss	17.5	c. c. Filter Cake 3/32 in.
Bt. P.R.D. No.	100	
12	Hr. Clock No. 1560	
Est. Gauge Depth Temp.	99	°F
Initial Hydro Mud Pressure	1825	p.s.i.
Initial Flow Pres.	10	p.s.i.
Tool Open	1 Hr.	
Final Flow Pres.	144	p.s.i.
Time Closed In	10 Min.	
Closed in Pres.	1105	p.s.i.
Final Hydro Mud Pressure	1755	p.s.i.

HOLE & TOOL DATA

Total Depth	3515	Packer Depth	3470
Hole Size	7-7/8"	Perforations	-
Formation Tested	Kansas City		
Size Drill Pipe	4½" API FH	Size Drill Collars	5½" x 51.38'
Tool No.	770	P.R.D. Pressure Dev. No.	1620
Bottom Choke	-	Surface Choke	-
Tool Valve	1"	Pilot Valve	-
Size & Length Anchor	4½" x 10.37', 4½" x 29.70' D.P. & 4½" x 4.83'		
Size & Type Packer	6-1/2" D. E. W. P.	No. Packers	1
Amount of Blanket	-	Lower P.R.D. Blanked	NO


REMARKS: Hole in good shape. Opened tool at 7:21 P.M. Good blow pressure increasing for 30 min. to 8" water. Reduced to 4" water by end of test. Closed tool at 8:21. Off bottom at 8:31 P.M. Mud lost approx. 20'. Recovered 295' saltwater.

Date	2-10-50
Ticket No.	9260
District	Hayes
Called Out	3:40 P.M.
On Location	4:50 P.M.
Kind of Job	Open Hole
Price	$210.00
Packer Chg.	-
Safety Joint	-
Extra Folder Charge	-
Total	$210.00
Witnessed By	J.P.Coplin
Tester	Thomas D. Pugh, Jr.

All depths measured from Kelly Bushings Elevation 2168 Ft. No. Folders Reproduced 5

HOWCO 893—Southwestern 10490B 5m 10-49

TIME

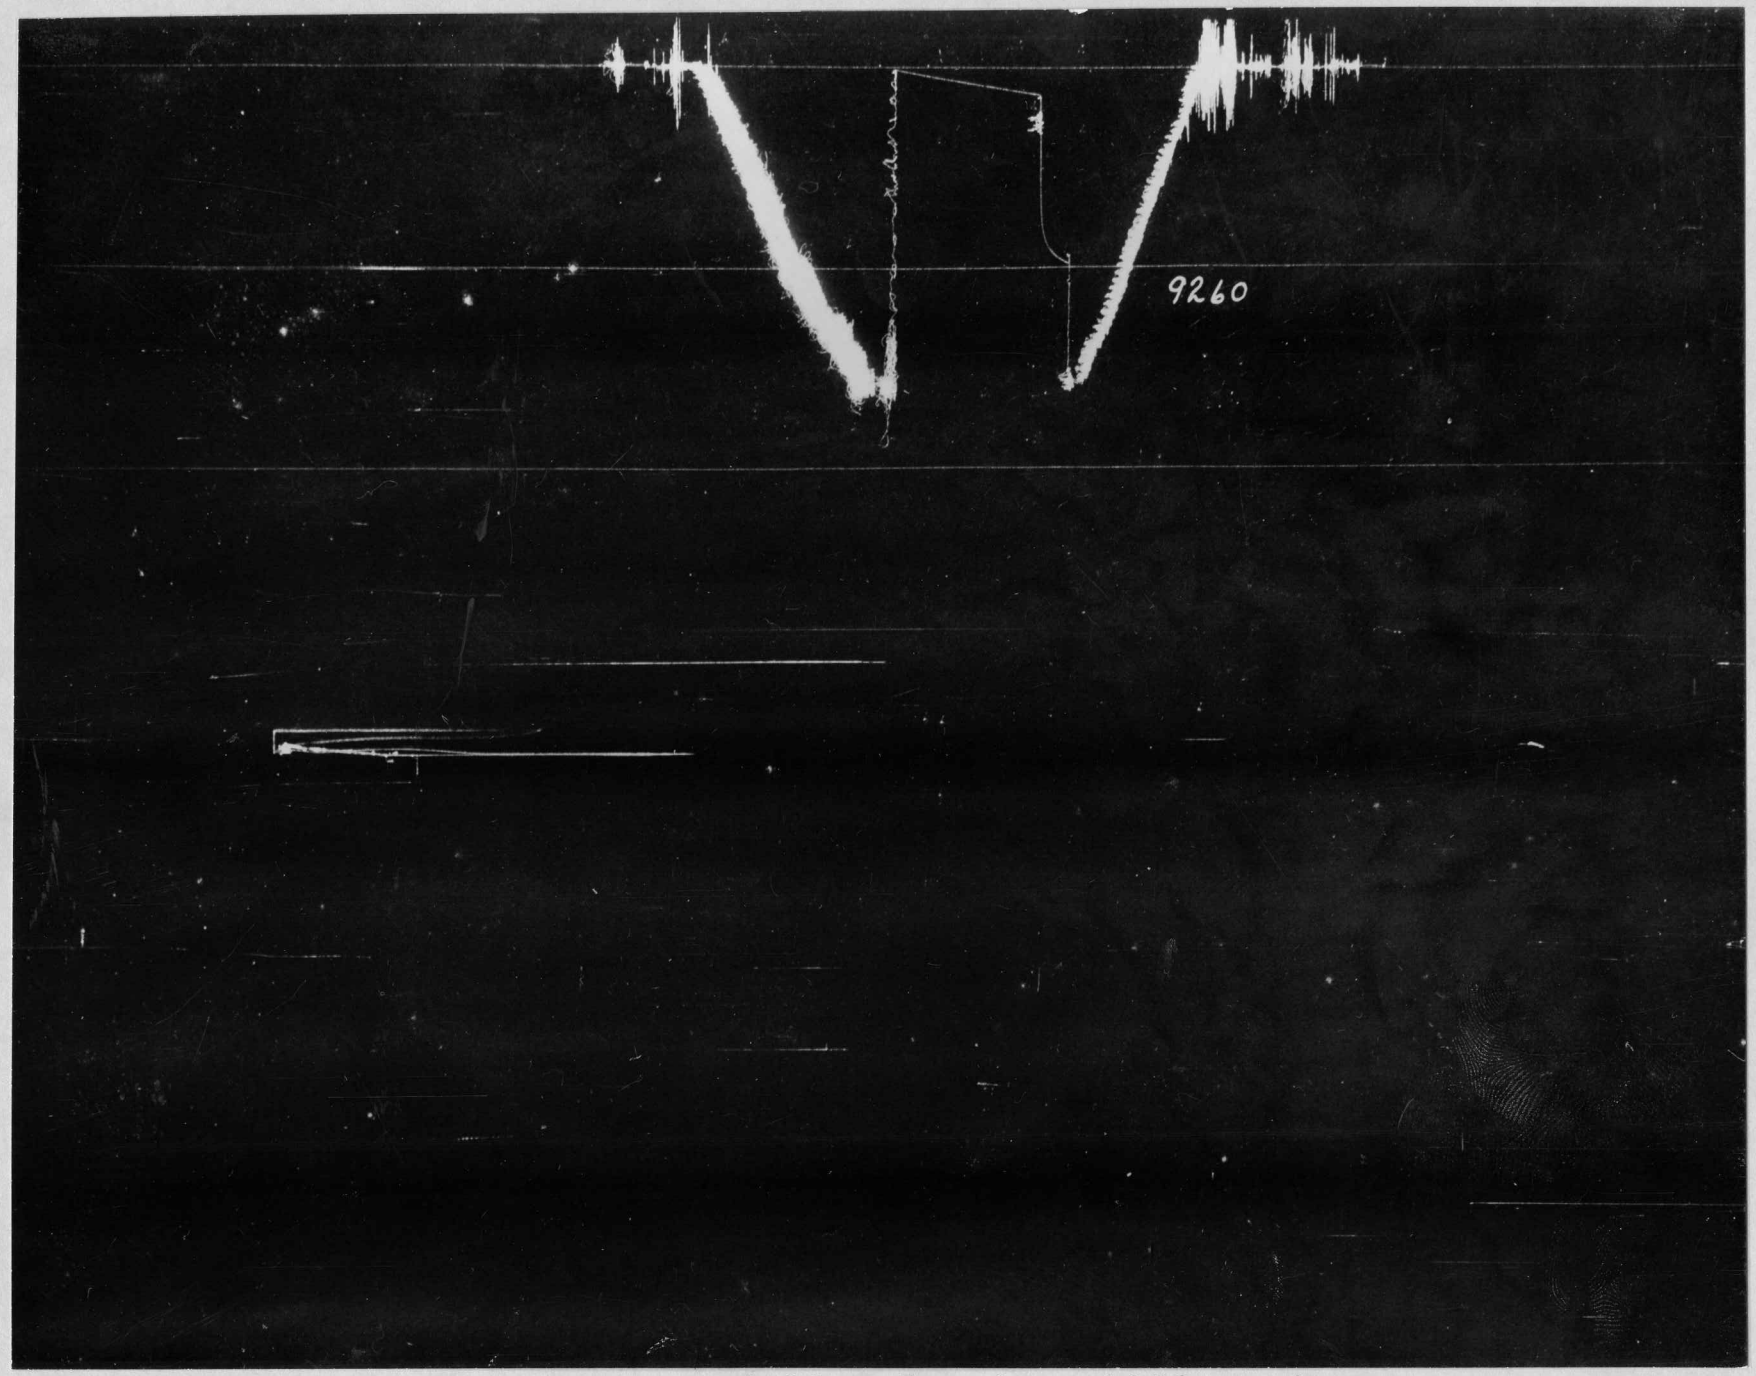

PRESSURE

Each Horizontal Line Equal to 1000 p.s.i.
