TEST TICKET

BEE FORMATION TESTING CO.

P. O. BOX 491
GREAT BEND, KANSAS

DATE 9-2-56

No. 1482

CUSTOMER'S ORDER NO.

NAME OF COMPANY STRATA DRLG Co

ADDRESS TO MAIL INVOICE McBRIDE BLDG. - GREAT BEND, KANSAS

ADDRESS TO MAIL PRESSURE CHARTS SAME

LEASE BOLLIG WELL NO. #1 COUNTY TREGO STATE KANSAS

TESTER J. C. Stanier jr APPROVED Charles W. Stewart

DRILL STEM TEST NO. 1 SUCCESSFUL NO. 1 MIS-RUN NO. 0 FORMATION TESTED K.C.

SIZE HOLE 7 7/8 TOOL JT. 4 1/2 FH

RUBBER SIZE 6 3/4 x 2 7/8 x 30 TEST TOOL SIZE 4 5/8

PACKER SET AT 3676' ANCHOR SIZE 4 1/2 FH

TOTAL DEPTH WELL 3697' LENGTH ANCHOR 21'

PRESSURE RECORDER CAP. 3000 x 3000 DRILL PIPE RUN: DRY ✓ WITH FLUID

RESULTS:

PACKER SET 6:10 A.M. TOOL OPEN 6:15 A.M. TOOL OPEN 30 MIN. HRS.

BLOW WEAK INTERMENTENT BLOW FOR 12 MIN.
BY PASS TOOL BLEW 5 MIN.

RECOVERY
30' MUD

SHUT IN PRESSURE TIME 15 MIN. MUD WT. 10.3 VIS. 37 WATER LOSS 25.0


BHP 1175 IFP FFP HYDROSTATIC HEAD 2050

EXTRA EQUIPMENT NONE JARS ✓ NO. ✓ SIZE ✓

OPERATOR TIME 8 TOOL RENTAL TIME

BEE FORMATION TESTING CO.

SHALL NOT BE LIABLE FOR DAMAGE OF ANY KIND TO THE PROPERTY OR PERSONNEL OF THE PARTY FOR WHOM A TEST IS MADE, OR FROM ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH OR IN THE COURSE OF THE USE OF ITS EQUIPMENT, ALL OF WHICH LOSS OR DAMAGE IS ASSUMED BY THE CUSTOMER. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT THE COST OF THE PARTY FOR WHOM TEST IS MADE.

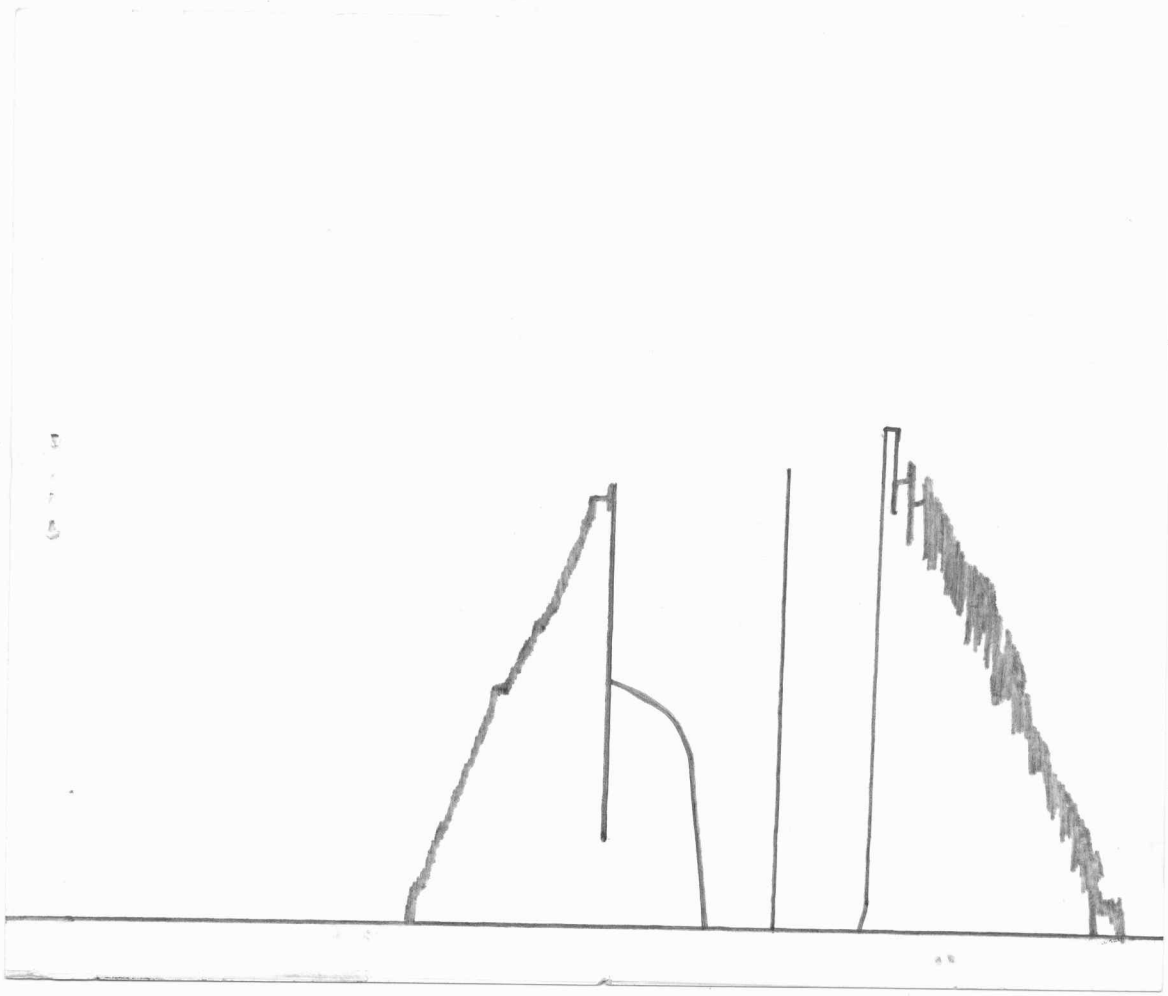

TEST TICKET

BEE FORMATION TESTING CO.

P. O. BOX 491
GREAT BEND, KANSAS

No. 1716

DATE 9-4-56

CUSTOMER'S ORDER NO.

NAME OF COMPANY STRATA Drlg. INC.

ADDRESS TO MAIL INVOICE

ADDRESS TO MAIL PRESSURE CHARTS

LEASE Bozlig WELL NO. #1 COUNTY Trego STATE KANSAS

TESTER D.K. Westhusin. APPROVED L.L. Clay

DRILL STEM TEST NO. 2 SUCCESSFUL NO. MIS-RUN NO. FORMATION TESTED Arb.

SIZE HOLE 7⅞ TOOL JT. 4½ F.H.

RUBBER SIZE 6¾ - 2⅞ - 29 TEST TOOL SIZE 4⅞

PACKER SET AT 3994 ANCHOR SIZE 4½

TOTAL DEPTH WELL 4005 LENGTH ANCHOR 11'

PRESSURE RECORDER CAP. 3000 - 3000 DRILL PIPE RUN: DRY yes WITH FLUID —

RESULTS:

PACKER SET 12:40 P.M. TOOL OPEN 1245 P.M. TOOL OPEN 1 hr. HRS.

BLOW WEAK Blow Throughout Test.

RECOVERY 180' of muddy water.

SHUT IN PRESSURE TIME 20 min. MUD WT. 10.5 VIS. 42 WATER LOSS 18.00

BHP 1065 IFP 60 FFP 145# HYDROSTATIC HEAD 2375'

EXTRA EQUIPMENT Safety Joint JARS NO. SIZE

OPERATOR TIME TOOL RENTAL TIME

BEE FORMATION TESTING CO.

SHALL NOT BE LIABLE FOR DAMAGE OF ANY KIND TO THE PROPERTY OR PERSONNEL OF THE PARTY FOR WHOM A TEST IS MADE, OR FROM ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH OR IN THE COURSE OF THE USE OF ITS EQUIPMENT, ALL OF WHICH LOSS OR DAMAGE IS ASSUMED BY THE CUSTOMER. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT THE COST OF THE PARTY FOR WHOM TEST IS MADE.

