
OIL WELL CEMENTING INC.

Date 3-10-71 DRILL STEM TEST RECOVERY REPORT Ticket No. 6712

3400

6712

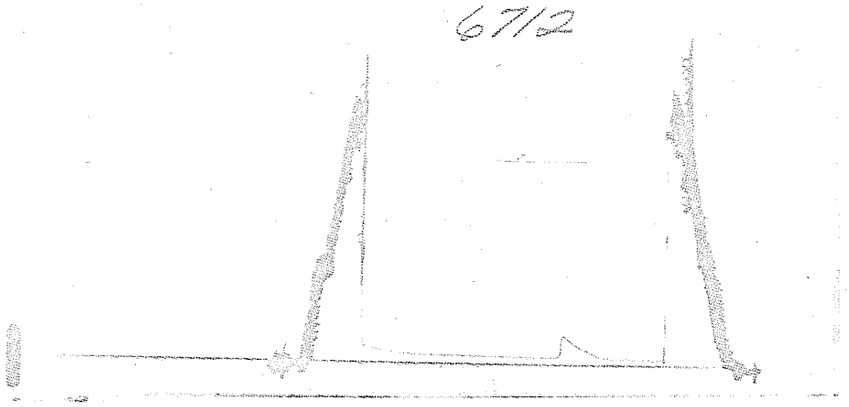

Company AMERICAN DRILLING CO. LTD. Contractor AMERICAN DRILLING CO.

Well No. 2 Lease BAKER County ELLSWORTH Sec. Twp Rng

Test No. 3 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 FH

Interval Tested From 2434 To 2475 Depth of Well 2475 Size Choke 5/8

Fluid Recovered In Temp. 90 Elev.

Initial Hyd. 1560 P.S.I Final Hyd. P.S.I.

First Initial Flow Pressure 25 P.S.I. Opened Tool 2:00 XXX P.M.

First Final Flow Pressure P.S.I. First Flow Pres. 45 Min.

Initial Closed-in Pressure 142 P.S.I. Initial Closed-in Pres. 45 Min.

Second Initial Flow Pressure 25 P.S.I. Second Flow Pres. 135 Min.

Second Final Flow Pressure P.S.I. Final Closed-in Pres. 45 Min.

Final Closed-in Pressure 83 P.S.I.

Blow WEAK BLOW, INCREASING TO FAIR THRU-OUT TEST

Recovery 310' GAS


40' SLIGHT OIL & GAS CUT MUD WITH FREE OIL IN TOOL

Remarks

Approved By RICHARD FOLEY Tester SMITH #013

SUN OIL WELL CEMENTING INC.

Date 3-11-71 DRILL STEM TEST RECOVERY REPORT Ticket No. 6713

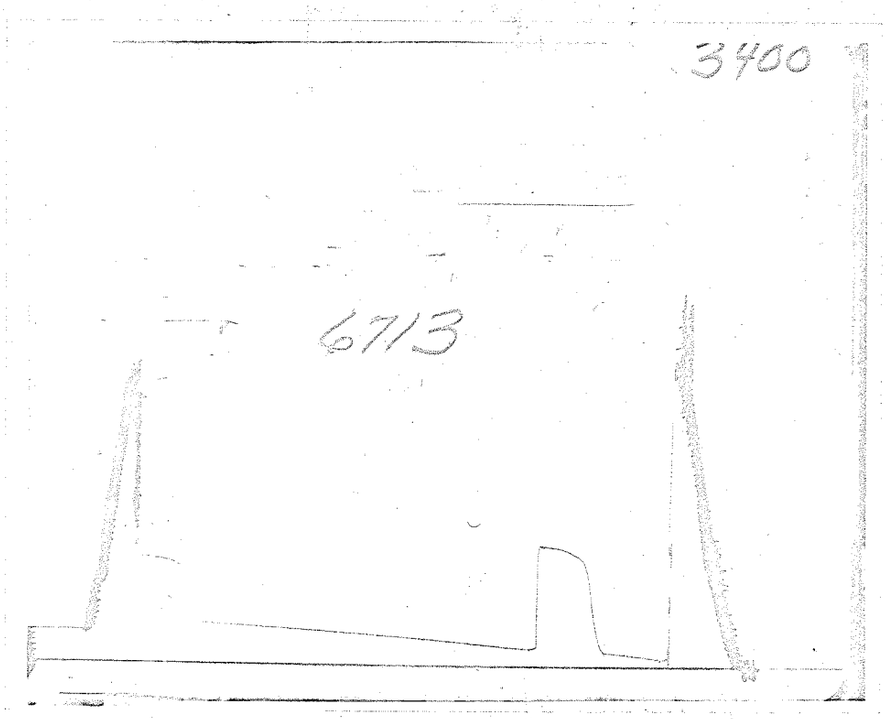

Company AMERICAN DRILLING CO. LTD. Contractor AMERICAN DRILLING CO.

Well No. 2 Lease BAKER County ELLSWORTH Sec. Twp Rng

Test No. 2 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 FH

Interval Tested From 2828 To 2858 Depth of Well 2858 Size Choke 5/8

Fluid Recovered In Temp. 94 Elev.

Initial Hyd. 1551 P.S.I Final Hyd. P.S.I.

First Initial Flow Pressure 25 P.S.I. Opened Tool 8:55 ~~XXX~~ P.M.

First Final Flow Pressure 58 P.S.I. First Flow Pres. 60 Min.

Initial Closed-in Pressure 620 P.S.I. Initial Closed-in Pres. 60 Min.

Second Initial Flow Pressure 83 P.S.I. Second Flow Pres. 300 Min.

Second Final Flow Pressure 209 P.S.I. Final Closed-in Pres. 60 Min.

Final Closed-in Pressure 553 P.S.I.

Blow STRONG BLOW THRU-OUT TEST

Recovery 2400' GAS 350' CLEAN GASSY OIL

60' MUDDY GASSY OIL EMULSION 30' THIN WATERY MUD

60' MUDDY OIL


Remarks

Approved By RICHARD FOLEY Tester SMITH #013

OIL WELL CEMENTING INC.

Date 3-12-71 **DRILL STEM TEST RECOVERY REPORT** Ticket No. 6714

3400

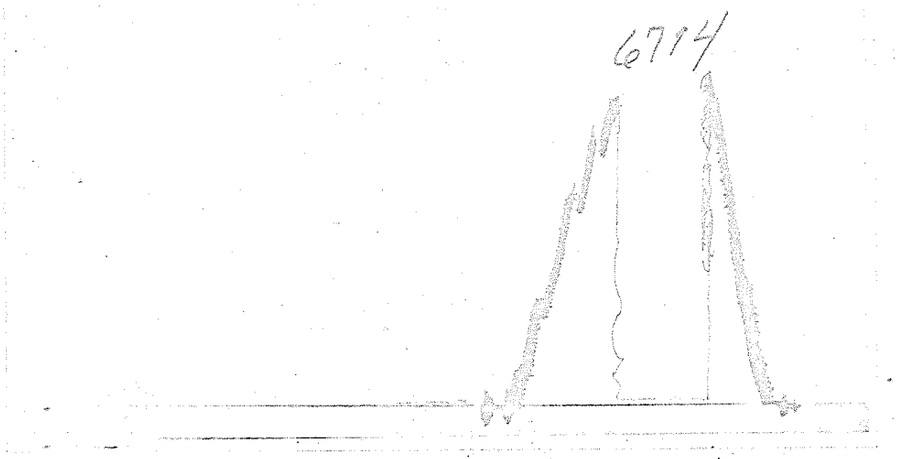

Company AMERICAN DRILLING CO. LTD. Contractor AMERICAN DRILLING CO.

Well No. 2 Lease BAKER County ELLSWORTH Sec. Twp Rng

Test No. 3 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 FH

Interval Tested From 2891 To 2922 Depth of Well 2922 Size Choke 5/8

Fluid Recovered In Temp. 96 Elev.

Initial Hyd. 1551 P.S.I Final Hyd. P.S.I.

First Initial Flow Pressure 16 P.S.I. Opened Tool 7:45 XXXX P.M.

First Final Flow Pressure P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 16 P.S.I. Initial Closed-in Pres. 30 Min.

Second Initial Flow Pressure 16 P.S.I. Second Flow Pres. 15 Min.

Second Final Flow Pressure P.S.I. Final Closed-in Pres. Min.

Final Closed-in Pressure P.S.I.

Blow VERY WEAK BLOW DEAD IN 4 MINUTES

Recovery 10' MUD

Remarks

Approved By RICHARD FOLEY Tester SMITH #013
