RJM Company
Wondra 'B' 5

8-17s-11w
15-009-25094

P.O. Box 138, Great Bend, Kansas 67530
(800) 792-6902

Company RJM Oil Company Inc
Address POBox 256 Claflin KS 67525
Lease & # Wondra B-5 Sec. 8 Twp 17 Rng 11w
Date 9 - 14 - 2007 County Barton Elevation 1910 G.L. _____ K.B.
Drilling Contractor Royal Drilling Inc
Drill Pipe Length 3309 I.D. of Drill Pipe 3.8 Tool Joint Size 4½ XH
Drill Collar Length _____ I.D. of Drill Collars 2.25 Tool Joint Size 4½ XH
Mud Weight 9.1 Viscosity 54 Filtrate 10.4 Chlorides-Pits 4,000 DST _____
Top Packer Depth 3323 Bottom Packer Depth 3328 Number of Packers 2
Tested From 3328 **to** 3371 **Total Depth** 3371 **Anchor Length** 43
Test # 1 **Formation Tested** _____ Hole Size 7 7/8
Initial Blow Strong Blow Bottom of Bucket in 5 min
Blow back on the 1st Shut-in No Blow Back
Final Blow Strong to Fair Blow Bottom of Bucket 7 min
Blow back on the 2nd Shut-in No Blow Back
Initial Hydrostatic 1672 P.S.I. **Final Hydrostatic** 1631 P.S.I. Maximum Temp. 108 F

Initial Opening	53 P.S.I. to 193 P.S.I.	from	12:41 Am	to	1:01 Am	30 minutes
Initial Shut-in	908 P.S.I.	from	1:01 Am	to	1:31 Am	30 minutes
Final Opening	206 P.S.I. to 278 P.S.I.	from	1:31 Am	to	2:41	30 minutes
Final Shut-in	899 P.S.I.	from	2:11 Am	to	2:56	45 minutes

Feet	Recovery Description	% Gas	% Oil	% Mud	% Water
470	Slightly Clean Gassy Oil	5	90	5	
180	Slightly mud cut Oil		80	20	

Total Feet Recovered 650 Recovery Chlorides — Rw. — ohms @ — Degrees
Gravity of oil 41 Corrected Gas to Surface in — minutes into the —
Max. Gas Gauged — MCF/day See Gas Flow Report Was a gas sample taken —
Comments —

Extra Equipment-Jars — Safety Joint — Circulating Sub _____ Straddle —
Electronic Recorder No. 3088 Depth 3367 Extra Packer (3rd) — Hook Wall —
Bottom Recorder No 47441 Depth 3368 Extra Packer (4th) — Sampler —
Tool Operator _____ Approved By _____

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902 — **DRILL STEM TEST REPORT** — GREAT BEND,KANSAS 67530

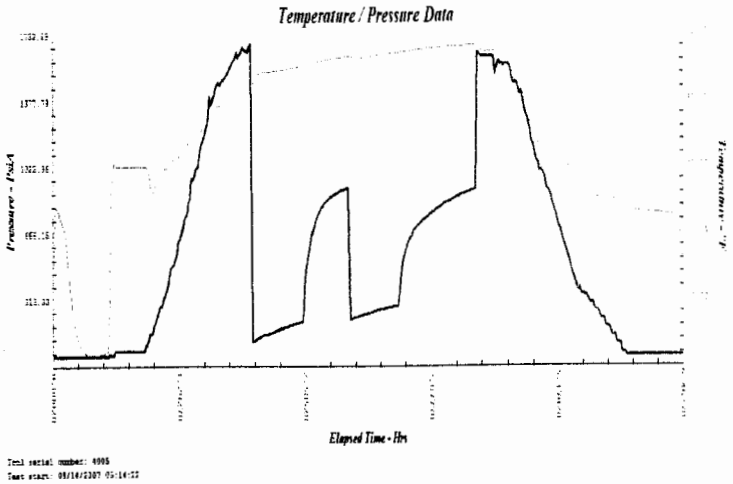

1	Initial Hydrostatic Pressure	1672
2	Initial Flow Pressure	83
3	Final Initial Flow Pressure	193
4	Initial Shut-In Pressure	908
5	Initial Final Flow Pressure	206
6	Final Flow Pressure	278
7	Final Shut-In Pressure	899
8	Final Hydrostatic Pressure	1631
	Maximum Temperature	108

GENERAL INFORMATION

COMPANY NAME	RJM OIL COMPANY INC		
TEST DATE	9/14/07	LEASE AND WELL NUMBER	WONDRA B-5
SECTION-TOWN-RANGE	40772	FORMATION TESTED	
STATE	KANSAS	DRILL STEM TEST NUMBER	1
COUNTY	BARTON	REPORT NUMBER	15098
ELEVATION GROUND LEVEL	1910	ELEVATION KELLY BUSHINGS	1916
COMPANY REPRESENTATIVE	JIM MUSGROVE	TESTING ENGINEER	JARED SCHECK

TOOL SETTING INFORMATION

		TOP PACKER DEPTH	3323
TEST INTERVAL (From)	3328	BOTTOM PACKER DEPTH	3328
TEST INTERVAL (to)	3328	NUMBER OF PACKERS	2
ANCHOR LENGTH	43	PACKER SIZE	6 3/4
TOTAL DEPTH (ft)	3328	HOLE SIZE	7 7/8

FLOW TIMES

INITIAL OPEN		FINAL OPEN	
TOOL OPEN (from)	12:41A	TOOL OPEN (from)	1:41
TOOL OPEN (to)	1:11	TOOL OPEN (to)	2:11
DURATION (min.)	30	DURATION (min.)	30
INITIAL SHUT-IN		**FINAL SHUT-IN**	
TOOL CLOSED (from)	1:11	TOOL CLOSED (from)	2:11
TOOL CLOSED (to)	1:41	TOOL CLOSED (to)	2:51
DURATION (min.)	30	DURATION (min.)	45

INITIAL FLOW STRONG BLOW BOTTOM OF BUCKET IN 5 MIN
NO BLOW BACK

FINAL FLOW STRONG TO FAIR BLOW BOTTOM OF BUCKET IN 7 MIN
NO BLOW BACK

Company: RJM OIL COMPANY INC Lease & Well No. WONDRA 5-B Test #: 1 Date: 9-14-07 SEC. 8 TWP. 17 RGE. 11

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	RJM OIL COMPANY INC		
TEST DATE	**9/14/07**	LEASE AND WELL NUMBER	**WONDRA B-5**
SECTION-TOWN-RANGE	**8/17/2011**	FORMATION TESTED	
STATE	**KANSAS**	DRILL STEM TEST NUMBER	1
COUNTY	**BARTON**	REPORT NUMBER	**15098**
ELEVATION GROUND LEVEL	**1910**	ELEVATION KELLY BUSHINGS	**1916**
COMPANY REPRESENTATIVE	**JIM MUSGROVE**	TESTING ENGINEER	**JARED SCHECK**

EXTRA EQUIPMENT

		EXTRA PACKER (3RD)	**NO**
JARS	**NO**	EXTRA PACKER (4TH)	**NO**
SAFETY JOINT	**NO**	STRADDLE	**NO**
ELECTRONIC RECORDER	**NO**	HOOK WALL	**NO**
CIRCULATING SUB	**NO**	SAMPLER	**NO**
	60 MILES ROUND TRIP FROM	**GREAT BEND**	
TOP RECORDER DEPTH	**3367**	BOTTOM RECORDER DEPTH	**3368**
RECORDER NUMBER	**4023**	RECORDER NUMBER	**3088**

WELL INFORMATION

DRILLING CONTRACTOR	**ROYAL DRILLING**		
DRILL PIPE LENGTH	**3309**	DRILL COLLAR LENGTH	
DRILL PIPE I.D.	**3.8**	DRILL COLLAR I.D.	**2.25**
TOOL JOINT SIZE	**4 1/2 X.H.**	TOOL JOINT SIZE	**4 1/2 X.H.**
CHLORIDES-PITS		MUD WEIGHT #/GAL	
CHLORIDES-DST		VISCOSITY	
		WATER LOSS	

COMMENTS

Superior Testers Enterprises L.L.C.

Drill Stem Test Report

Recovery Sample Description

1-800-792-6902 Great Bend,Kansas 67530

Drill Pipe	I.D.	Feet	Recovery Description For Drill Pipe	Gas	Oil	Mud	Water	Total bbls.
4 1/2	3.82							0.0000
		470	SLIGHTLEY CLEAN GASSY OIL	5%	90%	5%		6.6740
			SLIIGHTLEY MUD CUT OIL		80%	20%		0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
Drill Collars	I.D.		Recovery Description For Drill Collars	0.3337	6.0066	0.3337	0.0000	
	2.25							0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
Total Recovery		470	Feet					
			Total bbls. Recovered From Drill Pipe	0.3337	6.0066	0.3337	0.0000	Total
			Total bbls. Recovered From Drill Collars	0.0000	0.0000	0.0000	0.0000	bbls
			Total bbls Recovered	0.3337	6.0066	0.3337	0.0000	6.6740
				Gas	Oil	Mud	Water	
			Gravity of Oil Corrected					
MUD WEIGHT #/GAL		9.1	Resistivity		ohms @		Degrees	
VISCOSITY		54	Recovery Chlorides		ppm			
WATER LOSS		10.4	Pit Chlorides	4,000	ppm			
			4 1/2 inch Drill Pipe 3.83 I.D. Drill Collars 2.25 I.D					
			RJM OIL COMPANY INC WONDRA B-5 9-14-07 8-17-11W DST #1					

Temperature / Pressure Data

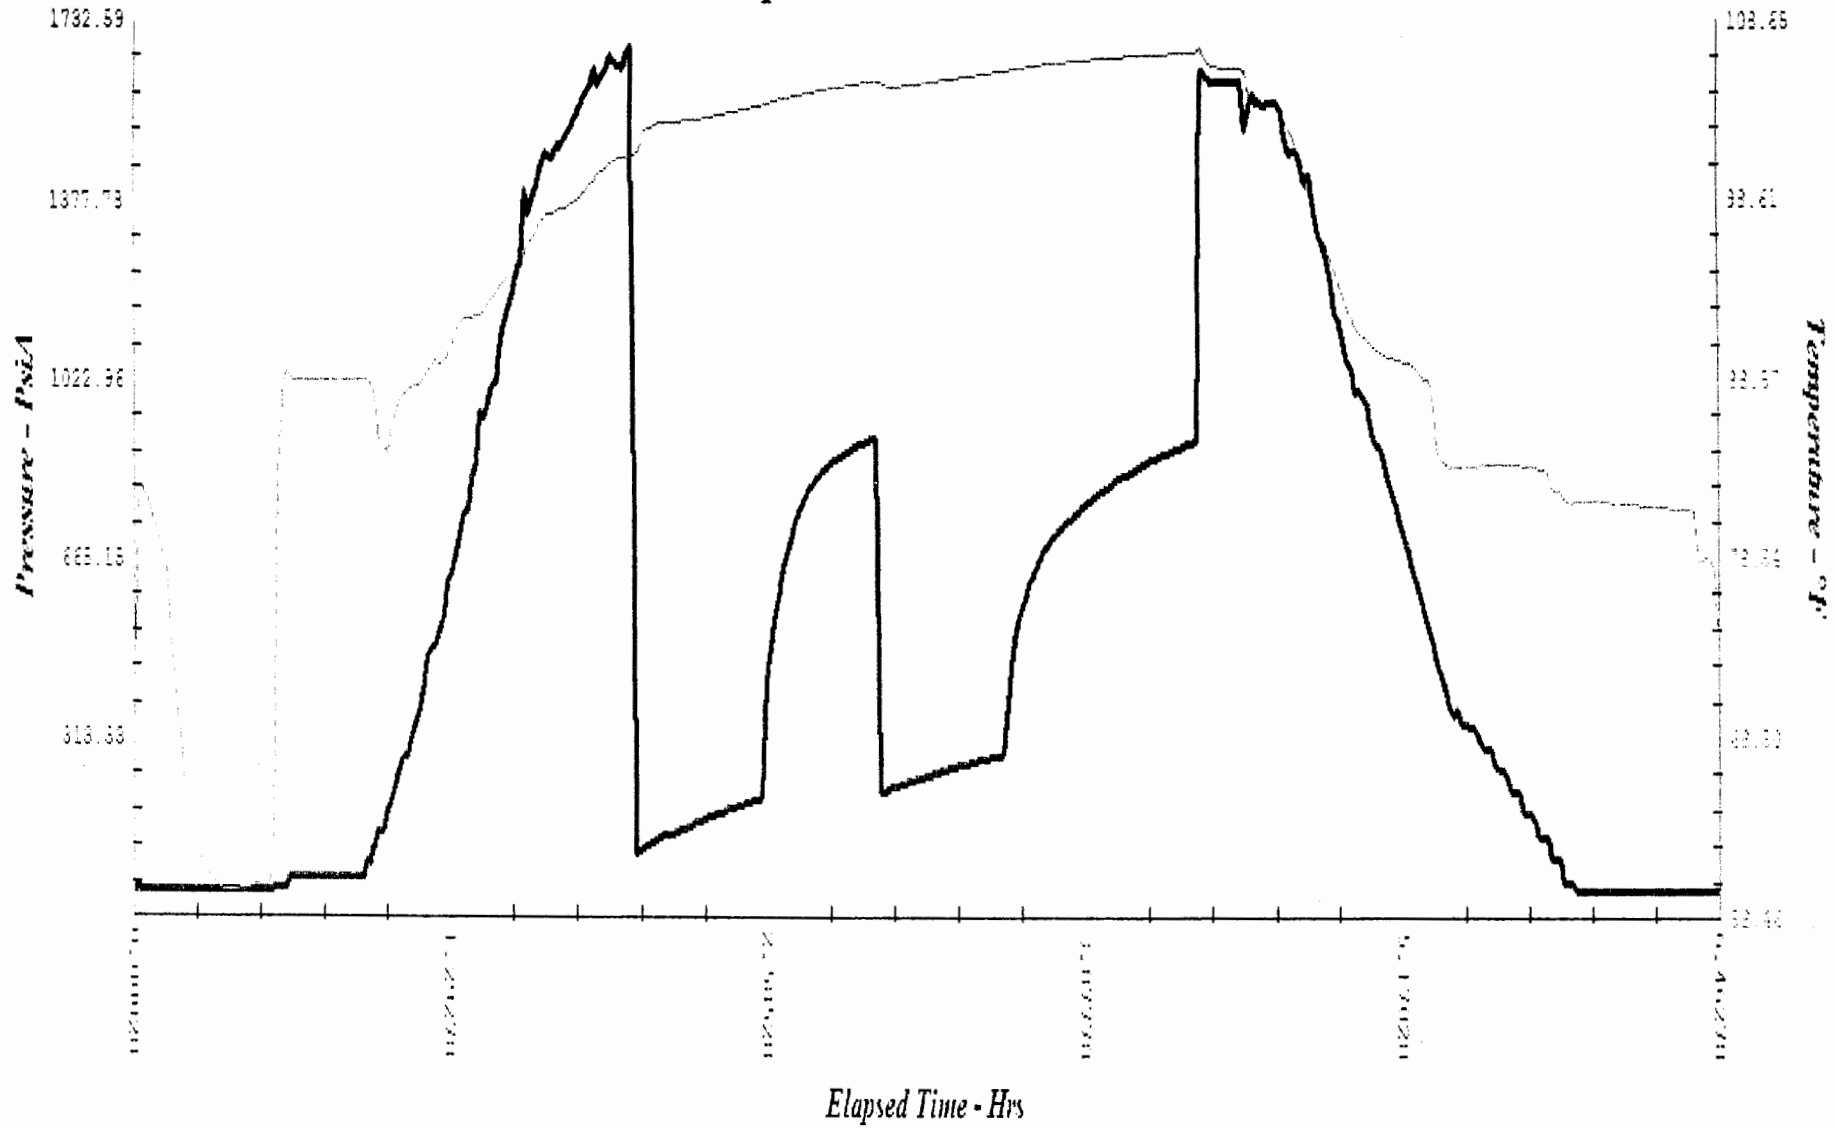

Tool serial number: 4006
Test start: 09/14/2007 08:14:22

RJM OIL COMPANY INC WONDRA B-5 9-14-07 8-17-11W DST #1
