DRILL STEM TEST REPORT

American Warrior Inc

Po box 399 Garden City KS, 67846

ATTN: Jason Alm

Bott #3-23

23-18S-21W

Job Ticket: 43865 **DST#: 1**

Test Start: 2011.06.14 @ 10:29:23

GENERAL INFORMATION:

Formation: **Cherokee Sand**
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 12:44:23
Time Test Ended: 15:36:23

Test Type: Conventional Bottom Hole
Tester: Cody Bloedorn
Unit No: 42

Interval: 4066.00 ft (KB) To 4090.00 ft (KB) (TVD)
Total Depth: 4090.00 ft (KB) (TVD)
Hole Diameter: 7.88 inches Hole Condition: Good


Reference Elevations: 2118.00 ft (KB)
2110.00 ft (CF)
KB to GR/CF: 8.00 ft

Serial #: 8700 **Outside**

Press@RunDepth: 17.10 psig @ 4067.00 ft (KB)
Start Date: 2011.06.14 End Date: 2011.06.14
Start Time: 10:29:28 End Time: 15:36:22

Capacity: 8000.00 psig
Last Calib.: 2011.06.14
Time On Btm: 2011.06.14 @ 12:43:53
Time Off Btm: 2011.06.14 @ 13:59:23

TEST COMMENT: 30 - IF- 1/4" blow , died in 11 Min
30 - ISI- No blow back
15 - FF- No blow back. PULLED TOOL
FSI- n/a

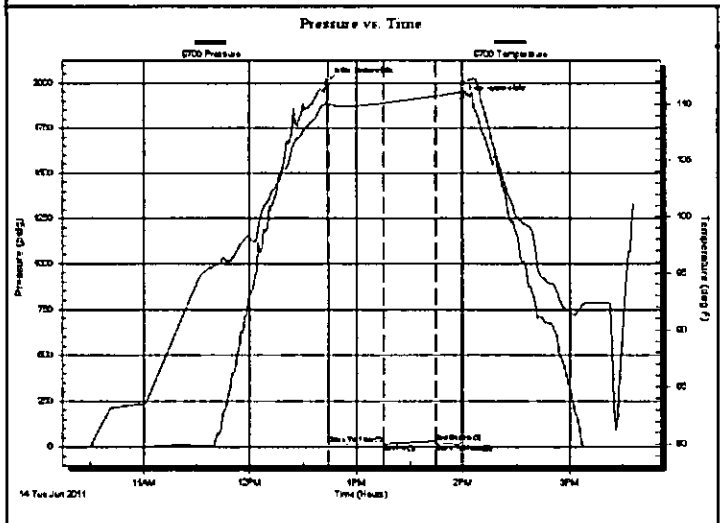

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2010.16	110.38	Initial Hydro-static
1	16.38	109.77	Open To Flow (1)
31	17.10	110.10	Shut-In(1)
61	30.08	110.72	End Shut-In(1)
61	17.68	110.71	Open To Flow (2)
75	18.23	111.06	Shut-In(2)
76	1910.01	112.29	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
1.00	1%O, 99%M	0.00

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)

TRILOBITE TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

American Warrior Inc

Po box 399 Garden City KS, 67846

ATTN: Jason Alm

Bott #3-23

23-18S-21W

Job Ticket: 43865 **DST#: 1**

Test Start: 2011.06.14 @ 10:29:23

Mud and Cushion Information

Mud Type:	Gel Chem	Cushion Type:		Oil API:	deg API
Mud Weight:	9.00 lb/gal	Cushion Length:	ft	Water Salinity:	ppm
Viscosity:	58.00 sec/qt	Cushion Volume:	bbl		
Water Loss:	6.40 in³	Gas Cushion Type:			
Resistivity:	ohm.m	Gas Cushion Pressure:	psig		
Salinity:	1700.00 ppm				
Filter Cake:	inches				

Recovery Information

Recovery Table


Length ft	Description	Volume bbl
1.00	1%O, 99%M	0.005

Total Length: 1.00 ft Total Volume: 0.005 bbl

Num Fluid Samples: 0 Num Gas Bombs: 0 Serial #:

Laboratory Name: Laboratory Location:

Recovery Comments: PULLED TOOL 15 MINUTES AFTER 2ND OPEN

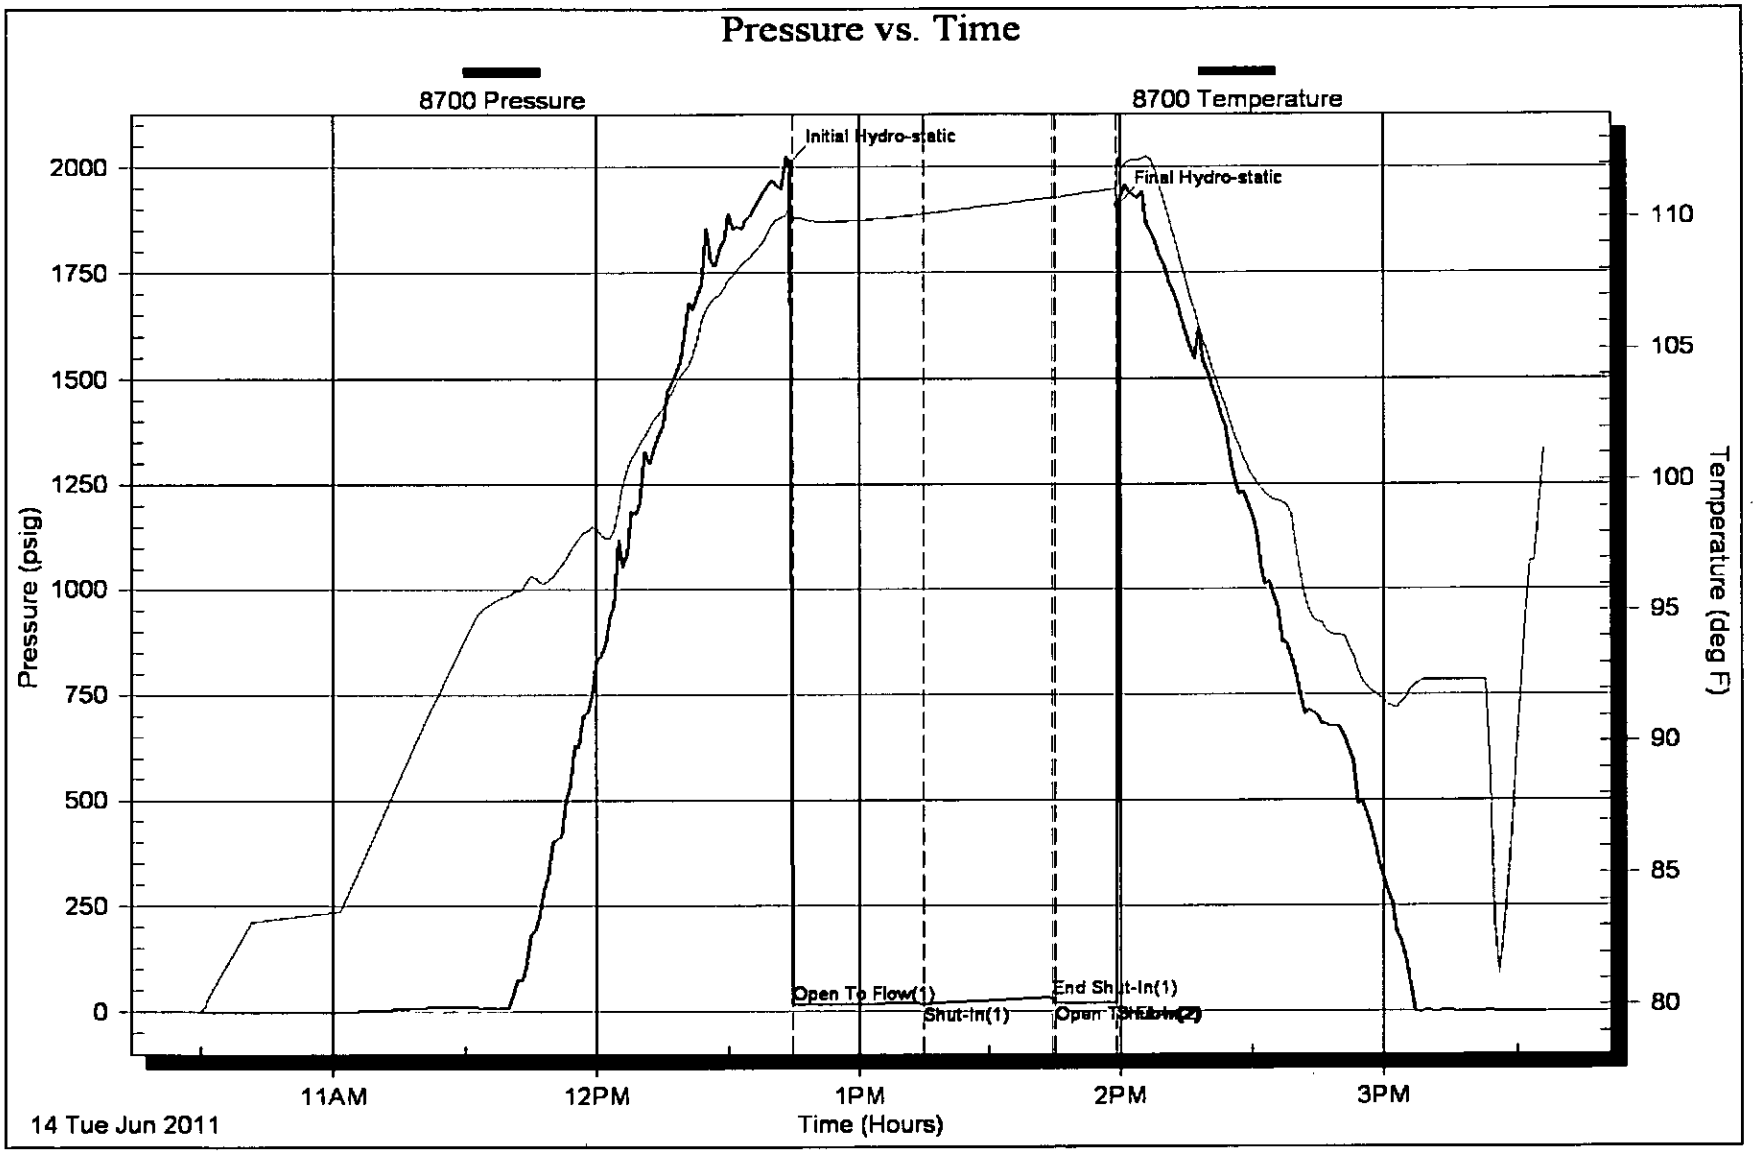
Pressure vs. Time
8700 Pressure
8700 Temperature
Initial Hydro-static
Final Hydro-static
Open To Flow(1)
Shut-In(1)
End Shut-In(1)
Pressure (psig)
Temperature (deg F)
2000
1750
1500
1250
1000
750
500
250
0
110
105
100
95
90
85
80
11AM
12PM
1PM
2PM
3PM
14 Tue Jun 2011
Time (Hours)

TRILOBITE TESTING INC.

P.O. Box 1733 • Hays, Kansas 67601

4/10

RECEIVED JUN 15 2011 BY:

Test Ticket

NO. 43865 15887

Well Name & No. Bott #3-23 Test No. 1 Date 6-14-11

Company American Warrior INC. Elevation 2118 KB 2110 GL

Address PoBox 399 Garden city, KS, 67846

Co. Rep / Geo. Jason Alm Rig Discovery #3

Location: Sec. 23 Twp. 18S Rge. 21W Co. Ness State KS

Interval Tested 4066 - 4090 Zone Tested Cherokee Sand

Anchor Length 24' Drill Pipe Run 4015 Mud Wt. 8.6

Top Packer Depth 4061 Drill Collars Run 31 Vis 58

Bottom Packer Depth 4066 Wt. Pipe Run — WL 6.4

Total Depth 4090 Chlorides 1700 ppm System LCM

Blow Description IF - 1/4" blow, died in 11 Min
ISI - No blow back, Pulled tool
FF - No blow back - 1/2
FSI - N/A

Rec 1	Feet of 150SM	%gas	%oil	%water	99	%mud
Rec	Feet of	%gas	%oil	%water		%mud
Rec	Feet of	%gas	%oil	%water		%mud
Rec	Feet of	%gas	%oil	%water		%mud
Rec	Feet of	%gas	%oil	%water		%mud

Rec Total ____ BHT ____ Gravity ____ API RW ____ @ ____ °F Chlorides ____ ppm

(A) Initial Hydrostatic 2010	☒ Test 1225	T-On Location 10:12 am	
(B) First Initial Flow 16	☒ Jars 250	T-Started 10:29 am	
(C) First Final Flow 17	☒ Safety Joint 75	T-Open 12:44 pm	
(D) Initial Shut-In 30	☐ Circ Sub	T-Pulled 1:59 pm	
(E) Second Initial Flow 17	☐ Hourly Standby	T-Out 3:37 pm	
(F) Second Final Flow —	☒ Mileage 112 RT 156.80	Comments	
(G) Final Shut-In —	☐ Sampler		
(H) Final Hydrostatic 1910	☐ Straddle	☐ Ruined Shale Packer	
	☐ Shale Packer	☐ Ruined Packer	
Initial Open 30	☐ Extra Packer	☐ Extra Copies	
Initial Shut-In 30	☐ Extra Recorder	Sub Total 0	
Final Flow 15	☐ Day Standby	Total 1706.80	
Final Shut-In N/A	☐ Accessibility	MP/DST Disc't	
	Sub Total 1706.80		

Approved By ____ Our Representative Cody Bloedorn

Trilobite Testing Inc. shall not be liable for damaged of any kind of the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test, tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

DRILL STEM TEST REPORT

American Warrior Inc

Po box 399 Garden City KS, 67846

ATTN: Jason Alm

Bott #3-23

23-18S-21W Ness

Job Ticket: 43866 **DST#: 2**

Test Start: 2011.06.14 @ 21:03:33

GENERAL INFORMATION:

Formation: **Cherokee "B" sand**
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 00:21:03
Time Test Ended: 03:00:03

Test Type: Conventional Bottom Hole
Tester: Cody Bloedorn
Unit No: 42


Interval: 4065.00 ft (KB) To 4120.00 ft (KB) (TVD)
Total Depth: 4120.00 ft (KB) (TVD)
Hole Diameter: 7.88 inches Hole Condition: Good

Reference Elevations: 2118.00 ft (KB)
2110.00 ft (CF)
KB to GR/CF: 8.00 ft

Serial #: 8700 **Outside**
Press@RunDepth: 184.45 psig @ 4104.00 ft (KB)
Start Date: 2011.06.14 End Date: 2011.06.15
Start Time: 21:03:38 End Time: 03:00:02

Capacity: 8000.00 psig
Last Calib.: 2011.06.15
Time On Btm: 2011.06.15 @ 00:20:33
Time Off Btm: 2011.06.15 @ 00:52:03

TEST COMMENT: 5 - IF- B.O.B. - 3 Min
10 - ISI- Weak surface blow
5 - FF- B.O.B. - 4 Min
10 - FSI- Very weak surface blow

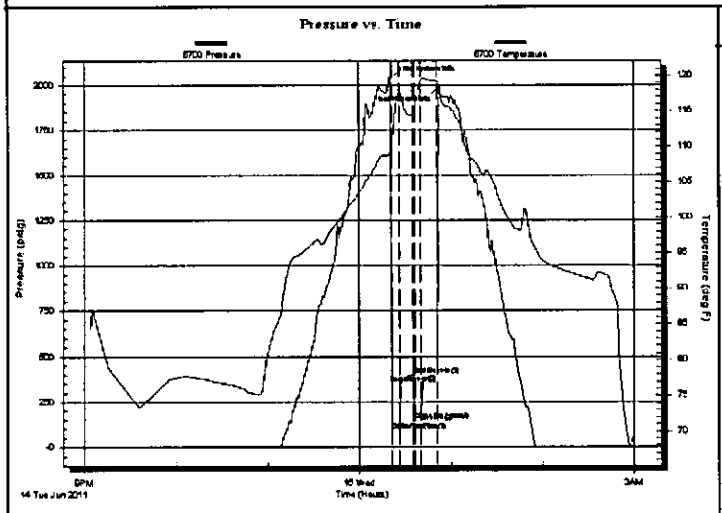

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2034.63	109.14	Initial Hydro-static
1	92.30	108.36	Open To Flow (1)
6	137.85	117.64	Shut-In(1)
15	397.02	114.54	End Shut-In(1)
16	148.56	114.74	Open To Flow (2)
20	184.45	119.11	Shut-In(2)
31	396.36	119.26	End Shut-In(2)
32	1987.21	119.01	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
310.00	30%W, 70%M with oil scum	4.07

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)

TRILOBITE TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

American Warrior Inc

Po box 399 Garden City KS, 67846

ATTN: Jason Alm

Bott #3-23

23-18S-21W Ness

Job Ticket: 43866 **DST#: 2**

Test Start: 2011.06.14 @ 21:03:33

Mud and Cushion Information

Mud Type:	Gel Chem	Cushion Type:		Oil API:	deg API
Mud Weight:	9.00 lb/gal	Cushion Length:	ft	Water Salinity:	ppm
Viscosity:	58.00 sec/qt	Cushion Volume:	bbl		
Water Loss:	6.39 in³	Gas Cushion Type:			
Resistivity:	ohm.m	Gas Cushion Pressure:	psig		
Salinity:	1700.00 ppm				
Filter Cake:	inches				

Recovery Information

Recovery Table


Length ft	Description	Volume bbl
310.00	30%W, 70%M with oil scum	4.066

Total Length: 310.00 ft Total Volume: 4.066 bbl

Num Fluid Samples: 0 Num Gas Bombs: 0 Serial #:

Laboratory Name: Laboratory Location:

Recovery Comments:

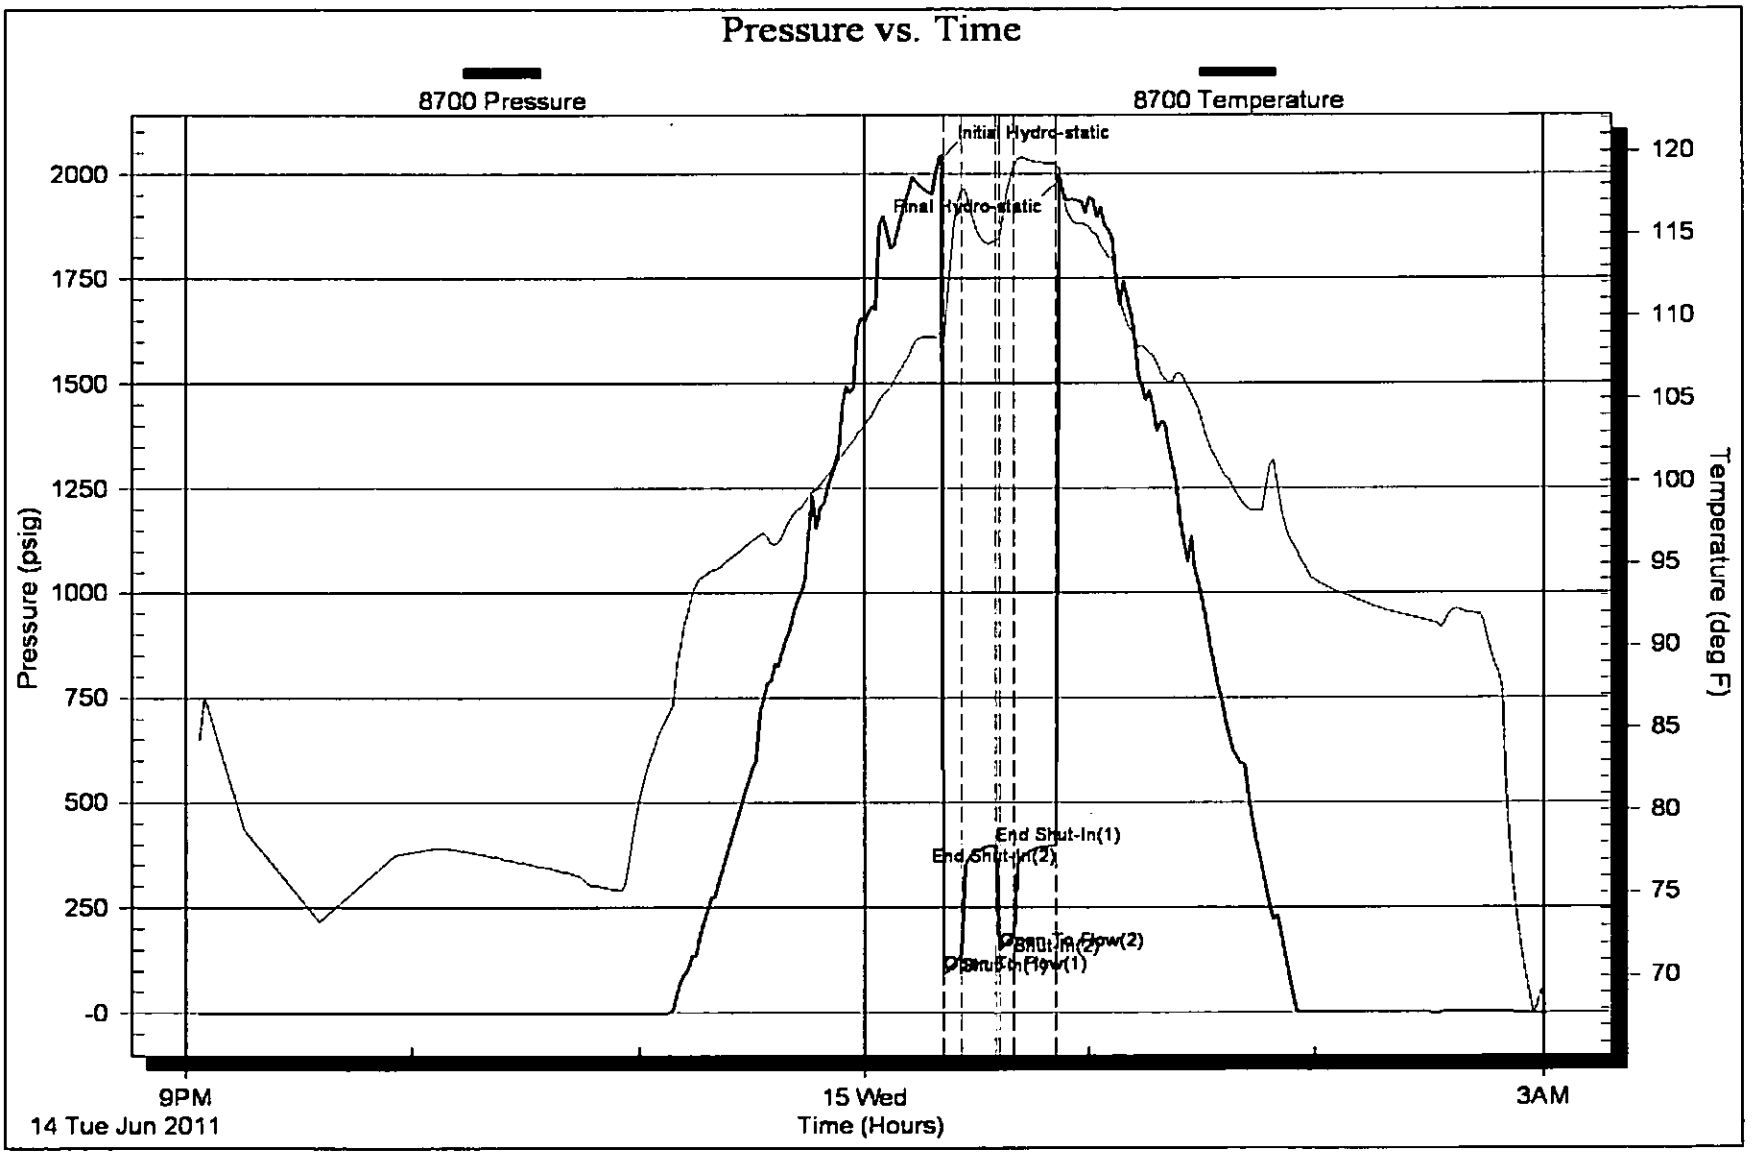
Pressure vs. Time
8700 Pressure
8700 Temperature
Initial Hydro-static
Final Hydro-static
End Shut-In(1)
End Shut-In(2)
Pressure (psig)
Temperature (deg F)
2000
1750
1500
1250
1000
750
500
250
-0
120
115
110
105
100
95
90
85
80
75
70
9PM
14 Tue Jun 2011
15 Wed
Time (Hours)
3AM

TRILOBITE TESTING INC.

P.O. Box 1733 • Hays, Kansas 67601

4/10

JUN 15 2011

BY

Test Ticket

NO. 43866

Well Name & No. Bott #3-23 Test No. 2 Date 6-14-11

Company American Warrior Inc, Elevation 2118 KB 2110 GL

Address Po Box 399 Garden City KS, 67846

Co. Rep / Geo. Jason Alm Rig Discovery #3

Location: Sec. 23 Twp. 18S Rge. 21W Co. Ness State KS

Interval Tested 4065-4120 Zone Tested Cherokee "B" Sand

Anchor Length 55' Drill Pipe Run 4015' Mud Wt. 8.6

Top Packer Depth 4060 Drill Collars Run 31' Vis 58

Bottom Packer Depth 4065 Wt. Pipe Run — WL 6.4

Total Depth 4120 Chlorides 1700 ppm System LCM

Blow Description IF- B.O.B. - 3 Min
ISI- Surface blow
FF- B.O.B. - 4 Min
FSI- Very weak surface blow

Rec 310	Feet of MW with oil scum	%gas	%oil 30	%water 70	%mud
Rec	Feet of	%gas	%oil	%water	%mud
Rec	Feet of	%gas	%oil	%water	%mud
Rec	Feet of	%gas	%oil	%water	%mud
Rec	Feet of	%gas	%oil	%water	%mud

Rec Total 310 BHT 119 Gravity ____ API RW ____ @ ____ °F Chlorides ____ ppm

(A) Initial Hydrostatic	2034	☒ Test 1225	T-On Location 8:48 pm
(B) First Initial Flow	92	☒ Jars 250	T-Started 9:03 pm
(C) First Final Flow	137	☒ Safety Joint 75	T-Open 12:21 am
(D) Initial Shut-In	397	☐ Circ Sub	T-Pulled 12:51 am
(E) Second Initial Flow	148	☐ Hourly Standby	T-Out 3:01 am
(F) Second Final Flow	184	☒ Mileage 112RT 150.80	Comments
(G) Final Shut-In	396	☐ Sampler	
(H) Final Hydrostatic	1987	☐ Straddle	☐ Ruined Shale Packer
		☐ Shale Packer	☐ Ruined Packer
Initial Open	5	☐ Extra Packer	☐ Extra Copies
Initial Shut-In	10	☐ Extra Recorder	Sub Total 8
Final Flow	5	☐ Day Standby	Total 1706.80
Final Shut-In	10	☐ Accessibility	MP/DST Disc't
		Sub Total 1706.80	

Approved By ____ Our Representative Cody Bloedorn

Trilobite Testing Inc. shall not be liable for damaged of any kind of the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test, tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.
