25-20s-35w

ORIGINAL

DRILL-STEM TEST DATA

15-203-20120

Computer Inventoried

Well Name:	BRACK #1				
Company :	ABERCROMBIE DRILLING				
Location - Sec:	25	**Twp:**	20S	**Rge:**	35W
County:	WICHITA	**State:**	KS		
Date:	06/06/95				

K C C

MAY 1 3 1996

TRILOBITE TESTING L.L.C.

OPERATOR : ABERCROMBIE DRILLING DATE 06/05/95
WELL NAME: BRACK #1 KB 3152.00 ft TICKET NO: 8113 DST #1
LOCATION : 25-20S-35W GR 3147.00 ft FORMATION: MARMATON
INTERVAL : 4516.00 To 4530.00 ft TD 4530.00 ft TEST TYPE: CONVENTIONAL

RECORDER DATA

Mins		Field	1	2	3	4
PF 30	Rec.	11058	11058	11057		
SI 45	Range(Psi)	4500.0	4500.0	4500.0	0.0	0.0
SF 60	Clock(hrs)	7452	7452	21048		
FS 45	Depth(ft)	4520.0	4520.0	4525.0	0.0	0.0

TIME DATA----------
PF Fr. 30 to hr
IS Fr. 45 to hr
SF Fr. to 1 hr
FS Fr. 45 to hr

	Field	1	2	3	4
A. Init Hydro	2221.0	2221.0	0.0	0.0	0.0
B. First Flow	33.0	28.0	0.0	0.0	0.0
B1. Final Flow	33.0	28.0	0.0	0.0	0.0
C. In Shut-in	647.0	633.0	0.0	0.0	0.0
D. Init Flow	33.0	28.0	0.0	0.0	0.0
E. Final Flow	33.0	28.0	0.0	0.0	0.0
F. Fl Shut-in	613.0	601.0	0.0	0.0	0.0
G. Final Hydro	2199.0	2201.0	0.0	0.0	0.0
Inside/Outside	I	I	O		

T STARTED hr
T ON BOTM hr
T OPEN 1600 hr
T PULLED 1900 hr
T OUT hr

RECOVERY
Tot Fluid 60.00 ft of 0.00 ft in DC and 60.00 ft in DP
60.00 ft of GAS IN PIPE
5.00 ft of FREE OIL - 100% OIL
25.00 ft of OIL CUT MUD - 10% OIL, 90% MUD
30.00 ft of SLIGHTLY OIL CUT MUD - 2% OIL, 98% MUD
0.00 ft of
0.00 ft of
0.00 ft of
RW 1.1 @ 70 F
SALINITY 5600.00 P.P.M. A.P.I. Gravity 32.00

BLOW DESCRIPTION
INITIAL BLOW -
SURFACE BLOW BUILT TO 1"

INITIAL SHUTIN -
NO RETURN BLOW

FINAL BLOW -
BUBBLE TO OPEN TOOL, NO BLOW, BLOW IN
20 MIN BUILT TO 1/2"

FINAL SHUTIN -
NO RETURN BLOW

SAMPLES:
SENT TO:

TOOL DATA----------


Tool Wt.	0.00 lbs
Wt Set On Packer	0.00 lbs
Wt Pulled Loose	0.00 lbs
Initial Str Wt	0.00 lbs
Unseated Str Wt	0.00 lbs
Bot Choke	0.75 in
Hole Size	7.88 in
D Col. ID	0.00 in
D. Pipe ID	3.80 in
D.C. Length	0.00 ft
D.P. Length	0.00 ft
H.W. I.D	2.70 in
H.W. Length	320.00 ft

MUD DATA----------

Mud Type	CHEMICAL
Weight	9.20 lb/
Vis.	42.00 S/L
W.L.	11.20 in3
F.C.	0.00 in
Mud Drop	
Amt. of fill	0.00 ft
Btm. H. Temp.	112.00 F
Hole Condition	
% Porosity	0.00
Packer Size	6.75 in
No. of Packers	2
Cushion Amt.	0.00
Cushion Type	
Reversed Out	
Tool Chased	
Tester	SHANE MCBRIDE
Co. Rep.	STEVE DAVIS
Contr.	ABERCROMBIE
Rig #	4
Unit #	
Pump T.	

Test Successful: Y

CHART PAGE

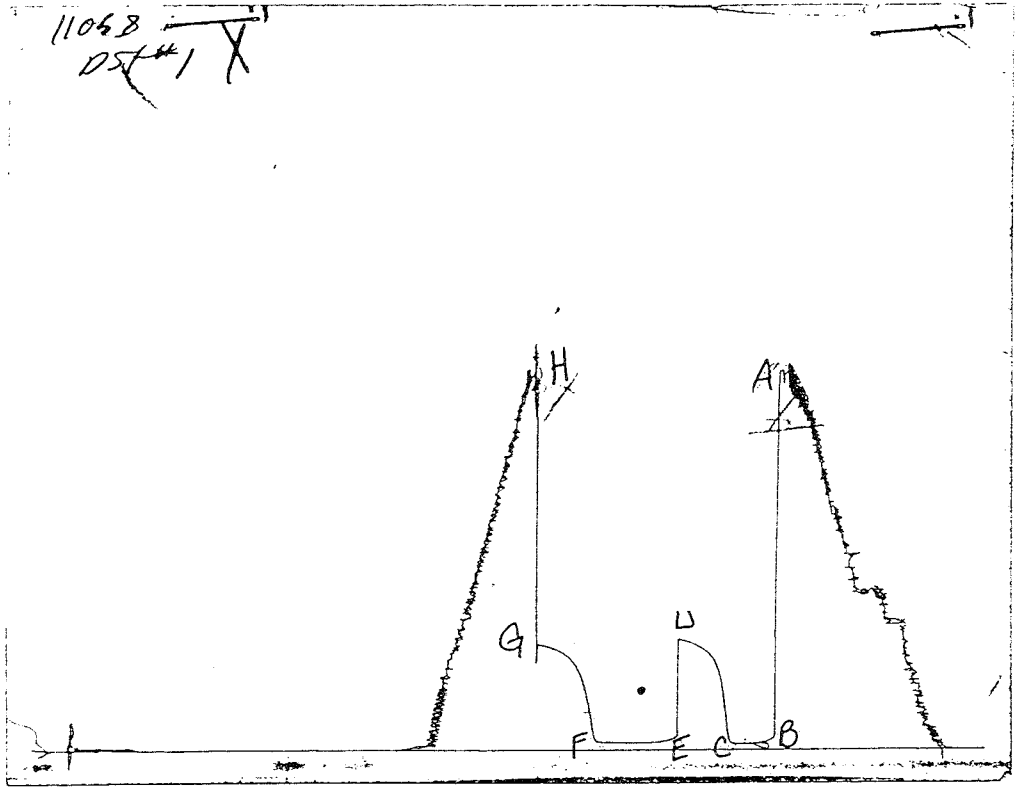

This is an actual photograph of an AK1 recorder chart


CALCULATED RECOVERY ANALYSIS WEIGHT PIPE

DST # 1 TICKET # 8113

****

SAMPLE #	TOTAL FEET	GAS %	GAS FEET	OIL %	OIL FEET	WATER %	WATER FEET	MUD %	MUD FEET
1	5		0	100	5		0		0
2	25		0	10	2.5		0	90	22.5
3	30		0	2	0.6		0	98	29.4
4			0		0		0		0
5			0		0		0		0
TOTAL	60	0	0	13.5	8.1	0	0	86.5	51.9

			HRS OPE	BBL/DAY
BBL OIL=	0.0567	*	1.50	0.9072
BBL WAT	0	*		0
BBL MUD	0.3633			
BBL GAS	0			

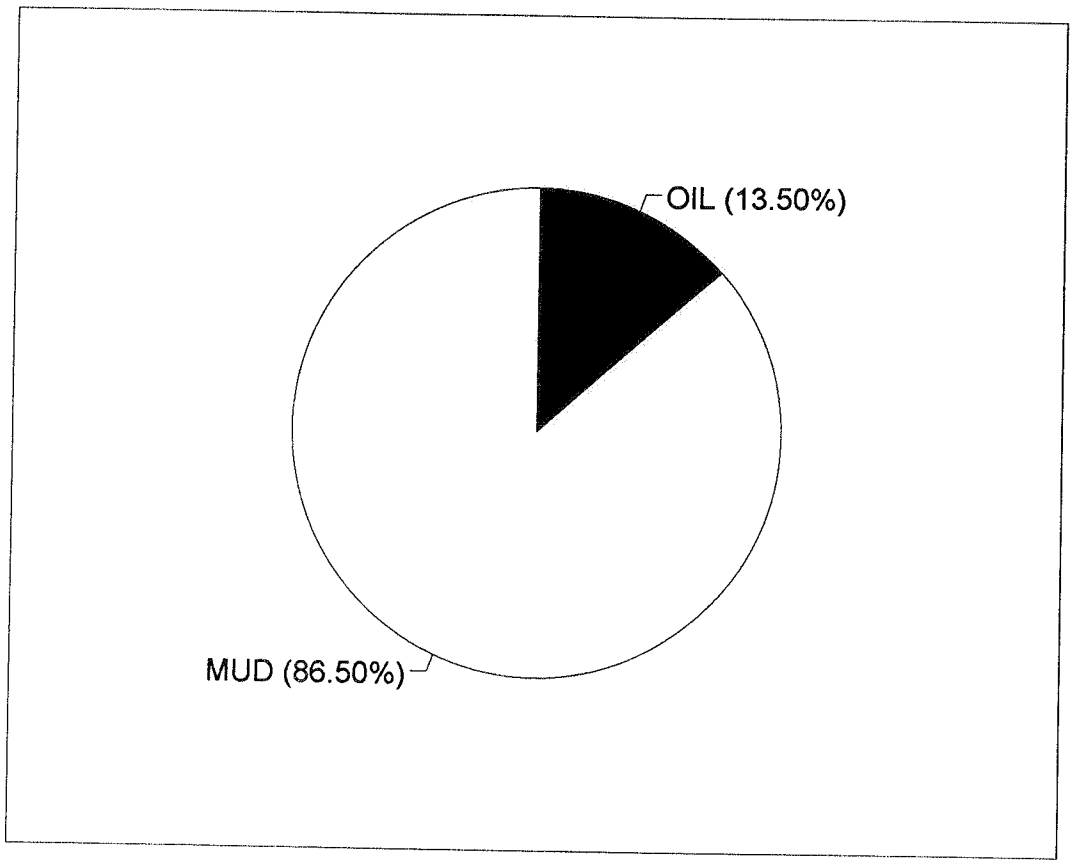

TRILOBITE TESTING L.L.C.

ORIGINAL

OPERATOR : ABERCROMBIE DRILLING DATE 06/06/95
WELL NAME: BRACK #1 KB 3152.00 ft TICKET NO: 8114 DST #2
LOCATION : 25-20S-35W GR 3147.00 ft FORMATION: MARMATON
INTERVAL : 4530.00 To 4538.00 ft TD 4538.00 ft TEST TYPE: CONVENTIONAL

RECORDER DATA

Mins			Field	1	2	3	4
PF	30	Rec.	11058	11058	11057		
SI	45	Range(Psi)	4500.0	4500.0	4500.0	0.0	0.0
SF	30	Clock(hrs)	7452	7452	21048		
FS	45	Depth(ft)	4535.0	4535.0	4531.0	0.0	0.0

TIME DATA----------
PF Fr. 30 to hr
IS Fr. 45 to hr
SF Fr. 30 to hr
FS Fr. 45 to hr

	Field	1	2	3	4
A. Init Hydro	2233.0	2244.0	0.0	0.0	0.0
B. First Flow	22.0	18.0	0.0	0.0	0.0
B1. Final Flow	22.0	18.0	0.0	0.0	0.0
C. In Shut-in	669.0	665.0	0.0	0.0	0.0
D. Init Flow	33.0	36.0	0.0	0.0	0.0
E. Final Flow	22.0	19.0	0.0	0.0	0.0
F. Fl Shut-in	669.0	655.0	0.0	0.0	0.0
G. Final Hydro	2177.0	2182.0	0.0	0.0	0.0
Inside/Outside	O	O	I		

T STARTED hr
T ON BOTM hr
T OPEN 0552 hr
T PULLED 0822 hr
T OUT hr

RECOVERY
Tot Fluid 15.00 ft of 0.00 ft in DC and 15.00 ft in DP
15.00 ft of MUD CUT WATER - 76% WATER, 24% MUD
0.00 ft of
0.00 ft of
0.00 ft of
0.00 ft of
0.00 ft of
0.00 ft of
RW .507 @ 70 F
SALINITY 11500.00 P.P.M. A.P.I. Gravity 0.00

BLOW DESCRIPTION
INITIAL BLOW -
SURFACE BLOW BUILT TO 1/2"

INITIAL SHUTIN -
NO RETURN BLOW

FINAL BLOW -
BUBBLE TO OPEN TOOL, NO BLOW

FINAL SHUTIN -
NO RETURN BLOW

SAMPLES:
SENT TO:

TOOL DATA----------


Tool Wt.	0.00 lbs
Wt Set On Packer	0.00 lbs
Wt Pulled Loose	0.00 lbs
Initial Str Wt	0.00 lbs
Unseated Str Wt	0.00 lbs
Bot Choke	0.75 in
Hole Size	7.88 in
D Col. ID	5.00 in
D. Pipe ID	3.80 in
D.C. Length	0.00 ft
D.P. Length	0.00 ft
H.W. I.D	2.70 in
H.W. Length	320.00 ft

MUD DATA----------

Mud Type	CHEMICAL
Weight	9.20 lb/cf
Vis.	42.00 S/L
W.L.	11.20 in3
F.C.	0.00 in
Mud Drop	
Amt. of fill	0.00 ft
Btm. H. Temp.	112.00 F
Hole Condition	
% Porosity	0.00
Packer Size	6.75 in
No. of Packers	2
Cushion Amt.	0.00
Cushion Type	
Reversed Out	
Tool Chased	
Tester	SHANE MCBRIDE
Co. Rep.	STEVE DAVIS
Contr.	ABERCROMBIE
Rig #	4
Unit #	
Pump T.	

Test Successful: Y

CHART PAGE

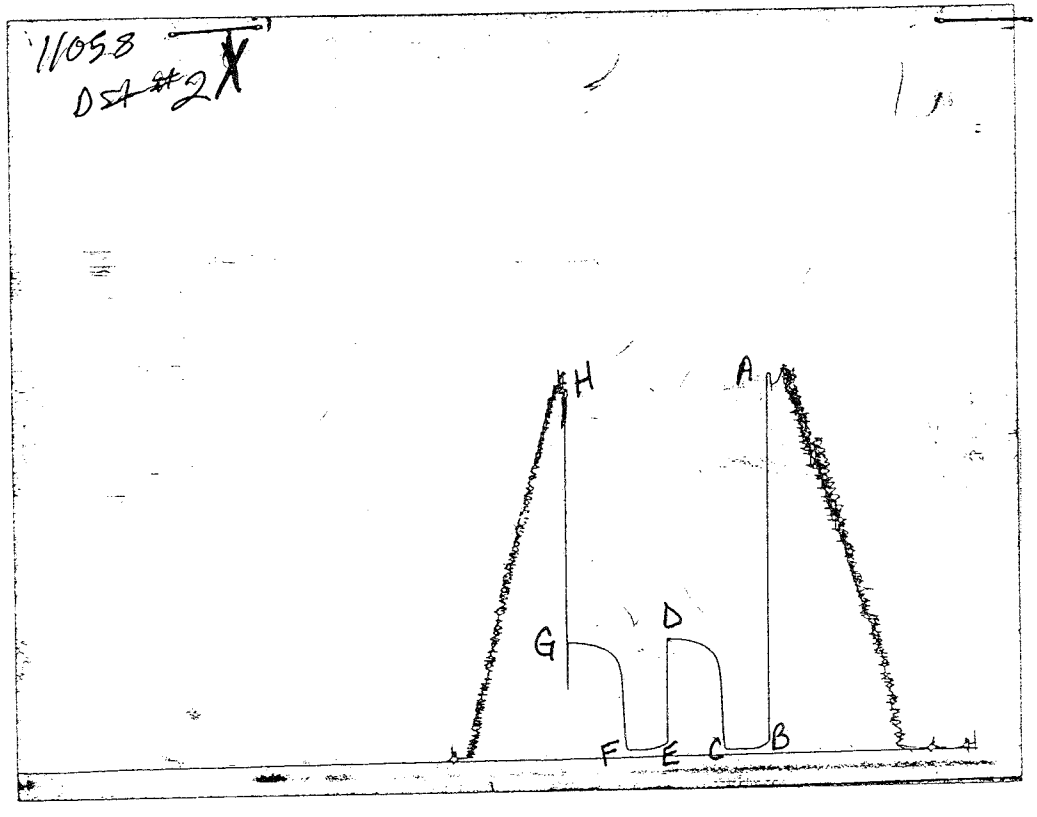

This is an actual photograph of an AK1 recorder chart

22222
