Sun Oil Well Cementing, Inc. **DRILL STEM TEST DATA**

P.O. Box 169 Great Bend, Kansas 67530

Lease	Clark-Welty	Date	11/29/75
Well No.	1		
County	Hodgeman	Elevation	2240 K. B.
Sec.	27		
Twp.	22	Test No.	1
Rng.	21		
Company	Larry G. Stephenson & Co. Inc.	Zone Tested	Miss
Contractor	Red Tiger Drilling Company	Ticket #	1917Tx
Charge To	Larry G. Stephenson & Co. Inc.	Tester	Blake
Approved By	Bob Hammond		

Initial Hydro Mud Press. 2449 P.S.I.

Initial Flow Press. 23 To 23 P.S.I. Initial Flow Period 30 Min.

Initial Shut-in Press. 40 P.S.I. Initial Shut-in 45 Min.

Final Flow Press. 23 To 23 P.S.I. Final Flow Period 30 Min.

Final Shut-in Press. 31 P.S.I. Final Shut-in 45 Min.

Final Hydro Mud Press. 2438 P.S.I. TIME TOOL OPEN

Temperature 113 Deg.

Mud Weight 9.5 Viscosity 39

Fluid Loss 7.6

Interval Tested 4434 To 4466

Top Packer Depth 4429 Surface Choke Size

Bottom Packer Depth 4434 Bottom Choke Size 5/8

Total Depth 4466 Main Hole Size 7 7/8

Drill Pipe Size 4½ Wt Rubber Size 6 3/4

Drill Collar I.D. Ft. Run

Blow Weak for 19 Min.

Recovery 20'Mud

Sun Oil Well Cementing, Inc. **DRILL STEM TEST DATA**

P.O. Box 169 Great Bend, Kansas 67530

Lease	Clark-Welty	Date	11/30/75
Well No.	1		
County	Hodgeman	Elevation	2240 K. B.
Sec.	27		
Twp.	22	Test No.	2
Rng.	21		
Company	Larry C. Stephenson & Company	Zone Tested	Miss
Contractor	Red Tiger Drilling		
Charge To	Larry C. Stephenson & Company Inc.	Ticket #	1918Tx
Approved By	Bob Hammond	Tester	Blake

Initial Hydro Mud Press. 2422 P.S.I.

Initial Flow Press. 74 To 67 P.S.I. Initial Flow Period 30 Min.

Initial Shut-in Press. 1247 P.S.I. Initial Shut-in 45 Min.

Final Flow Press. 72 To 70 P.S.I. Final Flow Period 90 Min.

Final Shut-in Press. 1059 P.S.I. Final Shut-in 45 Min.

Final Hydro Mud Press. 2418 P.S.I. TIME TOOL OPEN

Temperature 119 Deg.

Mud Weight 9.7 Viscosity 46

Fluid Loss 10.8

Interval Tested 4465 To 4475

Top Packer Depth 4460 Surface Choke Size

Bottom Packer Depth 4465 Bottom Choke Size 5/8

Total Depth 4475 Main Hole Size 7 7/8

Drill Pipe Size 4½ Wt Rubber Size 6 3/4

Drill Collar I.D. Ft. Run

Blow Weak on I. F. P. Weak intermitten on F. F. P.

Recovery 90' Watery Mud

Remarks: top trcorder clock Stopped

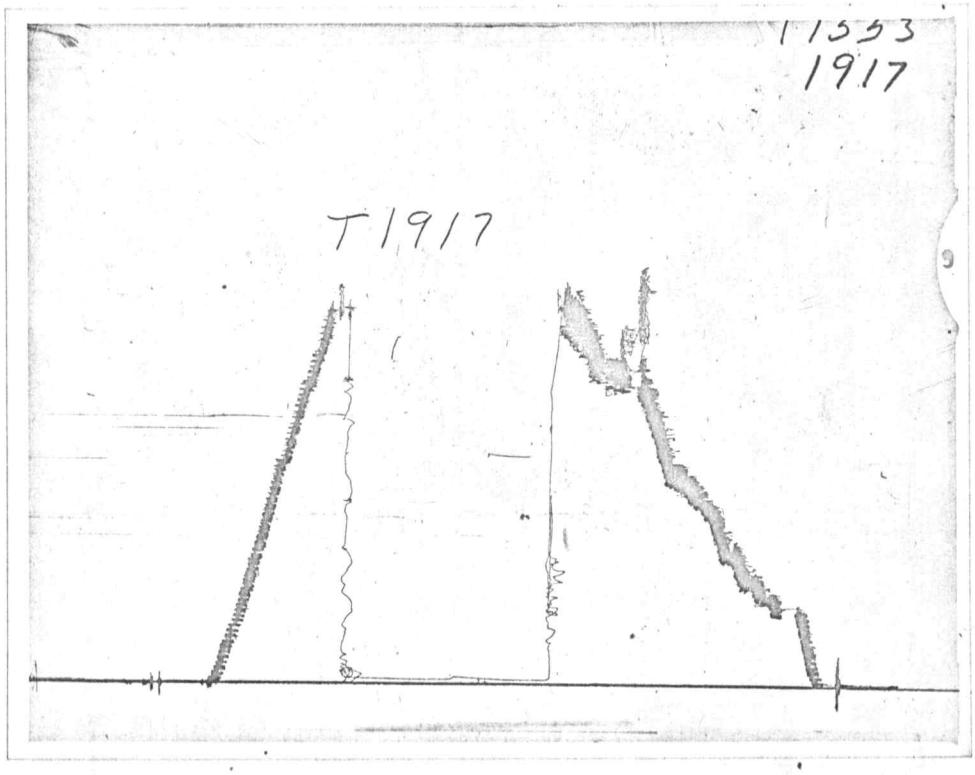

BOTTOM

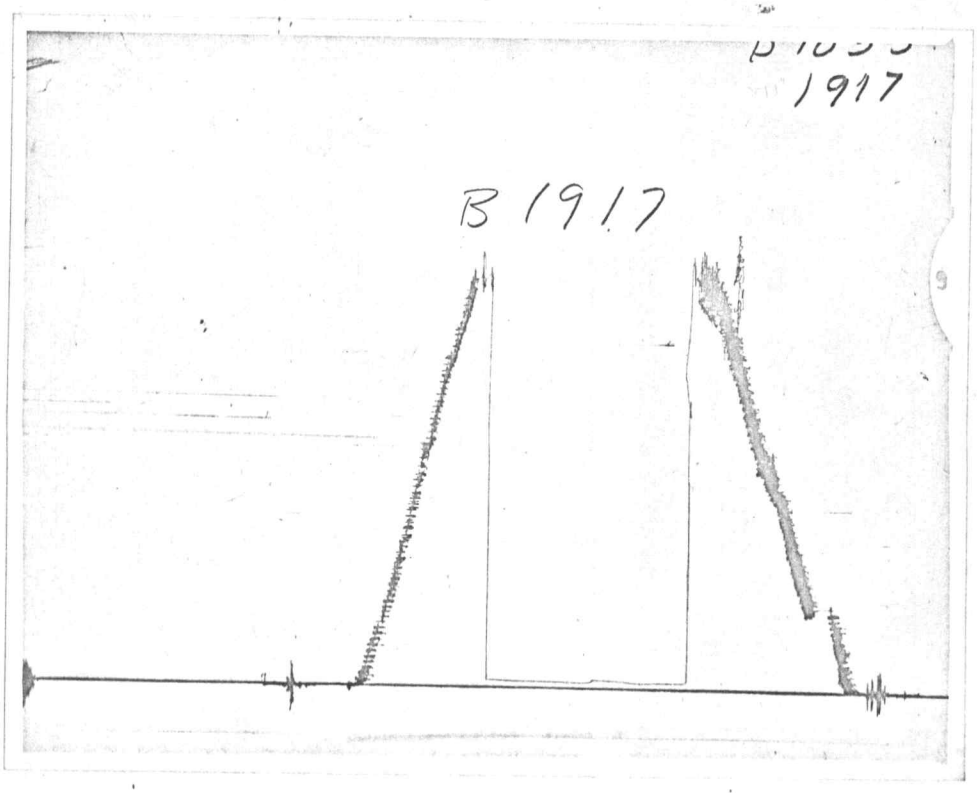

TOP

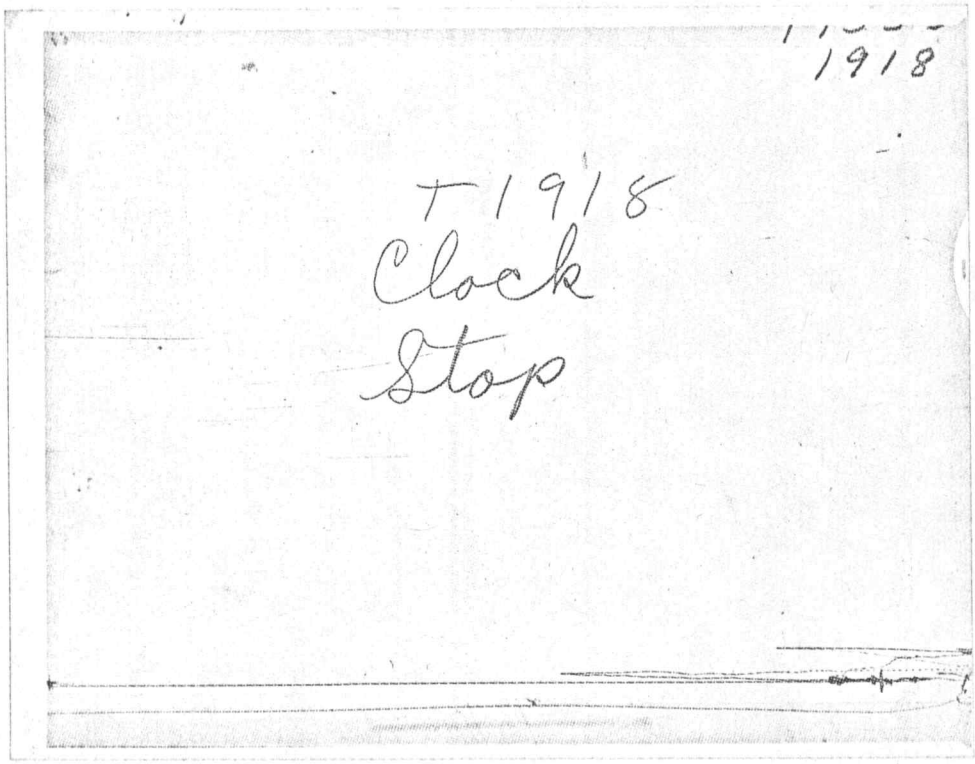
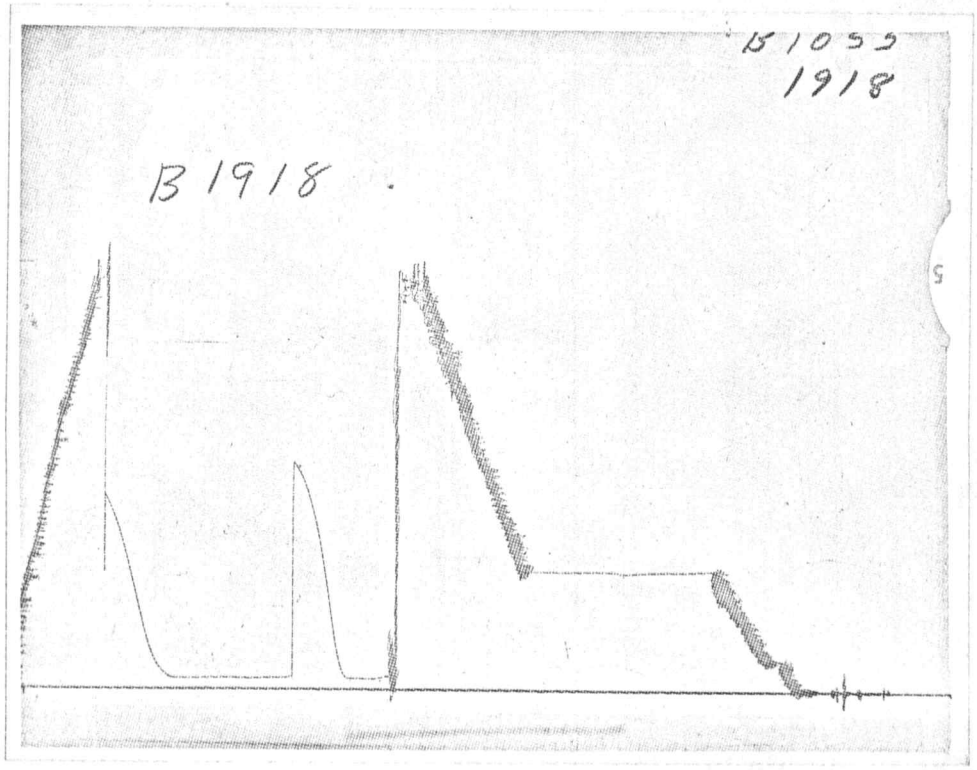
BOTTOM
