Home Office: Great Bend, Kansas
P. O. Box 393 GLadstone 3-7903

COMPANY GULF OIL CORPORATION WELL Albright #1
DATE November 7, 1956 COUNTY Kingman STATE Kansas
TEST NO. #1 TICKET NO. 6483-K TYPE TEST Open-hole (Conventional)
TEST APPROVED BY T. Terrel WESTERN REPRESENTATIVE Ernest Luckert

TEST DATA:

Tested From 4174' To 4214' Depth 4214'
Hydrostatic Mud Pressure—Initial (A) 2370# Final (E) 2355#
Flow Pressure—Initial (B) 65# Final (C) 65#
Bottom Hole Pressure—Initial (F) 1660# Final (D) 835#
Tool Open 1 Hr. - Min.; Shut-in-Initial - Hr. 20 Min.; Shut-in-Final - Hr. 30 Min.
Chokes; Surface 3/4" Bottom 1/2" Fluid Cushion: Type None Amount
Recovery:

160' Slightly gas cut drilling mud

SURFACE DATA:

BLOW: Good blow, decreasing. Gas to surface in 55 minutes.

Maximum Surface Pressure Did Well Flow? No

Description of Flow	Time	Max. Pressure	Size Surface Choke


GENERAL OPERATIONAL DATA:

Hole Size: Main Hole 7-7/8" Rat Hole Drill Pipe Size 4½" F. H.
Hole Condition Good Mud Weight 9.8# Viscosity 46
Type Pressure Recorder Western Recorder No. 23 & 24 Date Calib. 7-26-56
Extra Equipment: Dual Packer No Jars No Safety Joint No
Was Test Recovery Reversed Out? No Bottom Hole Temperature 109°
Number of Copies Requested

REMARKS:

W. L. - 13.8 C.C.

Elev. - 1564 K.B.

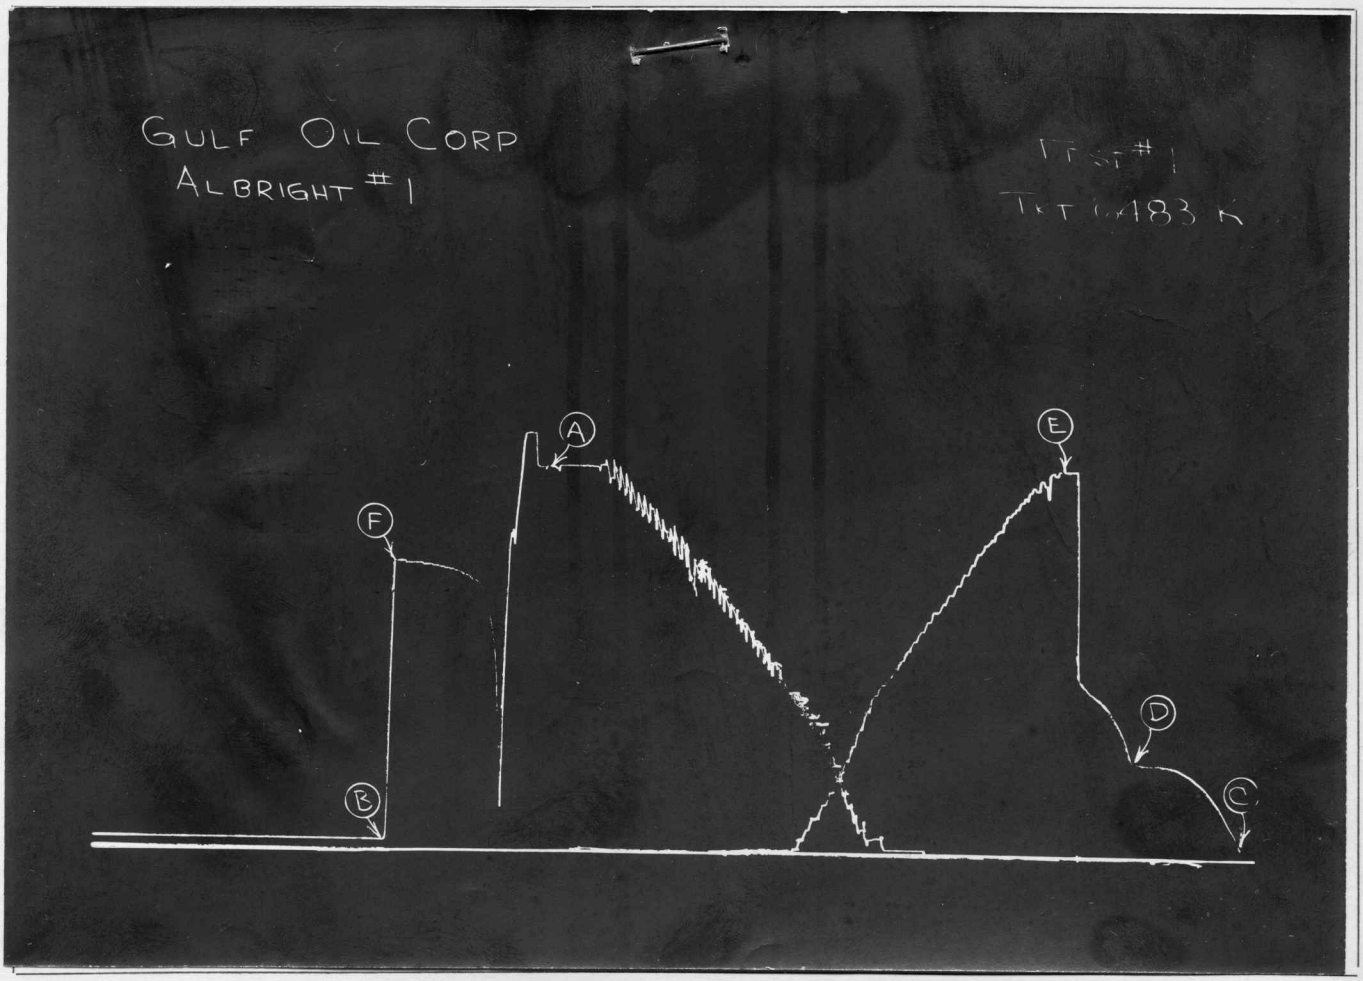

This is an actual photograph of recorder chart.

PRESSURE DATA		Point	Pressure
(A) Initial Hydrostatic Mud	2370#		
(B) Initial Flow	65#		
(C) Final Flow	65#		
(D) Final Shut-In	835#		
(E) Final Hydrostatic Mud	2355#		
(F) Initial Shut-In	1660#		

ELI ALBRIGHT	1	2	GULF OIL CORPORATION	PRATT
LEASE	WELL NO.	TEST NO.	COMPANY	DISTRICT

Halliburton
OIL WELL CEMENTING CO.

LOCATION	SEC. 36-29-8
FIELD	Spivey
COUNTY	Kingman
STATE	Kansas
CONTRACTOR	Lewis Drlg. Co.

MUD DATA

Kind	Starch
Weight	10 lbs.-gal.
Viscosity	53 Sec.
Filter Loss	7.2 c. c. Filter Cake 2/32 in.
Est. Gauge Depth Temp.	Calc. 110 F°
Tool Open	60 minutes
Time Closed In.	30 minutes
Depth Top Gauge	3842' Ft.
BT. P. R. D. No.	196 Blanked Off No
12 Hr. Clock No.	2798

Pressure Readings	Field	Office Corrected
Initial Hydro Mud Pressure		2238
Initial Flow. Pres.		35
Final Flow Pres.		35
Closed in Pres.		35
Final Hydro Mud Pressure		2238

HOLE & TOOL DATA

Total Depth	4215'	Casing Perforations Top	-
		Bottom	-
Top Packer Depth	3867'	Bottom Packer Depth	3885'
Casing or Hole Size	7 7/8"	Liner or Rathole Size	-
Formation Tested	Kansas City		
Size Drill Pipe	4½" API FH	Size Drill Collars	6"
Size Bottom Choke	3/4"	Size Surface Choke	1"
Size Hook Wall Packer	-	Size Rings -	No. Rings -
Size & Type Wall Packer	6 3/4" ESWP		No. Packers 2
Size & Length Anchor	5" x 18' + 330'		
Depth Bottom Gauge	3847' Ft.	Amount of Cushion	None
BT. P. R. D. No.	536 Blanked Off		
12 Hr. Clock No.	2232		

Field	Office Corrected
	2229 p.s.i.
	25 p.s.i.
	25 p.s.i.
	25 p.s.i.
	2229 p.s.i.

Date	11-9-56
Ticket No.	67034
HOWCO DISTRICT	Pratt
Kind of Job	Straddle Test
Price	$226.00
Second Packer Assembly	79.00
Safety Joint	-
Extra Folder Charge	-
HOWCO Jars	100.00
Total	$405.00
Witnessed By	Mr. T. Terrel
Tester	R. C. Kuhn

REMARKS: Interval tested 3867' to 3885' in the Kansas City. Tool opened @ 9:33 A. M. with a weak blow and continued throughout the test, closed in pressure taken @ 10:33 A. M., and started off bottom @ 11:13 A. M. Recovered 5' of drilling mud.


All depths measured from Kelly Bushing

No. Folders Reproduced 5

HOWCO No. 1102-A (Printed in U. S. A.)—Southwestern—4808E

Top Recorder

TIME

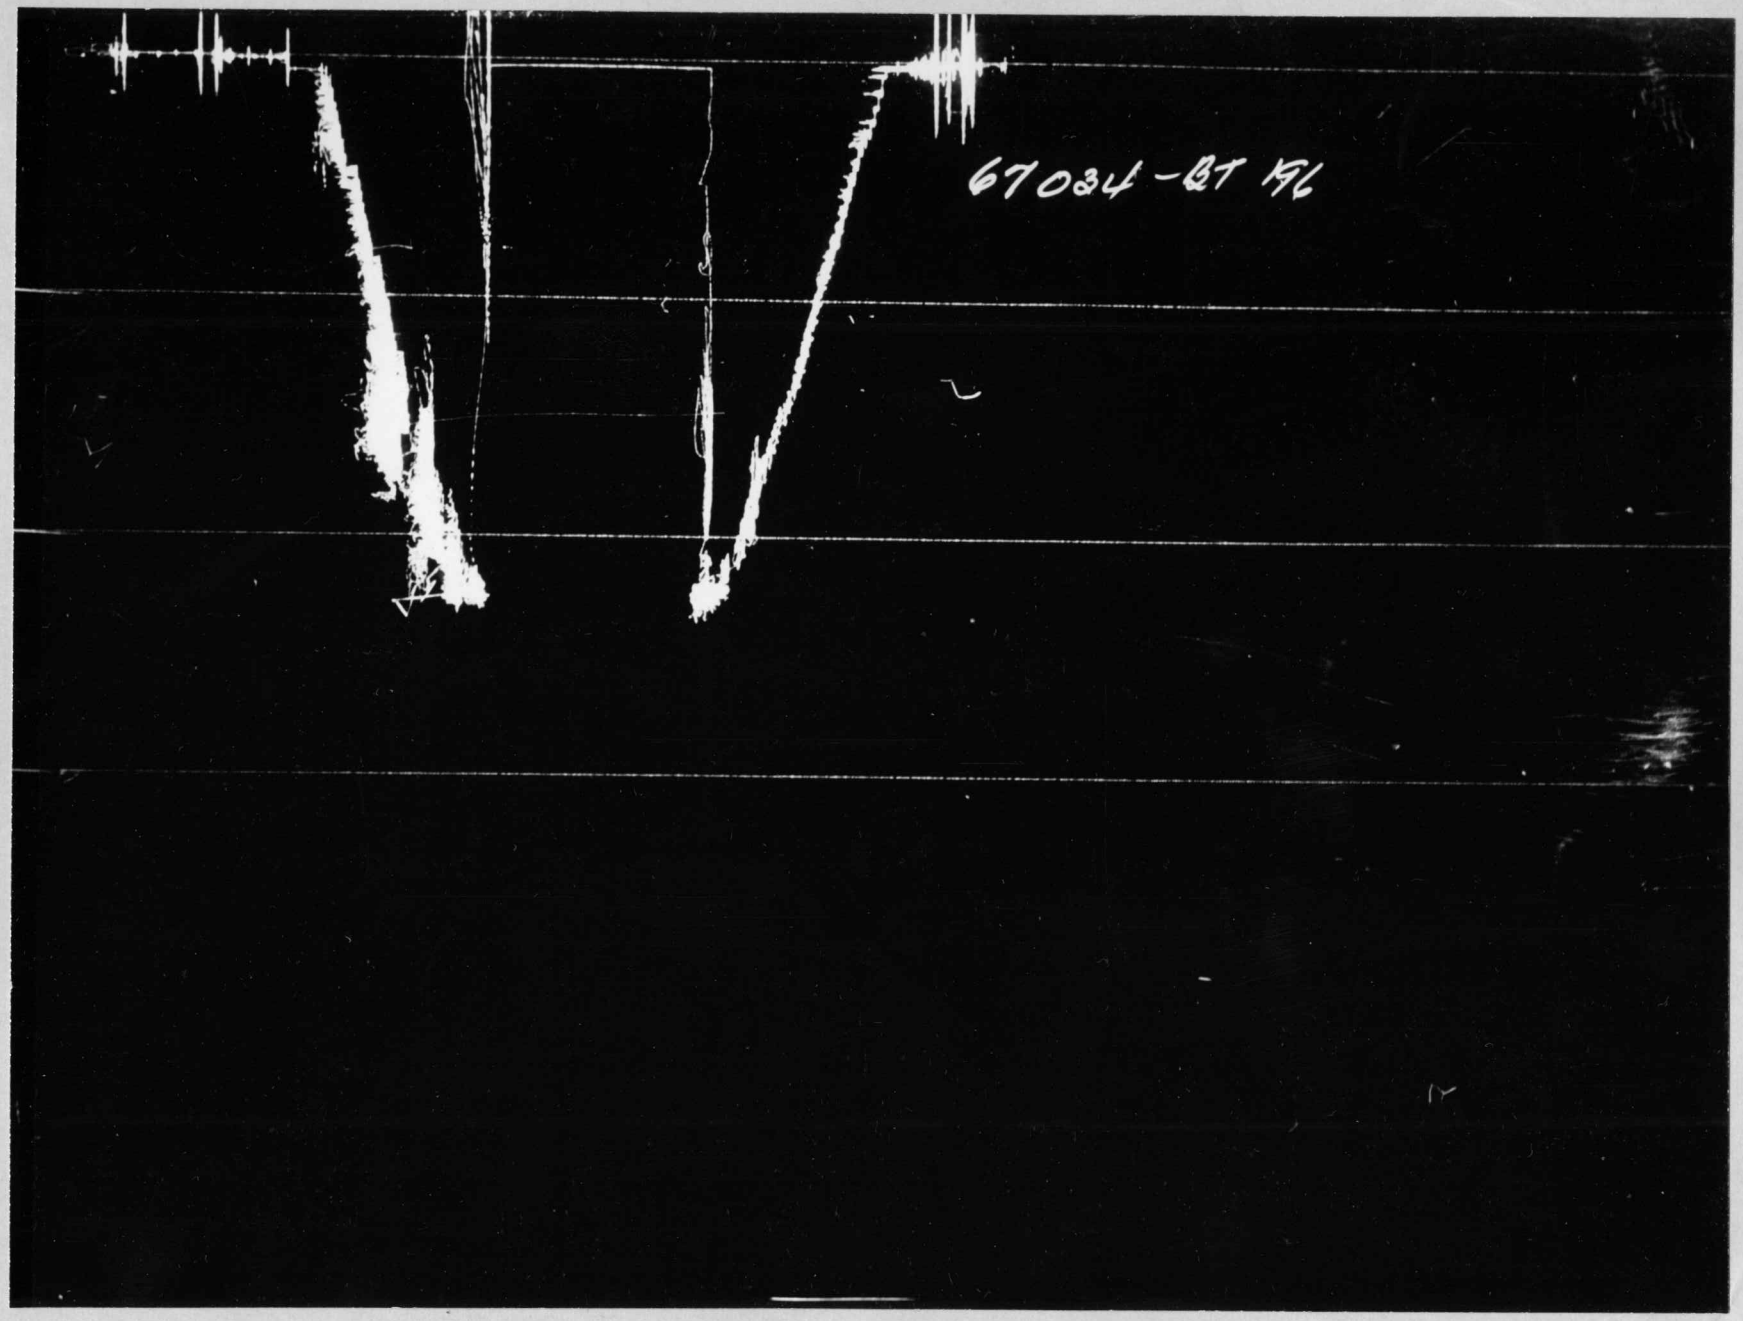


PRESSURE

Each Horizontal Line Equal to 1000 p.s.i.

LEASE | WELL NO. | TEST NO. | COMPANY | DISTRICT


Bottom Recorder


TIME

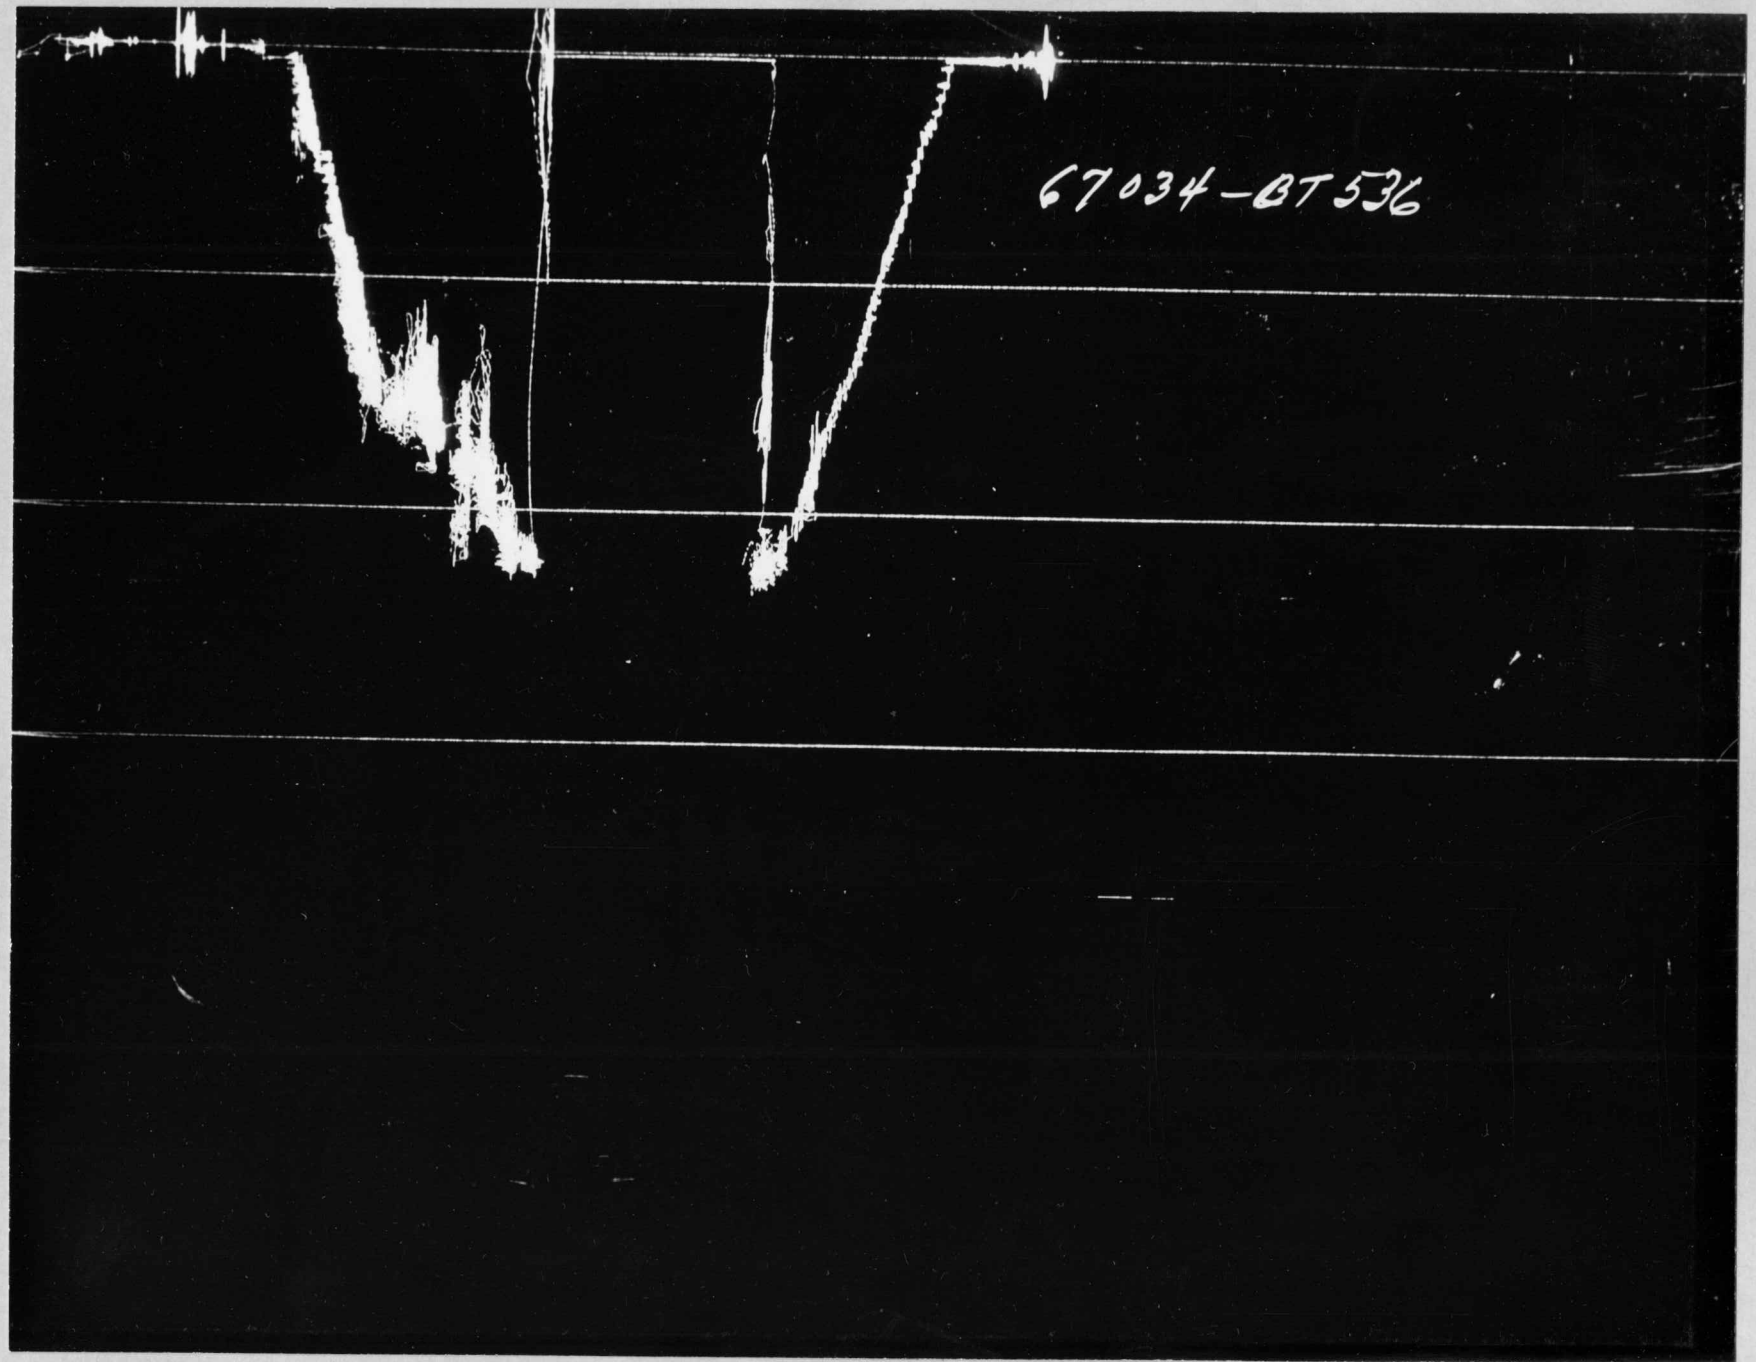

PRESSURE

Each Horizontal Line Equal to 1000 p.s.i.

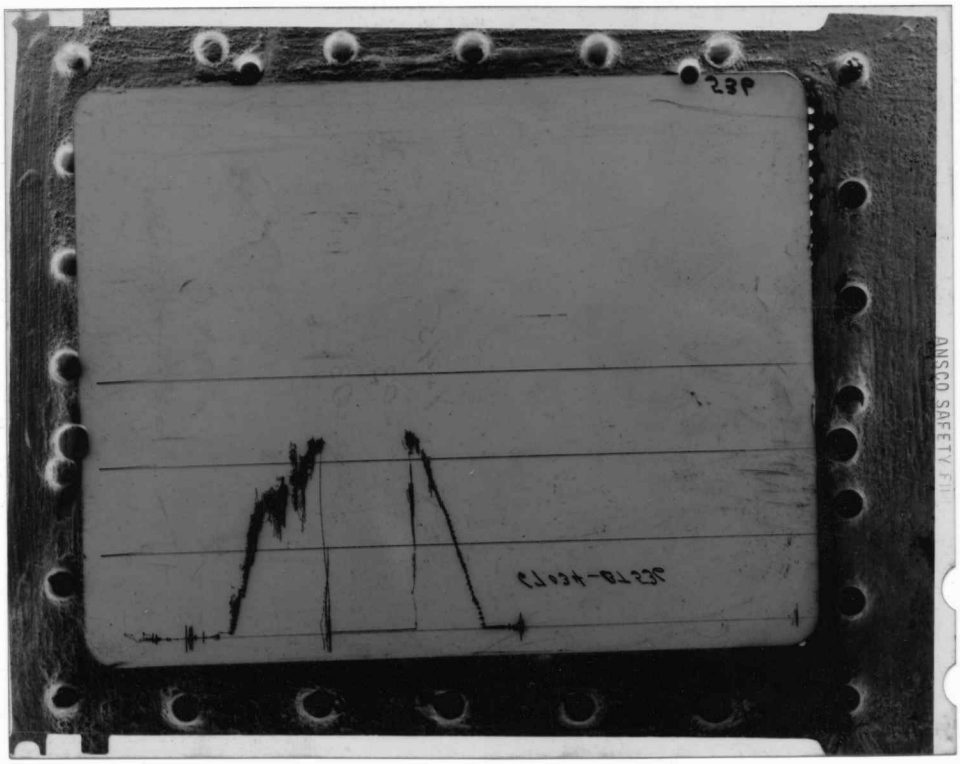
23P
ANSCO SAFETY FILM

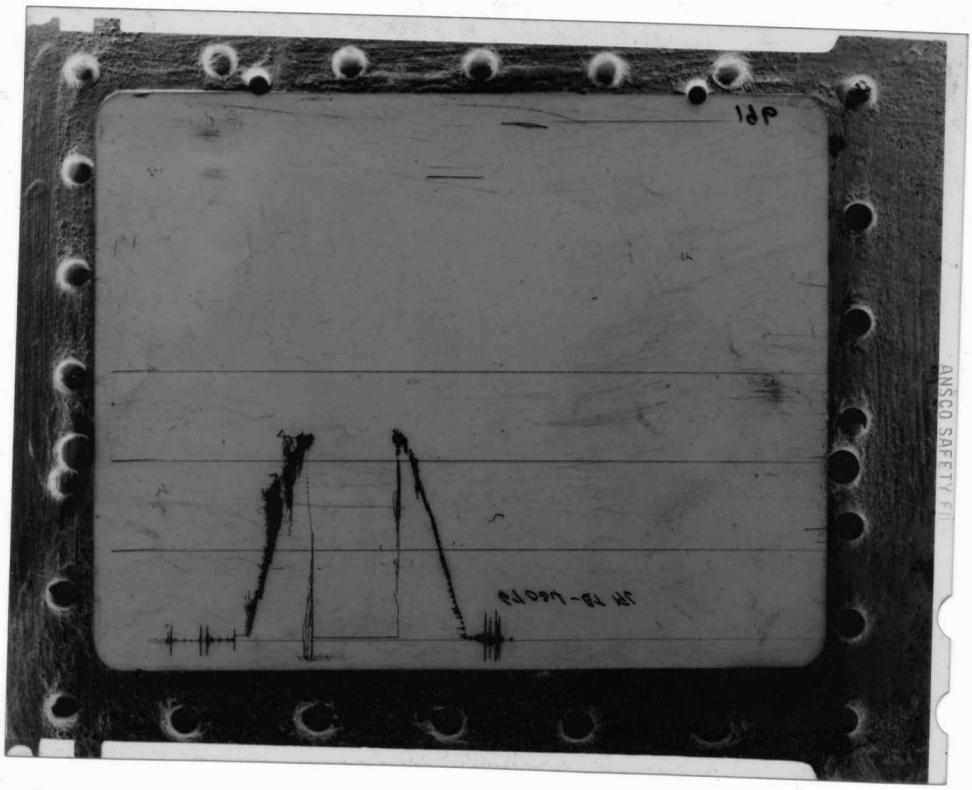
18P
ANSCO SAFETY FILM
