State Kansas County Barber

Company Messman-Rinehart Oil Co. Well No. 1

Farm T. L. Welsh "A"

Survey

Block No. Sec. 7 Twp. 32 S Range 15 W

Co-Ord. Elev. 1887' K/B

NE SW SE

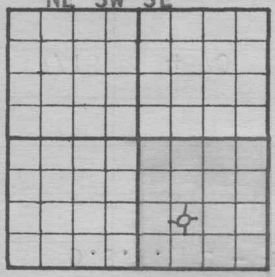

M-R Rig

50% - A. A. Seeligson, Jr.
25% - Chicago Group
25% - M-R Oil Co.

4950' Miss. test

NOTE: Show Sketch of Lease and Well Location in Above Space

Ft. from N. Line 990 Ft. from S. Line

990 Ft. from W. Line Ft. from E. Line

Date	Depth	
7/1/60		M.I.R.T.
7/2		10-3/4" @ 200' w/185 sx. cem.
		4 gel., 4 c.c., P.D. @ 10:00
		a.m. 7/2/60, WOC
7/3		WOC
7/4	2040	Drlg. (#2 bit @ 2040)
7/5	2470	Drlg. (#3 bit @ 2343)
7/6	2810	Drlg. (#4 bit @ 2575)
7/7	3215	Drlg. (#5 bit @ 2900)

13-13-S

Date	Depth	
7/8	3510	Drlg. (#6 bit @ 3302)
	4003	Heebner (-2116)
7/11	4250	Drlg. (#8 @ 3970) (#9 @ 4199)
	4156	Lansing (-2269)
7/12	4380	Drlg. (#10 @ 4355)
7/13	4448	Shut down for clutch rep.
7/14		(To start up about noon)
7/15	4541	Drlg. (On #12 bit)
7/18	4855	Drlg. (waiting on log truck)
	4716	Miss. (-2829)
D.S.T. #1 - 4711-46 - Op 1 hr., Rec. 5' mud, BHP 50-15#, FP 10-10#		
D.S.T. #2 - 4746-4870 - Op 1 hr., wk. bl. Rec. 50' mud, BHP (30") 1025-95#, FP 35-50#, Temp. 117°		
7/18	4870	R.T.D. (Logged hole) D & A 7/19/60
