1

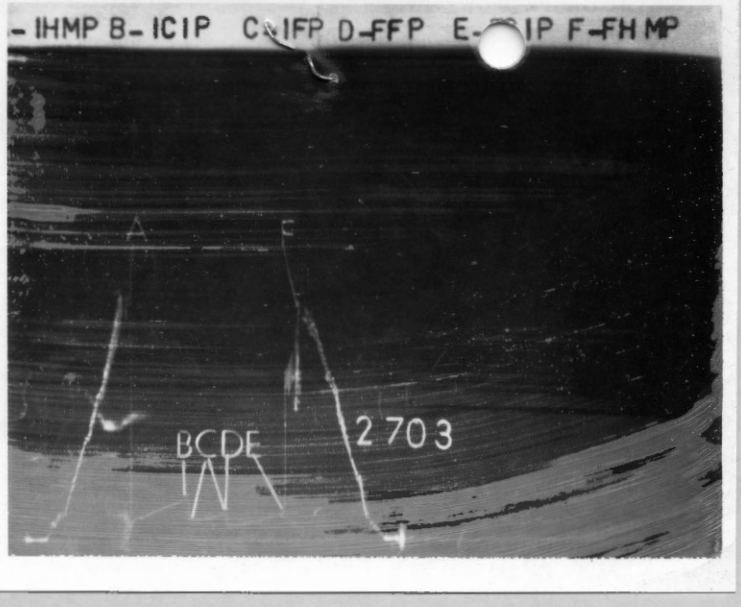

Initial Closed In Time	45 Minutes	bomin	Date 7-30-64
Tool Open Flow Period	45 Minutes		Ticket No. 2703
Final Closed In Time	45 Minutes	**BOMIN TESTING CO.** BOX 782 LIBERAL, KANSAS	DISTRICT LIBERAL, KANS.
Depth Top Gauge 5781 Ft.	Blanked Off No		Kind of Job OPEN HOLE TEST

Recorder No. 2896	12 Hr. Clock	CONTRACTOR WAKEFIELD DRILG. CO.	
Pressure Readings Field	Office Corrected	HOLE & TOOL DATA	
Initial Hydro Mud Pressure	2561	Elevation	Top Packer Depth 5751'
Initial Closed in Pres.	438	Total Depth 5865'	Bottom Packer Depth 5756'
Initial Flow Pres.	210	Casing or Hole Size 7 7/8"	Size & Type Wall Packer 6½" BT
Final Flow Pres.	175	Liner or Rathole Size --	Size Bottom Choke ½"
Final Closed in Pres.	329		Size Surface Choke 1"
Final Hydro Mud Pressure	2493	Interval Tested 5756'-5865'	ID & Length Air Chamber --
Depth Bottom Gauge 5865 Ft.	Blanked Off YES	Formation Tested MORROW	ID & Length Drill Collars 400'-2½"
Recorder No. 88	4 Hr. Clock	Est. Gauge Depth Temp. 131	Size Drill Pipe 4½ XH X 4½ FH
Pressure Readings Field	Office Corrected	MUD DATA Weight 9.1	Viscosity 52
Initial Hydro Mud Pressure		All depths measured from GL	No. Folders Reproduced 7
Initial Closed in Pres.		REMARKS: NOTE: 2 COPIES OF TEST TO	
Initial Flow Pres.		PHILLIPS OIL CO., AMARILLO, TEXAS	
Final Flow Pres.			
Final Closed in Pres.		10 MIN. PRE-FLOW WITH WEAK BLOW.	
Final Hydro Mud Pressure		WEAK BLOW THROUGHOUT TEST.	

(NOTE: IFP WITH PLUGGING ACTION)

Recovered	30	Feet of	DRILLING MUD
Recovered		Feet of	
Recovered		Feet of	
Recovered		Feet of	
Witnessed By	CLARK DAVIS		
Amount-Type of Cushion		Tester	BOB IVES

LOCATION 31-33-32W

FIELD

COUNTY SEWARD

STATE KANSAS

LIGHT

LEASE NAME

C-1

WELL NO.

1

TEST NO.

5756'-5865'

LEASE OWNER ANADARKO PRODUCTION CO.

OWNER'S DISTRICT LIBERAL, KANSAS
