DRILLING

IRRIGATION SUPPLIES

# PETERSON WELL DRILLING

331 HARRISON

PHONE 913-227-3520

## LINDSBORG, KANSAS 67456

## WATER WELL RECORD

### DRILLERS LOG OF WELL

| FROM (FT.) | TO (FT.) | KIND OF MATERIAL, COLOR, ETC. (NOTE WATER ZONES, AMOUNT, QUALITY) |
|---|---|---|
| 0 | 6 | Top Soil |
| 6 | 23 | Brown Clay |
| 23 | 30 | Gray Clay |
| 30 | 56 | Buff Clay |
| 56 | 114 | Red (Bench) Clay |
| 114 | 134 | Brown Clay |
| 134 | 136 | Lime Rock & Sand |
| 136 | 160 | Brown Clay |
| 160 | 175 | Brown Sandy Clay |
| 175 | 180 | Fine + Med Sand |
| 180 | 182 | Brown Clay |
| 182 | 192 | Coarse Sand with Clay |
| 192 | 192 | Brown Clay |
| 192 | 193 | Fine Sand |
| 193 | 195 | Green Shale |
| | | 175.00 test pumping |

Well Owner: Tom Peterson

Address: 25 Burgundy Rd

Drilling Contractor: Lake St. Louis Mo. 63367

Date Drilled: Oct. 14-21, 1977

Method of Drilling: (Cable tool, rotary, reverse rotary, etc.)

Casing Schedule: 16" Transite
(Amount, Size, Setting—New, Used—Steel, Galv.—Gage or Weight)

Screen Data (if any): 39 ft Transite
(Length, Diameter, Slot Size, Setting)
From 156 to 195

Measured depth to water on completed well (Static Level) is 107 ft. below Land Surface
(Land Surface, Top of Casing, Etc.)

Tested Yield: 750 gallons per Min.
(Min., Hour)

as determined by Test Pumping
(Bailing, Test Pumping, Etc.)

Drawdown: 160 ft. after 5 hrs.

pumping at 750 gal. per minute.

Remarks:

10-31-77
NO 7105

d

Location of Well [Show location in Section Plat]

Well site

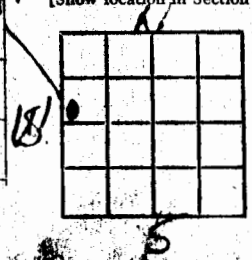


Topographic Sheet

Elev.

SW ¼ SW ¼ Sec. 32

T. 18 S., R. 3 W.

County McPherson
