1 LOCATION OF WATER WELL: County: HARVEY	Fraction: NE 1/4 NE 1/4 SE 1/4	Section Number: 08	Township Number: 24 SOUTH	Range Number: 3 WEST

Distance and direction from nearest town or city street address of well if located within city?
EB7B IS LOCATED 2640 FEET NORTH AND 30 FEET WEST OF BURMAC ROAD AND SW 60TH INTERSECTION

2 WATER WELL OWNER: **EQUUS BEDS GROUNDWATER MANAGEMENT DISTRICT**
RR#, St. Address, Box #: **313 SPRUCE STREET** Board of Agriculture, Division of Water Resources
City, State, ZIP Code **HALSTEAD, KS 67056** Application Number: **N/A**

3 LOCATE WELL'S LOCATION WITH AN "X" IN SECTION BOX:

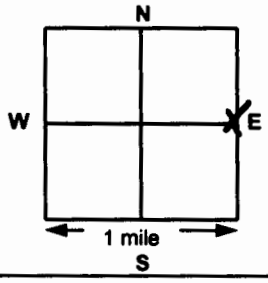

4 DEPTH OF COMPLETED WELL **75** feet ELEVATION: feet
Depth Groundwater Encountered 1 feet 2 feet 3 feet
WELL'S STATIC WATER LEVEL **10.42** feet below land surface measured on **11/28/00** mo/day/yr
Pump test data: Well water was feet after hrs pumping gpm
Estimated Yield gpm: Well water was feet after hrs pumping gpm
Bore Hole Diameter **6.0** inch to **77** feet and inch to feet

WELL WATER IS USED AS:
☐ 1 Domestic ☐ 3 Feedlot ☐ 5 Public water supply ☐ 8 Air conditioning ☐ 11 Injection
☐ 2 Irrigation ☐ 4 Industrial ☐ 6 Oil field water supply ☐ 9 Dewatering ☐ 12 Other (specify below)
☐ 7 Lawn and garden only ☒ 10 Monitoring well **EB7B**

Was a chemical/bacteriological sample submitted to Department? **NO** ; If yes, when mm/dd/yy sample was submitted Water Well Disinfected? **NO**

5 TYPE OF BLANK CASING USED:
☒ 1 Steel ☐ 3 RMP (SR) ☐ 5 Wrought iron ☐ 8 Concrete tile
☒ 2 PVC ☐ 4 ABS ☐ 6 Asbestos-Cement ☐ 9 Other (specify below)
☐ 7 Fiberglass

CASING JOINTS ☒ Glued ☐ Clamped ☐ Welded ☒ Threaded

Blank casing diameter **STEEL 2** inches to **7.0** feet, Diameter **PVC 2** inches to **65** feet, Diameter in to feet
Casing height ABOVE land surface **36** inches, weight pounds/foot Wall thickness or gauge No

TYPE OF SCREEN OR PERFORATION MATERIAL:
☐ 1 Steel ☐ 3 Stainless steel ☐ 5 Fiberglass ☒ 7 PVC ☐ 10 Asbestos-cement
☐ 2 Brass ☐ 4 Galvanized steel ☐ 6 Concrete tile ☐ 8 RMP (SR) ☐ 11 Other (specify
☐ 9 ABS ☐ 12 None used (open hole)

SCREEN OR PERFORATION OPENINGS ARE:
☐ 1 Continuous Slot ☒ 3 Mill Slot ☐ 5 Gauzed Wrapped ☐ 8 Saw Cut ☐ 11 None (open hole)
☐ 2 Louvered shutter ☐ 4 Key Punched ☐ 6 Wire Wrapped ☐ 9 Drilled holes
☐ 7 Torch cut ☐ 10 Other (specify)

SCREEN-PERFORATED INTERVALS: From **75** feet to **65** feet, From feet to feet
From feet to feet, From feet to feet
GRAVEL PACK INTERVALS: From **77** feet to **60** feet, From feet to feet
From feet to feet, From feet to feet

6 GROUT MATERIAL: 1 Neat cement ☐ 2 Neat Cement grout ☒ 3 Bentonite ☒ 4 Other ☐
Grout Intervals: From **2) 60** feet to **10** feet, From **3) 10** feet to **0** feet, From feet to feet

What is the nearest source of possible contamination:
☐ 1 Septic tank ☐ 4 Lateral lines ☐ 7 Pit privy ☐ 10 Livestock pens ☐ 14 Abandoned water well
☐ 2 Sewer lines ☐ 5 Cess pool ☐ 8 Sewage lagoon ☒ 11 Fuel storage ☐ 15 Oil well/Gas well
☐ 3 Watertight sewer line ☐ 6 Seepage pit ☐ 9 Feedyard ☐ 12 Fertilizer storage ☐ 16 Other (specify below)
☐ 13 Insecticide storage

Direction from well? **NORTHWEST** How many feet? **1900**

FROM	TO	LITHOLOGIC LOG	FROM	TO	LITHOLOGIC LOG
0.0	3	LOAM, brown			
3.0	7	CLAY, tan			
7.0	34	SAND, tan, medium			
34	36	CLAY, green			
36	45	SAND, tan, fine to coarse			
45	55	CLAY, brown, silty			
55	77	SAND, tan, fine to medium			

7 OWNER'S CERTIFICATION: This water well was constructed on **10/19/00** (mo/day/year under my jurisdiction and this record is true to the best of my knowledge and belief. This Water Well Record was completed on **2/8/01** (mo/day/year) under the business name of **Equus Beds Groundwater Management District No. 2.** Kansas Water Well License No. not applicable.

(Signature and Title)
