Pro-Stake LLC
Oil Field & Construction Site Staking
P.O. Box 2324
Garden City, Kansas 67846
Office/Fax: (620) 276-6159
Cell: (620) 272-1499
burt@pro-stakellc.kscoxmail.com

202941b
PLAT NO.

12039
INVOICE NO.

Stelbar Oil Corporation, Inc.
OPERATOR

Graham #1-30X
LEASE NAME

Stanton County, KS
COUNTY

30 Sec. **29s** Twp. **41w** Rng.

1570' FNL - 2300' FEL
LOCATION SPOT

GR. ELEVATION: **3413.1'**

SCALE: **1" =1000'**
DATE STAKED: **Aug. 6th, 2014**
MEASURED BY: **Ben R.**
DRAWN BY: **Norby S.**
AUTHORIZED BY: **Roscoe M.**

This drawing does not constitute a monumented survey or a land survey plat.
This drawing is for construction purposes only.

N
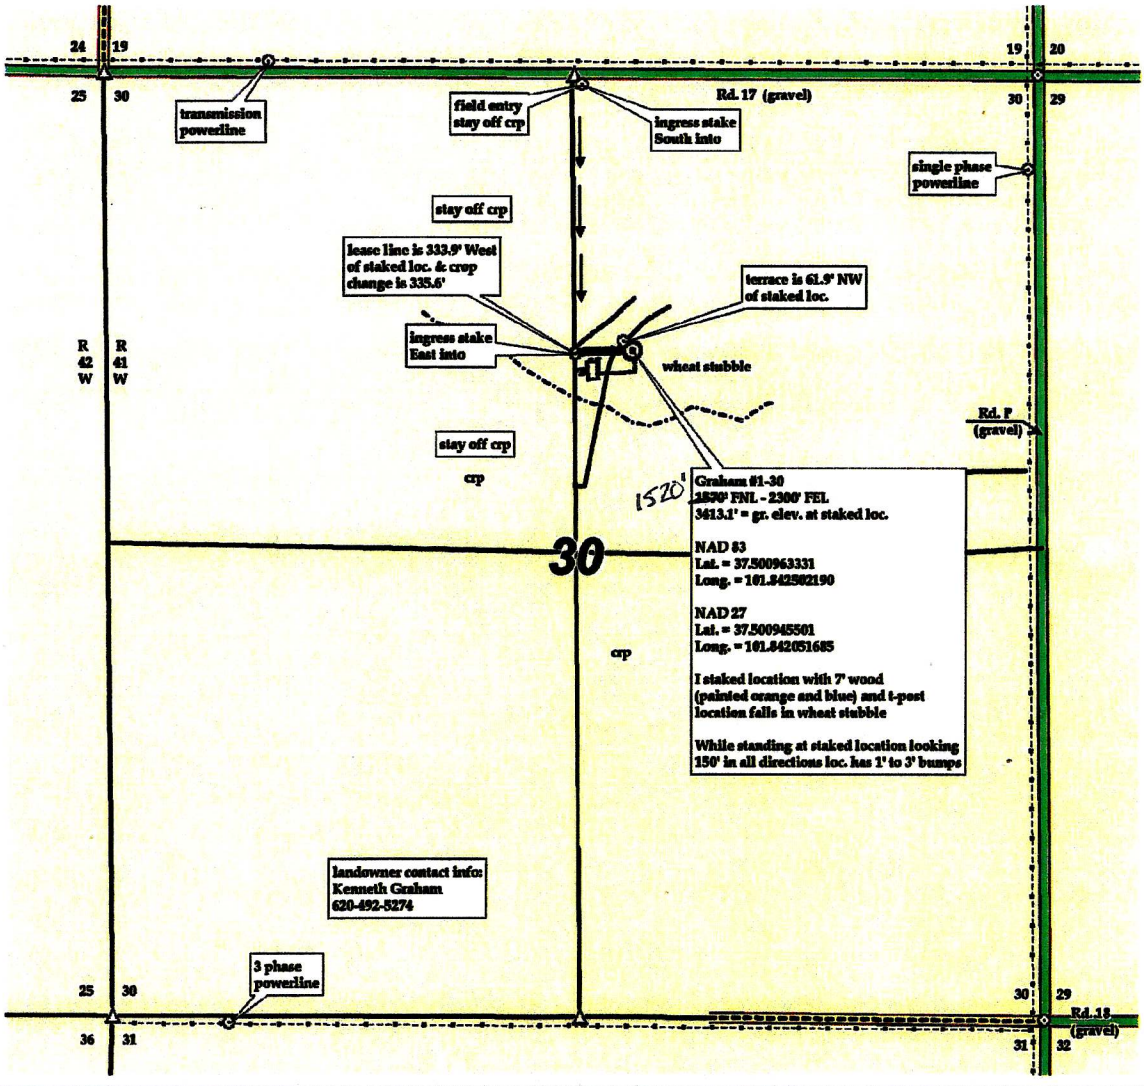
Directions: From the SW side of Manter, KS at the intersection of Hwy 160 and Manter Rd. – Now go 1.1 mile South on Manter Rd. – Now go 2 miles East on Rd. 17 to the NW corner of section 30-29s-41w – Now go 0.5 mile East on Rd. 17 to ingress stake South into – Now go 1570' South through wheat stubble to ingress stake East into – Now go 335' East through worked wheat stubble, into staked location.
