Geologic Report

Drilling Time and Sample Log

Hard Rock Consulting, Inc.

Operator	**American Warrior, Inc.**	Elevation	
Lease	**Fritz**	No. **1-29**	KB 2120'
API #	**15-135-25769-0000**		DF
Field	**Bazine**		GL 2114'
Location	**1860' FSL & 1880' FEL**	Casing Record	Surface 8 5/8" @ 1373'
Sec.	**29** Twp. **18s** Rge. **21w**	Electrical Surveys	Production 5 1/2" @ 4223'
County	**Ness** State **Kansas**		None

Formation	Log Tops	Sample Tops	Struct Comp
Anhydrite		1357' +763	+4
Base		1390' +730	+7
Heebner		3590' -1470	+1
Lansing		3636' -1516	+1
BKc		3954' -1834	FL
Pawnee		4036' -1916	+1
Fort Scott		4112' -1992	FL
Cherokee		4130' -2010	FL
Mississippian		4201' -2081	+3
Osage		4205' -2089	+1
Total Depth		4224' -2104	

Reference Well For Structural Comparison **American Warrior, Inc. LaDonna #3-29**
1800' FSL & 2296' FWL Sec. 29 T18s R21w Ness Co. Kansas

Drilling Contractor	**Petromark Drilling, LLC. Rig #1**		
Commenced	**5-27-2014**	Completed	**6-4-2014**
Samples Saved From	**3800'**	To	RTD
Drilling Time Kept From	**3500'**	To	RTD
Samples Examined From	**3800'**	To	RTD
Geological Supervision From	**3800'**	To	RTD

Displacement **3500'** Mud Type **Chemical**

Summary and Recommendations

The location for the Fritz #1-29 was found via 3-D seismic survey. The new well ran structurally as expected via the survey. Two Drill Stem Tests were conducted one of which recovered commercial amounts of oil from the Mississippian Osage Formation. After all gathered data had been examined the decision was made to run 5 1/2 inch production casing to further evaluate the Fritz #1-29 well.

Respectfully Submitted,
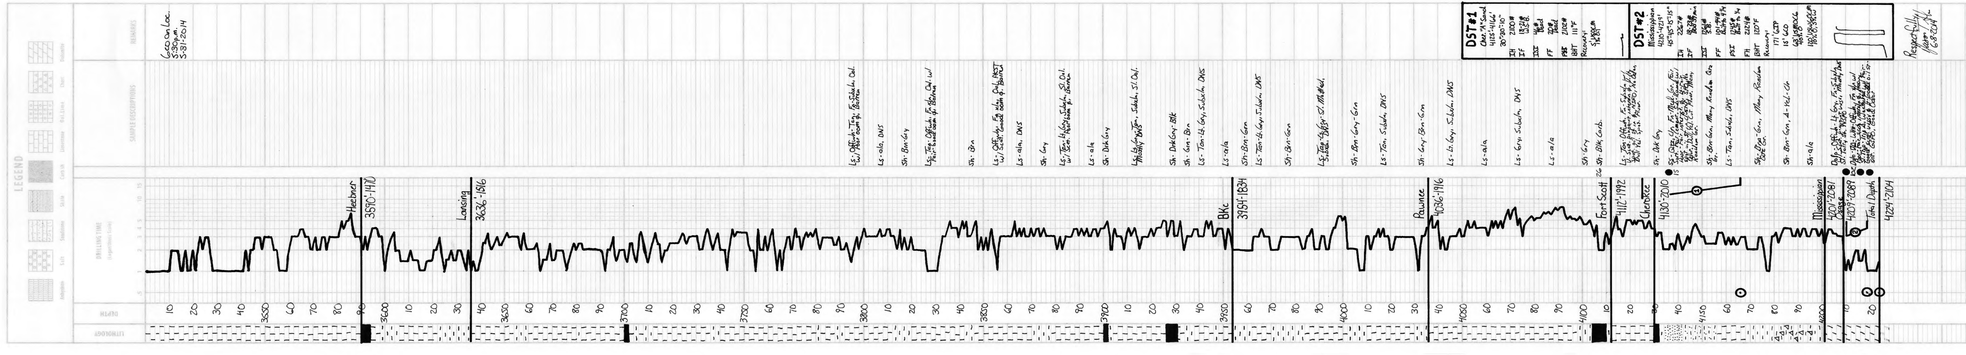
Jason T Alm
Hard Rock Consulting, Inc.
