WELLBORE SCHEMATIC

CURRENT

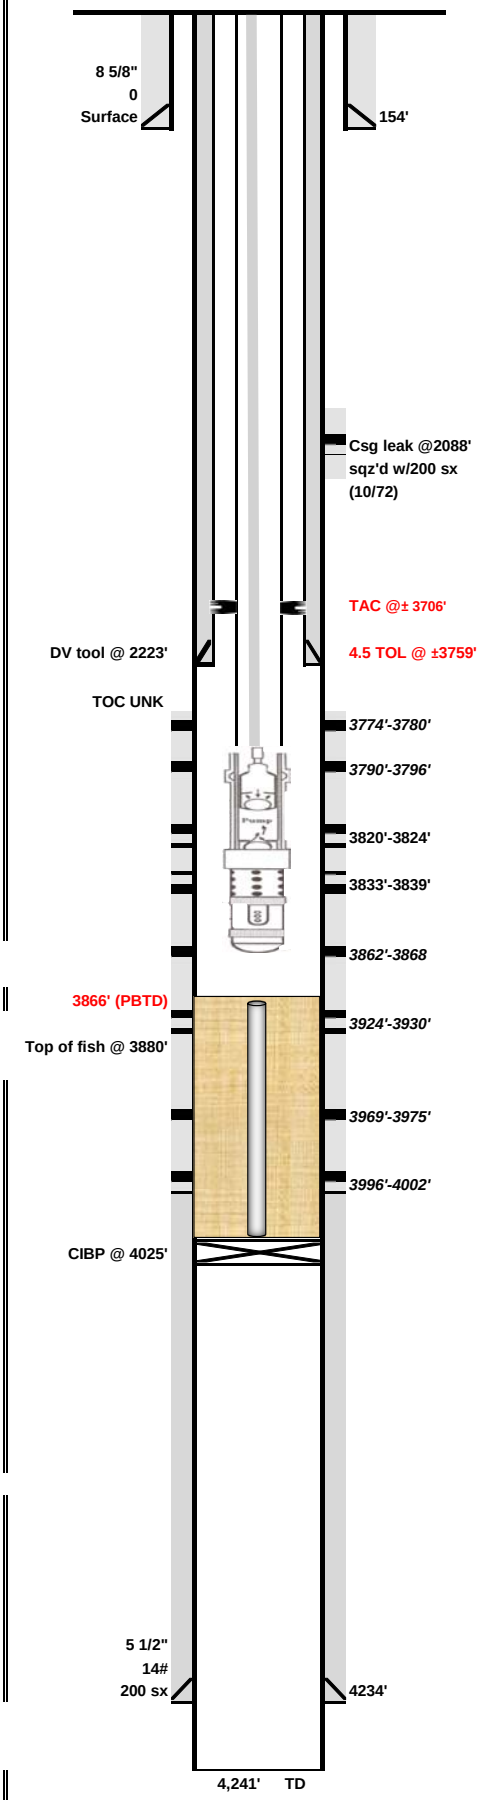

Lease:	**Elrick**			Well No.	**7**
API No.				Status	Active
Location:	NE NW SW Sec.10-10S-25W				
County:	Graham	State:	Kansas	Field:	Elrick W.F.O
TD	4241'	GL	2021'	Spud Date:	6/10/1958
PBTD	3866'	KB	2535'	Comp Date:	6/19/1958
Current Perfs/OH:	3774-3868	Current Zone:	LKC		

Surface Equipment

Unit Make:		Unit Size:	
Unit S/N:		Unit Rotation:	
SPM:	Stroke Length:	Unit Sheave:	
Prime Mover:		Motor Sheave:	
Motor S/N:		Motor RPM:	

Casing Breakdown

	Size	Grade / Wt	Depth	Hole Size	Cement
Surface	8 5/8"		154'	12-1/4"	Surface
Production	5 1/2"	14#	4234'	7-7/8"	200 sx
Production					
Production					
Liner					

Tubing Breakdown

Qty	Description	Footage
	KB	3.00'
119	2-3/8", 4.7#, EUE reconditioned	
	4-1/2" x 2-3/8" anchor	
4	2-3/8", 4.7#, EUE reconditioned	
	SN	1.00'
1	BP perf sub 2-3/8"	3.00'
	EOT at 3834'	
	TOTAL	**7.00'**

Rod Breakdown

Qty	Description	Footage
1	2-1/2" x 1 1/2" x 12' Dreiling insert pump	12.00'
1	7/8" Pony rod	2.00'
12	7/8" Weatherford KD 63	300.00'
65	3/4" Weatherford KD 63	1625.00'
75	7/8" Weatherford KD 63	1875.00'
1	22' x 1-1/4" PR w/ 1-1/2"x10' liner	22.00'
	TOTAL	**3836.00'**

Comments

12/15: Left fish in hole composed of ~5 jts of 2-7/8". TOF at 3880' Sanded hole with 33 sx sand. Perfs taking all sand. Tagged TOS at 3874'. Set CIBP at 3760'. Set 4.5" liner at 3759', cemented w/ 250 sxs Class A w/ 2% CC. Circd. DO cmt to 3866' (PBTD)

PREPARED BY:	LMCV	UPDATED:	1/23/2015
