00313
CRD NO.

# PRO-STAKE LLC

Construction Site Staking

13064
INVOICE NO.

P.O. Box 2324 Garden City, Kansas 67846
Office/Fax: (620) 276-6159 – Cell: (620) 272-1499
burt@pro-stakellc.kscoxmail.com

Herman L. Lobe, LLC
OPERATOR

Sumner County, KS
COUNTY

| 2 | 31s | 3w |
|---|---|---|
| Sec. | Twp. | Rng. |

BECKER 'B' #4
LEASE NAME

335' FSL & 1500' FEL
LOCATION SPOT

1308.5'
GR. ELEVATION

SCALE: 1" = 1000'
DATE STAKED: July 20th, 2016
MEASURED BY: Kent C.
DRAWN BY: Norby S.
AUTHORIZED BY: Jesse M.
DATE REVISED:

N

LEGEND

- irr. well
- water hydrant
- tank battery
- staked loc.
- prod. well / aband. well
- house
- building
- gas line
- water line
- transmission powerline
- 3 phase powerline
- single phase powerline
- fence
- gravel / sand rd.
- gravel trail / lease rd.
- dirt rd.
- dirt trail / lease rd.
- Hwy / blacktop rd.

**DIRECTIONS:** From the SE side of Conway Springs, Ks at the intersection of Hwy 49 & Parallel St. / Rd. 90 – Now go 1 mile East on Parallel St. / Rd. 90 to the NW corner of section 2-31s-3w - Now go 1 mile South on Sringdale Rd. – Now go 0.7 mile East on Rd. 80 and ingress North into – Now go 0.1 mile North on lease rd. to ingress East into – Now go approx. 100' through worked wheat stubble, into staked location.

**Final ingress must be verified with landowner or operator.**
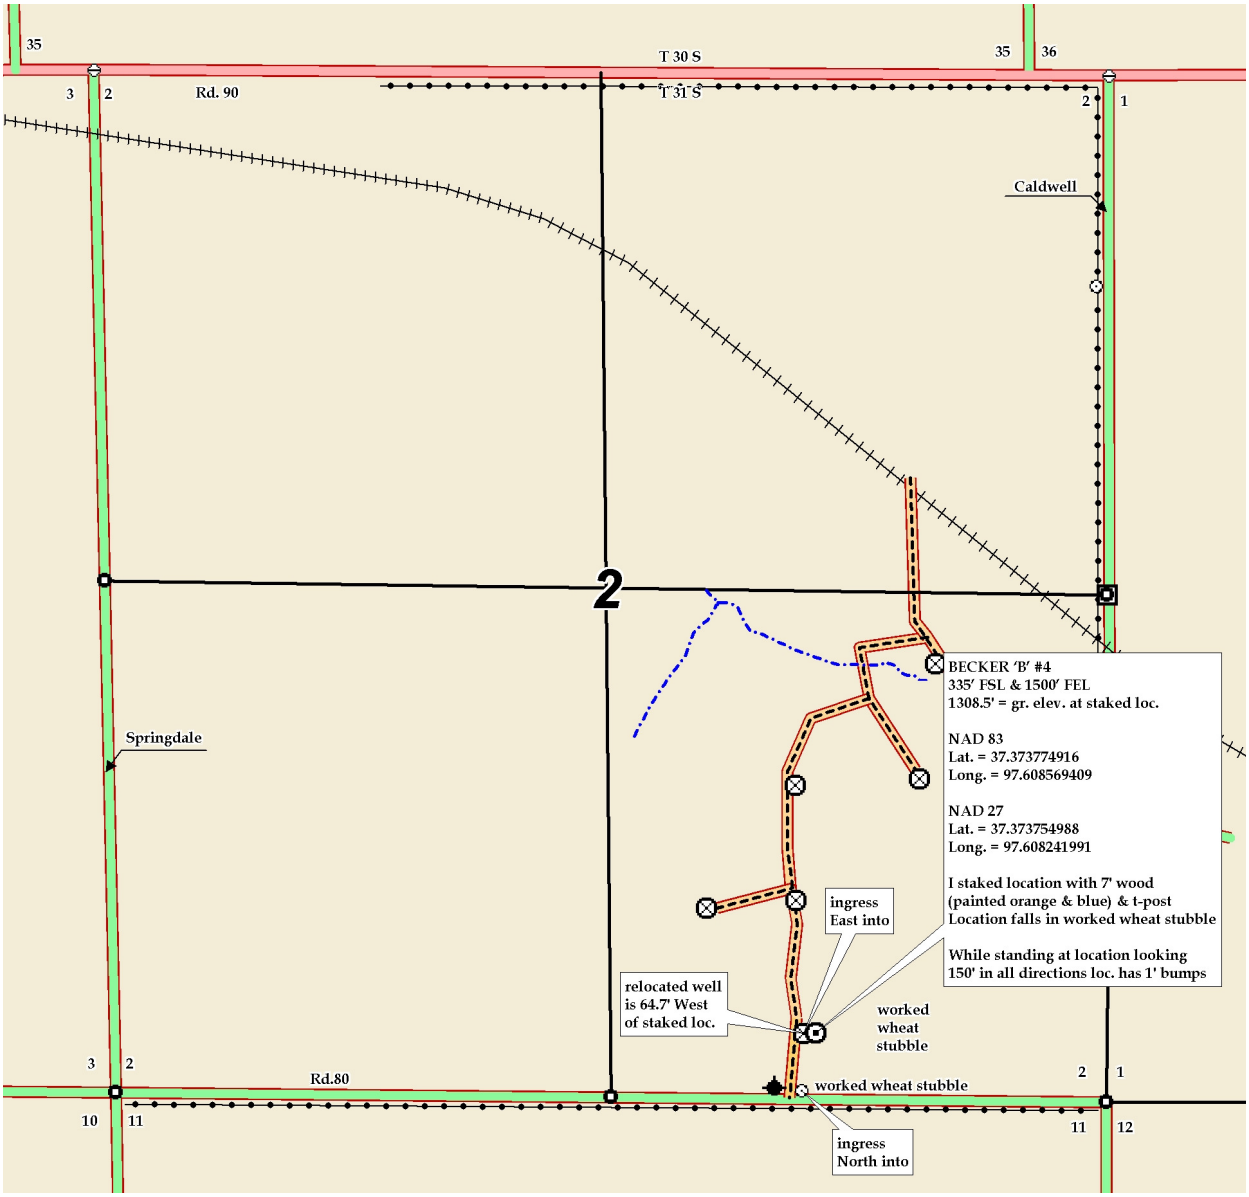
*This drawing does not constitute a monumented survey or a land survey plat.*
*This drawing is for construction purposes only.*
