Well Name:	**Dale #1**
State:	KS
County:	Scott
Field:	White & Ellis
API:	15-171-20810
Location:	1400' FSL 1175' FWL Section 33-T17S-R34W
Operator:	**NGO**

Elevations	
RKB	3147
DF	
GL	3137

Directional Data		
KOP		RKB
Max DEV	o	RKB
Max Dogleg	o	RKB
Dev @ Perfs	o	RKB
Return to Vertical		RKB

Last Update:	1/30/2017
Schematic AS OF Date:	6/10/2014
Spud	6/16/2011
TD:	6/28/2011
Completion:	6/30/2011

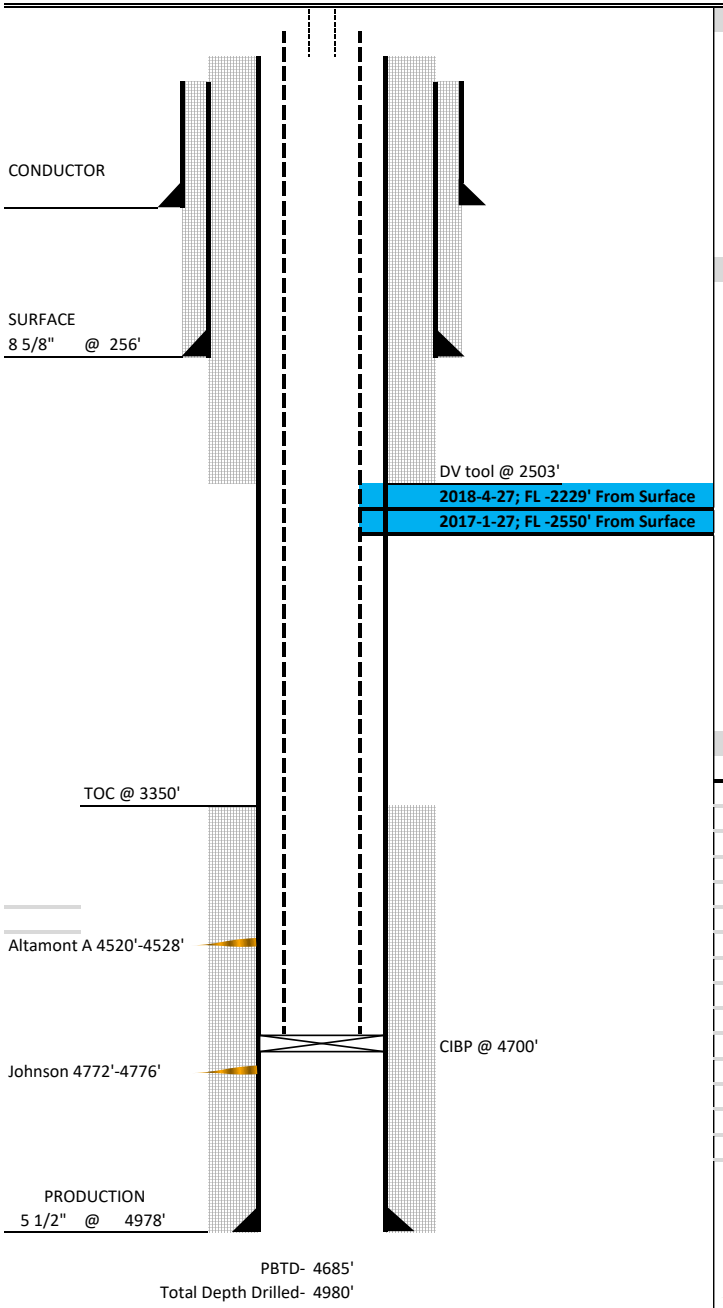

CASING / CEMENT

INTERVAL	HOLE	CSG	WT.	GR.	Depth Top	Depth Btm	LENGTH	CMT	TOC
COND.	-	-	-	-	'	'	'		
SURF.	12.25"	8 5/8"	24#	J-55	'	256'		180 sx	
Production	7.625"	5 1/2"	15.5#		'	4978'		400 sx	
DV Tool									
Tbg									
SN									
Rods									

Perf Data

Stage #	Formation	Top Perf	Btm Perf	Length	Net ft	SPF	Total Holes
1	Johnson	4,772'	4,776'	4'	4'	6	24
2	Altamont A	4,520'	4,528'	8'	8'	6	48
				'			-

NOTES: 12/29/2016
Dale will be TA in Janauray 2017, pumping unit went to the Sowers 1-5, tubing and rods went to the Riedel 2-5, the tanks are still onsite.

Stimulation Data

Stage #	Water	Proppant	Acid	Avg R	Max R	Avg P	ISIP	FG
