State Kansas County Rice

Company Continental Oil Company Well No. 11

Farm B. B. Ainsworth

Survey

Block No. Sec. 24 Twp. 18S Range 8W

Co-Ord. Elev. 1729 KB
1726 DF

SE NW SE

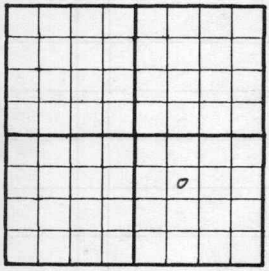

Rig #3

100% Continental Oil Co.

AM 7-7291

NOTE: Show Sketch of Lease and Well Location in Above Space

Ft. from N. Line 1650 Ft. from S. Line

Ft. from W. Line 1650 Ft. from E. Line

| Date | Depth | |
|---|---|---|
| | | MIRT 10-7-54 & SPD |
| 10-8 | | 8 5/8" @ 309' w/175 sx cem. |
| | 3 c.c. | P.D. 2:45 a.m. 10-8-54 |
| 10-9 | 700 | Drlg |
| 10-11 | 2250 | Drlg |
| 10-12 | 2646 | Drlg |
| 10-13 | 2978 | Drlg |
| 10-14 | 3143 | Arbuckle (-1414) |
| | 3147 | R.T.D. Waiting on Log |
| 10-15 | | 5 1/2" @ 2' off bottom (3145') |

T 13-13-S

| Date | Depth | 716525 |
|---|---|---|
| | | w/200 sx cem. |
| | 3147 | R.T.D. 3141 Sj T.D. Will |
| | | strap drill pipe to check |
| | | R.T.D. |
| | | (Strapped pipe @ 3145') |
| 10-16 | | MICT |
| 10-18 | | Completed cable tool work. |
| | | Moved out 10-18-54. |
